Appendix 4 – WCDOT ADA Prioritization Schedule and Condition Ratings

Date of Inventory: 2022

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violation	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH54	S Briggs St & E Washington St	WCDOT	1	17	3	Repair Tiles	$500.00	2029	WCDOT GM
CH54	S Briggs St & E Washington St	WCDOT	4		3	MEP. Repair Tiles	$500.00	2029	WCDOT GM
CH54	S Briggs St & E Washington St	WCDOT			3		$ -		
CH54	S Briggs St & E Washington St	WCDOT			3		$ -		
CH54	S Briggs St & E Washington St	WCDOT	5		3	MEP. No Remediation Necessary.	$ -	2029	WCDOT GM
CH54	S Briggs St & E Washington St	WCDOT	7		3	MEP. Repair Tiles	$500.00	2029	WCDOT GM
CH54	S Briggs St & E Washington St	WCDOT			3		$ -		
CH54	S Briggs St & E Washington St	WCDOT			3		$ -		
CH54	S Briggs St & 3rd Ave	WCDOT			1		$ -		
CH54	S Briggs St & 3rd Ave	WCDOT			1		$ -		
CH54	S Briggs St & 2nd Ave	WCDOT		1	3		$ -		
CH54	S Briggs St & 2nd Ave	WCDOT	1		3		$ -		
CH54	N Briggs St & E Cass St	IDOT	15	49	3	Repair Curb Ramp	$3,500.00	2029	WCDOT GM
CH54	N Briggs St & E Cass St	IDOT	11		3	Repair Curb Ramp	$3,500.00	2029	WCDOT GM
CH54	N Briggs St & E Cass St	IDOT	9		3	Repair Curb Ramp & Ped Button Improvement	$3,500.00	2029	WCDOT GM
CH54	N Briggs St & E Cass St	IDOT	14		3	Repair Curb Ramp	$3,500.00	2029	WCDOT GM
CH62	N Briggs St & Driveway	WCDOT	2	2	3	Repair Curb Ramp	$3,500.00	2029	WCDOT GM
CH62	N Briggs St & Driveway	WCDOT			3		$ -		
CH62	N Briggs St & Sterling Ave	WCDOT	6	11	3	Repair Curb Ramp	$3,500.00	2029	WCDOT GM
CH62	N Briggs St & Sterling Ave	WCDOT	5		3	Repair Curb Ramp	$3,500.00	2029	WCDOT GM
CH62	N Briggs St & Elgin Ave	WCDOT	5	5	3	Repair Curb Ramp	$3,500.00	2029	WCDOT GM
CH62	N Briggs St & Elgin Ave	WCDOT			3		$ -		
CH62	N Briggs St & Copperfield Ave	WCDOT	6	49	3	Repair Curb Ramp & Ped Button Improvement	$1,750.00	2029	WCDOT GM
CH62	N Briggs St & Copperfield Ave	WCDOT	6		3	Repair Curb Ramp	$1,750.00	2029	WCDOT GM
CH62	N Briggs St & Copperfield Ave	WCDOT	6		3	Repair Curb Ramp	$1,750.00	2029	WCDOT GM

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violation	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH62	N Briggs St & Copperfield Ave	WCDOT	5		3	Repair Curb Ramp	$1,750.00	2029	WCDOT GM
CH62	N Briggs St & Copperfield Ave	WCDOT	4		3	Repair Curb Ramp	$2,500.00	2029	WCDOT GM
CH62	N Briggs St & Copperfield Ave	WCDOT	7		3	Repair Curb Ramp	$2,500.00	2029	WCDOT GM
CH62	N Briggs St & Copperfield Ave	WCDOT	8		3	Repair Curb Ramp & Ped Button Improvement	$2,500.00	2029	WCDOT GM
CH62	N Briggs St & Copperfield Ave	WCDOT	7		3	Repair Curb Ramp & Ped Button Improvement	$2,500.00	2029	WCDOT GM
CH62	N Briggs St & Belmont Ave	WCDOT	8	26	3	Repair Curb Ramp	$2,000.00	2029	WCDOT GM
CH62	N Briggs St & Belmont Ave	WCDOT	6		3	Repair Curb Ramp	$2,000.00	2029	WCDOT GM
CH62	N Briggs St & Belmont Ave	WCDOT	8		3	Repair Curb Ramp	$2,000.00	2029	WCDOT GM
CH62	N Briggs St & Belmont Ave	WCDOT	4		3	Repair Curb Ramp	$2,000.00	2029	WCDOT GM
CH62	N Briggs St & Driveway	WCDOT	5	10	3	Repair Curb Ramp	$2,000.00	2029	WCDOT GM
CH62	N Briggs St & Driveway	WCDOT	5		3	Repair Curb Ramp	$2,000.00	2029	WCDOT GM
CH62	N Briggs St & Maple Rd	WCDOT	2		3	Ped Button Improvement	$3,500.00	2029	WCDOT GM
CH62	N Briggs St & Maple Rd	WCDOT	1		3	Ped Button Improvement	$3,500.00	2029	WCDOT GM
CH62	N Briggs St & Maple Rd	WCDOT	3		3	Repair Curb Ramp	$3,500.00	2029	WCDOT GM
CH62	N Briggs St & Maple Rd	WCDOT			3	Ped Button Improvement	$ -	2029	WCDOT GM
CH62	N Briggs St & Maple Rd	WCDOT	7		3	Repair Curb Ramp & Ped Button Improvement	$3,500.00	2029	WCDOT GM
CH62	N Briggs St & Maple Rd	WCDOT	5		3	Repair Curb Ramp & Ped Button Improvement	$3,500.00	2029	WCDOT GM
CH62	N Briggs St & Maple Rd	WCDOT	7		3	Repair Curb Ramp	$3,500.00	2029	WCDOT GM
CH62	N Briggs St & Maple Rd	WCDOT	8		3	Repair Curb Ramp	$3,500.00	2029	WCDOT GM
CH62	N Briggs St & Driveway	WCDOT	5	11	3	Repair Curb Ramp	$2,000.00	2029	WCDOT GM
CH62	N Briggs St & Driveway	WCDOT	6		3	Repair Curb Ramp	$2,000.00	2029	WCDOT GM
CH62	N Briggs St & Elgin Ave	WCDOT	5	10	3	Repair Curb Ramp	$2,000.00	2029	WCDOT GM
CH62	N Briggs St & Elgin Ave	WCDOT	5		3	Repair Curb Ramp	$2,000.00	2029	WCDOT GM
CH62	N Briggs St & Sterling Ave	WCDOT	5	5	3	Repair Curb Ramp	$2,000.00	2029	WCDOT GM
CH62	N Briggs St & Sterling Ave	WCDOT			3		$ -	2032	WCDOT GM

* Project timelines are estimates only and may change due to change in project schedules.

** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH24	W Indiana Ave & Elliott St	Beecher	6	16	1			2023	WCDOT GM
CH24	W Indiana Ave & Elliott St	Beecher	10		1			2023	WCDOT GM
CH24	W Indiana Ave & Gould St	Beecher	11	19	1			2023	WCDOT GM
CH24	W Indiana Ave & Gould St	Beecher	8		1			2023	WCDOT GM
CH24	W Indiana Ave & Driveway	Beecher	3	13	1			2023	WCDOT GM
CH24	W Indiana Ave & Driveway	Beecher	10		1			2023	WCDOT GM
CH24	W Indiana Ave & S Woodward St	Beecher	3	47	1			2023	WCDOT GM
CH24	W Indiana Ave & S Woodward St	Beecher	6		1			2023	WCDOT GM
CH24	W Indiana Ave & S Woodward St	Beecher	7		1			2023	WCDOT GM
CH24	W Indiana Ave & S Woodward St	Beecher	6		1			2023	WCDOT GM
CH24	W Indiana Ave & S Woodward St	Beecher	10		1			2023	WCDOT GM
CH24	W Indiana Ave & S Woodward St	Beecher	9		1			2023	WCDOT GM
CH24	W Indiana Ave & S Woodward St	Beecher	6		1			2023	WCDOT GM
CH24	W Indiana Ave & Driveway	Beecher	4	5	1			2023	WCDOT GM
CH24	W Indiana Ave & Driveway	Beecher	1		1			2023	WCDOT GM
CH24	W Indiana Ave & Maxwell St	Beecher	2	16	1			2023	WCDOT GM
CH24	W Indiana Ave & Maxwell St	Beecher	7		1			2023	WCDOT GM
CH24	W Indiana Ave & Maxwell St	Beecher	3		1			2023	WCDOT GM
CH24	W Indiana Ave & Maxwell St	Beecher	4		1			2023	WCDOT GM
CH24	W Indiana Ave & Catalpa St	Beecher	7	15	1			2023	WCDOT GM
CH24	W Indiana Ave & Catalpa St	Beecher	8		1			2023	WCDOT GM
CH24	W Indiana Ave & Prairie Ave	Beecher	8	25	1			2023	WCDOT GM
CH24	W Indiana Ave & Prairie Ave	Beecher	8		1			2023	WCDOT GM
CH24	W Indiana Ave & Prairie Ave	Beecher	9		1			2023	WCDOT GM

* Project timelines are estimates only and may change due to change in project schedules.

** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH88	S Weber Rd & Lily Cache Ln	Bolingbrook	4	35	2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Lily Cache Ln	Bolingbrook	8		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Lily Cache Ln	Bolingbrook	2		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Lily Cache Ln	Bolingbrook	4		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Lily Cache Ln	Bolingbrook	5		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Lily Cache Ln	Bolingbrook	5		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Lily Cache Ln	Bolingbrook	6		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Lily Cache Ln	Bolingbrook	1		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	8	20	2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	5		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	5		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	2		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	2	11	2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	2		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	1		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	6		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Chanticleer Ave	Bolingbrook	5	35	1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Chanticleer Ave	Bolingbrook	4		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Chanticleer Ave	Bolingbrook	6		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Chanticleer Ave	Bolingbrook	6		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Chanticleer Ave	Bolingbrook	4		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Chanticleer Ave	Bolingbrook	6		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Chanticleer Ave	Bolingbrook	4		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Wingfield Way	Bolingbrook	6	8	1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Wingfield Way	Bolingbrook	2		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	3	14	2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	4		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	3		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	4		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & W 111th St	Bolingbrook	4	15	1		$ -	2027	WCDOT GM

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH88	S Weber Rd & W 111th St	Bolingbrook	1		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & W 111th St	Bolingbrook	4		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & W 111th St	Bolingbrook	6		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	1	2	2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	1		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Parkside Dr	Bolingbrook	3	27	1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Parkside Dr	Bolingbrook	2		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Parkside Dr	Bolingbrook	6		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Parkside Dr	Bolingbrook	3		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Parkside Dr	Bolingbrook	6		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Parkside Dr	Bolingbrook	7		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & 115th St	Bolingbrook	8	48	1		$ -	2027	WCDOT GM
CH88	S Weber Rd & 115th St	Bolingbrook	6		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & 115th St	Bolingbrook	6		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & 115th St	Bolingbrook	6		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & 115th St	Bolingbrook	5		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & 115th St	Bolingbrook	6		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & 115th St	Bolingbrook	6		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & 115th St	Bolingbrook	5		1		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	4	9	2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	5		2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook	5	5	2		$ -	2027	WCDOT GM
CH88	S Weber Rd & Driveway	Bolingbrook			2		$ -	2027	WCDOT GM
CH88	N Weber Rd & Driveway	Bolingbrook			1		$ -		
CH88	N Weber Rd & Driveway	Bolingbrook			1		$ -		
CH14	Plainfield-Naperville Rd & Driveway	Bolingbrook	5	7	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Driveway	Bolingbrook	2		1		$ -	2023	WCDOT GM

* Project timelines are estimates only and may change due to change in project schedules.

** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH32	S Tryon St & Driveway	Channahon	6	10	1		$ -	2025	Local
CH32	S Tryon St & Driveway	Channahon	4		1		$ -	2025	Local
CH32	S Tryon St & Reed St	Channahon	8	12	1		$ -	2025	Local
CH32	S Tryon St & Reed St	Channahon	4		1		$ -	2025	Local
CH32	S Ford Rd & S River Trl	Channahon	7	12	1		$ -	2025	Local
CH32	S Ford Rd & S River Trl	Channahon	5		1		$ -	2025	Local
CH32	S Ford Rd & Crowfoot Ln	Channahon	5	10	1		$ -	2025	Local
CH32	S Ford Rd & Crowfoot Ln	Channahon	5		1		$ -	2025	Local
CH32	S Ford Rd & Mohawk Ln	Channahon	5	10	1		$ -	2025	Local
CH32	S Ford Rd & Mohawk Ln	Channahon	5		1		$ -	2025	Local
CH32	S Ford Rd & Driveway	Channahon	3	6	1		$ -	2025	Local
CH32	S Ford Rd & Driveway	Channahon	3		1		$ -	2025	Local
CH32	S Ford Rd & Driveway	Channahon	3	5	1		$ -	2025	Local
CH32	S Ford Rd & Driveway	Channahon	2		1		$ -	2025	Local
CH32	S Ford Rd & Chipwood Dr	Channahon	5	24	1		$ -	2025	Local
CH32	S Ford Rd & Chipwood Dr	Channahon	9		1		$ -	2025	Local
CH32	S Ford Rd & Chipwood Dr	Channahon	5		1		$ -	2025	Local
CH32	S Ford Rd & Chipwood Dr	Channahon	5		1		$ -	2025	Local
CH32	S Ford Rd & W McGowan Woods Rd	Channahon	3	3	1		$ -	2025	Local
CH32	S Ford Rd & Lakeview Dr	Channahon	4	4	1		$ -	2025	Local
CH77	W Bluff Rd & S Valley Dr	Channahon	9	14	1		$ -	2025	Local
CH77	W Bluff Rd & S Valley Dr	Channahon	5		1		$ -	2025	Local
CH77	W Bluff Rd & S Edwin Dr	Channahon	4	5	1		$ -	2025	Local
CH77	W Bluff Rd & S Edwin Dr	Channahon	1		1		$ -	2025	Local

* Project timelines are estimates only and may change due to change in project schedules.
** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH5	Caton Farm Rd & Caton Crest Dr	Crest Hill			1		$ -		
CH5	Caton Farm Rd & Caton Crest Dr	Crest Hill			1		$ -		
CH36	W Renwick Rd & Borio Dr	Crest Hill			1		$ -		
CH36	W Renwick Rd & Borio Dr	Crest Hill		2	1		$ -		
CH36	W Renwick Rd & Borio Dr	Crest Hill	2		1		$ -	2031	WCDOT GM
CH36	W Renwick Rd & Borio Dr	Crest Hill			1		$ -		
CH88	Weber Rd & W McGilvary Dr	Crest Hill	7	12	1		$ -	2029	WCDOT GM
CH88	Weber Rd & W McGilvary Dr	Crest Hill	5		1		$ -	2029	WCDOT GM
CH88	Weber Rd & Root St	Crest Hill	10	60	2		$ -	2025	Local
CH88	Weber Rd & Root St	Crest Hill	8		2		$ -	2025	Local
CH88	Weber Rd & Root St	Crest Hill	13		1		$ -	2025	Local
CH88	Weber Rd & Root St	Crest Hill	5		1		$ -	2025	Local
CH88	Weber Rd & Root St	Crest Hill	7		1		$ -	2025	Local
CH88	Weber Rd & Root St	Crest Hill	11		1		$ -	2025	Local
CH88	Weber Rd & Root St	Crest Hill	6		1		$ -	2025	Local

* Project timelines are estimates only and may change due to change in project schedules.

** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH49	W Exchange St & Driveway	Crete	8	12	1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	4		1		$ -	2028	Local
CH49	W Exchange St & S Independence Blvd	Crete	4	27	1		$ -	2028	Local
CH49	W Exchange St & S Independence Blvd	Crete	4		1		$ -	2028	Local
CH49	W Exchange St & S Independence Blvd	Crete	1		1		$ -	2028	Local
CH49	W Exchange St & S Independence Blvd	Crete	3		1		$ -	2028	Local
CH49	W Exchange St & S Independence Blvd	Crete	6		1		$ -	2028	Local
CH49	W Exchange St & S Independence Blvd	Crete	3		1		$ -	2028	Local
CH49	W Exchange St & S Independence Blvd	Crete	3		1		$ -	2028	Local
CH49	W Exchange St & S Independence Blvd	Crete	3		1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	7	10	1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	3		1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	2	7	1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	5		1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	1	2	1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	1		1		$ -	2028	Local
CH49	W Exchange St & S Sangamon St	Crete	5	9	1		$ -	2028	Local
CH49	W Exchange St & S Sangamon St	Crete	4		1		$ -	2028	Local
CH49	W Exchange St & Peoria St	Crete	9	12	1		$ -	2028	Local
CH49	W Exchange St & Peoria St	Crete	3		1		$ -	2028	Local
CH49	W Exchange St & Washington St	Crete	10	26	1		$ -	2028	Local
CH49	W Exchange St & Washington St	Crete	5		1		$ -	2028	Local
CH49	W Exchange St &	Crete	8		1		$ -	2028	Local

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
	Washington St								
CH49	W Exchange St & Washington St	Crete	3		1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	5	10	1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	5		1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	6	9	1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	3		1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	5	13	1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	8		1		$ -	2028	Local
CH49	W Exchange St & Lincoln Ave	Crete	10	21	1		$ -	2028	Local
CH49	W Exchange St & Lincoln Ave	Crete	11		1		$ -	2028	Local
CH49	W Exchange St & Columbia St	Crete	5	12	1		$ -	2028	Local
CH49	W Exchange St & Columbia St	Crete	7		1		$ -	2028	Local
CH49	W Exchange St & Vincennes St	Crete	3	8	1		$ -	2028	Local
CH49	W Exchange St & Vincennes St	Crete	5		1		$ -	2028	Local
CH49	W Exchange St & Lumber St	Crete	7	12	1		$ -	2028	Local
CH49	W Exchange St & Lumber St	Crete	5		1		$ -	2028	Local
CH49	W Exchange St & Union Pacific Railroad	Crete	1	5	1		$ -	2028	Local
CH49	W Exchange St & Union Pacific Railroad	Crete			1		$ -	2028	Local
CH49	W Exchange St & Union Pacific Railroad	Crete	4		1		$ -	2028	Local
CH49	W Exchange St & Benton St	Crete	9	47	1		$ -	2028	Local
CH49	W Exchange St & Benton St	Crete	6		1		$ -	2028	Local
CH49	W Exchange St & Benton St	Crete	7		1		$ -	2028	Local
CH49	W Exchange St & Benton St	Crete	2		1		$ -	2028	Local
CH49	W Exchange St & Benton St	Crete	10		1		$ -	2028	Local
CH49	W Exchange St & Benton St	Crete	13		1		$ -	2028	Local

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH49	W Exchange St & Wood	Crete	7	28	1		$ -	2028	Local
CH49	W Exchange St & Wood	Crete	9		1		$ -	2028	Local
CH49	W Exchange St & Wood	Crete	7		1		$ -	2028	Local
CH49	W Exchange St & Wood	Crete	5		1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	2	28	1		$ -	2028	Local
CH49	W Exchange St & Driveway	Crete	2		1		$ -	2028	Local
CH49	W Exchange St & Elizabeth St	Crete	6		1		$ -	2028	Local
CH49	W Exchange St & Elizabeth St	Crete	8		1		$ -	2028	Local
CH49	W Exchange St & Elizabeth St	Crete	3		1		$ -	2028	Local
CH49	W Exchange St & Elizabeth St	Crete	5		1		$ -	2028	Local
CH49	W Exchange St & Elizabeth St	Crete	1		1		$ -	2028	Local
CH49	W Exchange St & Elizabeth St	Crete	1		1		$ -	2028	Local
CH49	W Exchange St & Elizabeth St	Crete	1	5	1		$ -	2028	Local
CH49	W Exchange St & Elizabeth St	Crete	4		1		$ -	2028	Local
CH49	W Exchange St & Park St	Crete	6	7	1		$ -	2028	Local
CH49	W Exchange St & Park St	Crete	1		1		$ -	2028	Local
CH49	W Exchange St & Selleck St	Crete	5	11	1		$ -	2028	Local
CH49	W Exchange St & Selleck St	Crete	6		1		$ -	2028	Local
CH49	W Exchange St & Perry St	Crete	4	17	1		$ -	2028	Local
CH49	W Exchange St & Perry St	Crete	2		1		$ -	2028	Local
CH49	W Exchange St & East St	Crete	3		1		$ -	2028	Local
CH49	W Exchange St & East St	Crete	3		1		$ -	2028	Local
CH49	W Exchange St & East St	Crete	5		1		$ -	2028	Local
CH49	W Exchange St & East St	Crete	5	10	1		$ -	2028	Local
CH49	W Exchange St & East St	Crete	5		1		$ -	2028	Local
CH49	W Exchange St & Dairy Ln	Crete	2	2	1		$ -	2028	Local
CH49	W Exchange St & Dairy Ln	Crete	3	3	1		$ -	2028	Local

* Project timelines are estimates only and may change due to change in project schedules.

** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH7	S Old Chicago Rd & Bike Path	Forest Preserve District of Will County	2	4	1		$ -	2027	WCDOT GM
CH7	S Old Chicago Rd & Bike Path	Forest Preserve District of Will County	2		1		$ -	2027	WCDOT GM
CH17	Western Ave & Bike Path	Forest Preserve District of Will County	5	6	2		$ -	2029	WCDOT GM
CH17	Western Ave & Bike Path	Forest Preserve District of Will County	1		2		$ -	2029	WCDOT GM
CH25	W Peotone Rd & Bike Path	Forest Preserve District of Will County	2	5	1		$ -	2027	WCDOT GM
CH25	W Peotone Rd & Bike Path	Forest Preserve District of Will County	3		1		$ -	2027	WCDOT GM
CH51	Mills Rd & Bike Path	Forest Preserve District of Will County	1	5	2		$ -	2028	5 Year Plan
CH51	Mills Rd & Bike Path	Forest Preserve District of Will County	4		2		$ -	2028	5 Year Plan
CH55	Cherry Hill Rd & Bike Path	Forest Preserve District of Will County	4	7	2		$ -	2028	5 Year Plan
CH55	Cherry Hill Rd & Bike Path	Forest Preserve District of Will County	3		1		$ -	2028	5 Year Plan
CH73	S Symerton Rd & Bike Path	Forest Preserve District of Will County	1	2	2		$ -	2028	WCDOT GM
CH73	S Symerton Rd & Bike Path	Forest Preserve District of Will County	1		2		$ -	2028	WCDOT GM
CH90	W Hoff Rd & Bike Path	Forest Preserve District of Will County	2	4	1		$ -	2032	WCDOT GM
CH90	W Hoff Rd & Bike Path	Forest Preserve District of Will County	2		1		$ -	2032	WCDOT GM

* Project timelines are estimates only and may change due to change in project schedules.

** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH74	W Laraway Rd & Ledgestone Way	Frankfort	5	14	1		$ -	2028	5 Year Plan
CH74	W Laraway Rd & Ledgestone Way	Frankfort	9		1		$ -	2028	5 Year Plan
CH74	W Laraway Rd & 116th Ave	Frankfort	3	29	3		$ -	2028	5 Year Plan
CH74	W Laraway Rd & 116th Ave	Frankfort	1		3		$ -	2028	5 Year Plan
CH74	W Laraway Rd & 116th Ave	Frankfort	3		3		$ -	2028	5 Year Plan
CH74	W Laraway Rd & 116th Ave	Frankfort	5		3		$ -	2028	5 Year Plan
CH74	W Laraway Rd & 116th Ave	Frankfort	4		3		$ -	2028	5 Year Plan
CH74	W Laraway Rd & 116th Ave	Frankfort	6		3		$ -	2028	5 Year Plan
CH74	W Laraway Rd & 116th Ave	Frankfort	5		3		$ -	2028	5 Year Plan
CH74	W Laraway Rd & 116th Ave	Frankfort	2		3		$ -	2028	5 Year Plan
CH74	W Laraway Rd & Driveway	Frankfort	10	17	1		$ -	2028	5 Year Plan
CH74	W Laraway Rd & Driveway	Frankfort	7		1		$ -	2028	5 Year Plan
CH74	W Laraway Rd & Wolf Rd	Frankfort	3	16	1		$ -	2028	5 Year Plan
CH74	W Laraway Rd & Wolf Rd	Frankfort	3		1		$ -	2028	5 Year Plan
CH74	W Laraway Rd & Wolf Rd	Frankfort			1		$ -	2028	5 Year Plan
CH74	W Laraway Rd & Wolf Rd	Frankfort			1		$ -	2028	5 Year Plan
CH74	W Laraway Rd & Wolf Rd	Frankfort			1		$ -	2028	5 Year Plan
CH74	W Laraway Rd & Wolf Rd	Frankfort	1		1		$ -	2028	5 Year Plan
CH74	W Laraway Rd & Wolf Rd	Frankfort	5		1		$ -	2028	5 Year Plan
CH74	W Laraway Rd & Wolf Rd	Frankfort	4		1		$ -	2028	5 Year Plan
CH74	W Laraway Rd & Heritage Dr	Frankfort	2	3	1		$ -	2026	5 Year Plan
CH74	W Laraway Rd & Heritage Dr	Frankfort	1		1		$ -	2026	5 Year Plan
CH74	W Laraway Rd & Regency Dr	Frankfort	8	15	1		$ -	2026	5 Year Plan
CH74	W Laraway Rd & Regency Dr	Frankfort	7		1		$ -	2026	5 Year Plan
CH74	W Laraway Rd & Driveway	Frankfort	2	5	1		$ -	2026	5 Year Plan

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH74	W Laraway Rd & Driveway	Frankfort	3		1		$ -	2026	5 Year Plan
CH74	W Laraway Rd & Driveway	Frankfort	7	16	1		$ -	2030	WCDOT GM
CH74	W Laraway Rd & Driveway	Frankfort	9		1		$ -	2030	WCDOT GM
CH74	W Laraway Rd & Majestic Ln	Frankfort	2	8	1		$ -	2030	WCDOT GM
CH74	W Laraway Rd & Majestic Ln	Frankfort	1		1		$ -	2030	WCDOT GM
CH74	W Laraway Rd & Majestic Ln	Frankfort	1		1		$ -	2030	WCDOT GM
CH74	W Laraway Rd & Majestic Ln	Frankfort	4		1		$ -	2030	WCDOT GM
CH74	W Laraway Rd & S 80th Ave	Frankfort	5	15	3		$ -	2030	WCDOT GM
CH74	W Laraway Rd & S 80th Ave	Frankfort	3		3		$ -	2030	WCDOT GM
CH74	W Laraway Rd & S 80th Ave	Frankfort	5		3		$ -	2030	WCDOT GM
CH74	W Laraway Rd & S 80th Ave	Frankfort	2		3		$ -	2030	WCDOT GM

* Project timelines are estimates only and may change due to change in project schedules.
** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH4	S Cedar Rd & Driveway	Homer Glen	4	7	3		$ -	2028	Local
CH4	S Cedar Rd & Driveway	Homer Glen	3		3		$ -	2028	Local
CH4	S Cedar Rd & Driveway	Homer Glen	4	6	3		$ -	2028	Local
CH4	S Cedar Rd & Driveway	Homer Glen	2		3		$ -	2028	Local
CH16	S Bell Rd & Glengary Rd	Homer Glen		6	2		$ -	2028	Local
CH16	S Bell Rd & Glengary Rd	Homer Glen	6		2		$ -	2028	Local
CH16	S Bell Rd & Glengary Rd	Homer Glen			2		$ -	2028	Local
CH16	S Bell Rd & Glengary Rd	Homer Glen			2		$ -	2028	Local
CH16	S Bell Rd & Glengary Rd	Homer Glen			2		$ -	2028	Local
CH16	S Bell Rd & Glengary Rd	Homer Glen			2		$ -	2028	Local
CH16	S Bell Rd & Driveway	Homer Glen			1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen			1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen			1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen			1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen			1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen			1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen	5	5	1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen			1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen	2	2	1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen			1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen	6	6	1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen			1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen	4	4	2		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen			2		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen	1	5	2		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen	4		2		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen			2		$ -	2023	5 Year Plan
CH16	S Bell Rd & W Martingale Ln	Homer Glen	2	10	2		$ -	2023	5 Year Plan
CH16	S Bell Rd & W Martingale Ln	Homer Glen	1		2		$ -	2023	5 Year Plan
CH16	S Bell Rd & W Martingale Ln	Homer Glen	2		2		$ -	2023	5 Year Plan
CH16	S Bell Rd & W Martingale Ln	Homer Glen	5		2		$ -	2023	5 Year Plan
CH16	S Bell Rd & Founders Xing	Homer Glen	2	2	2		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen			1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen			1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen			1		$ -	2023	5 Year Plan

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH16	S Bell Rd & W 151st St	Homer Glen		1	1		$ -	2023	5 Year Plan
CH16	S Bell Rd & W 151st St	Homer Glen	1		1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Driveway	Homer Glen			1		$ -	2028	Local
CH16	S Bell Rd & Driveway	Homer Glen			1		$ -	2028	Local
CH16	S Bell Rd & Woodland Dr	Homer Glen			1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Woodland Dr	Homer Glen			1		$ -	2023	5 Year Plan
CH16	S Bell Rd & Meadowview Ln	Homer Glen		1	3		$ -	2023	5 Year Plan
CH16	S Bell Rd & Meadowview Ln	Homer Glen			3		$ -	2023	5 Year Plan
CH16	S Bell Rd & Meadowview Ln	Homer Glen	1		3		$ -	2023	5 Year Plan
CH16	S Bell Rd & Meadowview Ln	Homer Glen			3		$ -	2023	5 Year Plan
CH37	W 143rd St & Driveway	Homer Glen	4	4	2		$ -	2028	Local
CH37	W 143rd St & Somerset Rd	Homer Glen	2	9	1		$ -	2028	Local
CH37	W 143rd St & Somerset Rd	Homer Glen	7		1		$ -	2028	Local
CH37	W 143rd St & Mallard St	Homer Glen	2	28	1		$ -	2028	Local
CH37	W 143rd St & Mallard St	Homer Glen	2		1		$ -	2028	Local
CH37	W 143rd St & Mallard St	Homer Glen	4		1		$ -	2028	Local
CH37	W 143rd St & Mallard St	Homer Glen	6		1		$ -	2028	Local
CH37	W 143rd St & Mallard St	Homer Glen	5		1		$ -	2028	Local
CH37	W 143rd St & Mallard St	Homer Glen	4		1		$ -	2028	Local
CH37	W 143rd St & Mallard St	Homer Glen	3		1		$ -	2028	Local
CH37	W 143rd St & Mallard St	Homer Glen	2		1		$ -	2028	Local
CH37	W 143rd St & S Pheasant Rd	Homer Glen	6	28	2		$ -	2028	Local
CH37	W 143rd St & S Pheasant Rd	Homer Glen	2		2		$ -	2028	Local
CH37	W 143rd St & S Pheasant Rd	Homer Glen	5		2		$ -	2028	Local
CH37	W 143rd St & S Pheasant Rd	Homer Glen	4		2		$ -	2028	Local
CH37	W 143rd St & S Pheasant Rd	Homer Glen	6		2		$ -	2028	Local
CH37	W 143rd St & S Pheasant Rd	Homer Glen	5		2		$ -	2028	Local
CH37	W 143rd St & S Greystone Dr	Homer Glen	6	35	2		$ -	2023	5 Year Plan
CH37	W 143rd St & S Greystone Dr	Homer Glen	6		2		$ -	2023	5 Year Plan

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH37	W 143rd St & S Greystone Dr	Homer Glen	2		2		$ -	2023	5 Year Plan
CH37	W 143rd St & S Greystone Dr	Homer Glen	2		2		$ -	2023	5 Year Plan
CH37	W 143rd St & S Greystone Dr	Homer Glen	10		2		$ -	2023	5 Year Plan
CH37	W 143rd St & S Greystone Dr	Homer Glen	9		2		$ -	2023	5 Year Plan
CH37	W 143rd St & Driveway	Homer Glen	7	12	2		$ -	2023	5 Year Plan
CH37	W 143rd St & Driveway	Homer Glen	5		2		$ -	2023	5 Year Plan
CH37	W 143rd St & Driveway	Homer Glen	7	15	2		$ -	2023	5 Year Plan
CH37	W 143rd St & Driveway	Homer Glen	8		2		$ -	2023	5 Year Plan
CH1	W Hadley Rd & Wedgewood Dr	Homer Glen	5	5	1		$ -	2028	Local

* Project timelines are estimates only and may change due to change in project schedules.

** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH5	Caton Farm Rd & Golfview Dr	Joliet	9	32	1		$ -	2032-2037	Local
CH5	Caton Farm Rd & Golfview Dr	Joliet	5		1		$ -	2032-2037	Local
CH5	Caton Farm Rd & Golfview Dr	Joliet	11		1		$ -	2032-2037	Local
CH5	Caton Farm Rd & Golfview Dr	Joliet	7		1		$ -	2032-2037	Local
CH5	Caton Farm Rd & Chevy Chase Dr	Joliet	6	9	1		$ -	2032-2037	Local
CH5	Caton Farm Rd & Chevy Chase Dr	Joliet	3		1		$ -	2032-2037	Local
CH5	Caton Farm Rd & Driveway	Joliet	10	15	2		$ -	2032-2037	Local
CH5	Caton Farm Rd & Driveway	Joliet	5		2		$ -	2032-2037	Local
CH5	Caton Farm Rd & Enid St	Joliet	5	11	2		$ -	2032-2037	Local
CH5	Caton Farm Rd & Enid St	Joliet	6		2		$ -	2032-2037	Local
CH5	Caton Farm Rd & June St	Joliet	1	3	1		$ -	2032-2037	Local
CH5	Caton Farm Rd & June St	Joliet	1		2		$ -	2032-2037	Local
CH5	Caton Farm Rd & June St	Joliet			1		$ -	2032-2037	Local
CH5	Caton Farm Rd & June St	Joliet	1		1		$ -	2032-2037	Local
CH5	Caton Farm Rd & Driveway	Joliet	8	8	2		$ -	2032-2037	Local
CH5	Caton Farm Rd & Essington Rd	Joliet	1	7	2		$ -	2032-2037	Local
CH5	Caton Farm Rd & Essington Rd	Joliet	2		2		$ -	2032-2037	Local
CH5	Caton Farm Rd & Essington Rd	Joliet	3		2		$ -	2032-2037	Local
CH5	Caton Farm Rd & Essington Rd	Joliet	1		2		$ -	2032-2037	Local
CH42	Brandon Rd & W Laraway Rd	Joliet	1	2	1		$ -	2032-2037	Local
CH42	Brandon Rd & W Laraway Rd	Joliet	1		1		$ -	2032-2037	Local
CH51	Mills Rd & Driveway	Joliet	8	13	1		$ -	2032-2037	Local
CH51	Mills Rd & Driveway	Joliet	5		1		$ -	2032-2037	Local
CH51	Mills Rd & Driveway	Joliet	8	8	1		$ -	2032-2037	Local
CH52	N Gougar Rd & Lightning Ct	Joliet	5	7	1		$ -	2032-2037	Local
CH52	N Gougar Rd & Lightning Ct	Joliet	2		1		$ -	2032-2037	Local
CH52	N Gougar Rd & Apache Dr	Joliet	6	10	1		$ -	2032-2037	Local

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH52	N Gougar Rd & Apache Dr	Joliet	4		1		$ -	2032-2037	Local
CH52	N Gougar Rd & Edgecreek Dr	Joliet	7	7	1		$ -	2032-2037	Local
CH52	N Gougar Rd & Chestnut Pointe Dr	Joliet	9	13	1		$ -	2032-2037	Local
CH52	N Gougar Rd & Chestnut Pointe Dr	Joliet	4		1		$ -	2032-2037	Local
CH52	N Gougar Rd & Golf Rd	Joliet	6	6	1		$ -	2032-2037	Local
CH52	N Gougar Rd & Driveway	Joliet	2	4	2		$ -	2032-2037	Local
CH52	N Gougar Rd & Driveway	Joliet	2		2		$ -	2032-2037	Local
CH62	Fernwood Ave & Freedom Blvd	Joliet	5	15	1		$ -	2032-2037	Local
CH62	Fernwood Ave & Freedom Blvd	Joliet	3		1		$ -	2032-2037	Local
CH62	Fernwood Ave & Freedom Blvd	Joliet	4		1		$ -	2032-2037	Local
CH62	Fernwood Ave & Freedom Blvd	Joliet	3		1		$ -	2032-2037	Local

* Project timelines are estimates only and may change due to change in project schedules.

** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH37	W 143rd St & W Prologis Pkwy	Lockport	7	10	1		$ -	2037	WCDOT GM
CH37	W 143rd St & W Prologis Pkwy	Lockport	3		2		$ -	2037	WCDOT GM
CH37	W 143rd St & W Prologis Pkwy	Lockport			1		$ -		
CH4	S Cedar Rd & W Victoria Xing	Lockport	5	12	1		$ -	2027	WCDOT GM
CH4	S Cedar Rd & W Victoria Xing	Lockport	4		1		$ -	2027	WCDOT GM
CH4	S Cedar Rd & W Victoria Xing	Lockport	3		1		$ -	2027	WCDOT GM
CH62	S Briggs St & Newberry Ridge Dr	Lockport	6	11	1		$ -	2029	WCDOT GM
CH62	S Briggs St & Newberry Ridge Dr	Lockport	5		1		$ -	2029	WCDOT GM
CH62	S Briggs St & Parkview Ln	Lockport	6	15	1		$ -	2029	WCDOT GM
CH62	S Briggs St & Parkview Ln	Lockport	3		1		$ -	2029	WCDOT GM
CH62	S Briggs St & Parkview Ln	Lockport	6		1		$ -	2029	WCDOT GM
CH62	S Briggs St & Rosanne St	Lockport	5	16	1		$ -	2029	WCDOT GM
CH62	S Briggs St & Rosanne St	Lockport	4		1		$ -	2029	WCDOT GM
CH62	S Briggs St & Rosanne St	Lockport	3		1		$ -	2029	WCDOT GM
CH62	S Briggs St & Rosanne St	Lockport	4		1		$ -	2029	WCDOT GM
CH62	S Briggs St & South St	Lockport	4	7	1		$ -	2029	WCDOT GM
CH62	S Briggs St & South St	Lockport	3		1		$ -	2029	WCDOT GM
CH62 CH75	S Briggs St & E Division St	Lockport			3		$ -		
CH62 CH75	S Briggs St & E Division St	Lockport			3		$ -		
CH75	E Division St & Cleveland St	Lockport	2	4	3		$ -	2028	WCDOT GM
CH75	E Division St & Cleveland St	Lockport	2		3		$ -	2028	WCDOT GM
CH75	E Division St & Grandview Ave	Lockport	7	7	3		$ -	2028	WCDOT GM
CH75	E Division St & Driveway	Lockport	4	8	1		$ -	2028	WCDOT GM
CH75	E Division St & Driveway	Lockport	4		1		$ -	2028	WCDOT GM
CH75	E Division St & Summit Dr	Lockport	4	6	1		$ -	2028	WCDOT GM
CH75	E Division St & Summit Dr	Lockport	1		1		$ -	2028	WCDOT GM
CH75	E Division St & Summit Dr	Lockport			1		$ -	2028	WCDOT GM
CH75	E Division St & Summit Dr	Lockport	1		1		$ -	2028	WCDOT GM
CH75	E Division St & Peachtree Ln	Lockport	8	30	1		$ -	2028	WCDOT GM

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH75	E Division St & Peachtree Ln	Lockport	6		1		$ -	2028	WCDOT GM
CH75	E Division St & Peachtree Ln	Lockport	7		1		$ -	2028	WCDOT GM
CH75	E Division St & Peachtree Ln	Lockport	9		1		$ -	2028	WCDOT GM
CH75	E Division St & Strawberry Hill Dr	Lockport	9	33	1		$ -	2028	WCDOT GM
CH75	E Division St & Strawberry Hill Dr	Lockport	6		1		$ -	2028	WCDOT GM
CH75	E Division St & Strawberry Hill Dr	Lockport	10		1		$ -	2028	WCDOT GM
CH75	E Division St & Strawberry Hill Dr	Lockport	8		1		$ -	2028	WCDOT GM
CH75	E Division St & Read St	Lockport	1	2	1		$ -	2028	WCDOT GM
CH75	E Division St & Read St	Lockport	1		1		$ -	2028	WCDOT GM
CH75	E Division St & Driveway	Lockport	11	16	1		$ -	2028	WCDOT GM
CH75	E Division St & Driveway	Lockport	5		1		$ -	2028	WCDOT GM
CH75	E Division St & Driveway	Lockport	6	7	1		$ -	2028	WCDOT GM
CH75	E Division St & Driveway	Lockport	1		1		$ -	2028	WCDOT GM
CH75	E Division St & Lago Vista Blvd	Lockport	4	26	1		$ -	2028	WCDOT GM
CH75	E Division St & Lago Vista Blvd	Lockport	9		1		$ -	2028	WCDOT GM
CH75	E Division St & Lago Vista Blvd	Lockport	8		1		$ -	2028	WCDOT GM
CH75	E Division St & Lago Vista Blvd	Lockport	5		1		$ -	2028	WCDOT GM
CH75	E Division St & S Bello Dr	Lockport	9	23	1		$ -	2028	WCDOT GM
CH75	E Division St & S Bello Dr	Lockport	6		1		$ -	2028	WCDOT GM
CH75	E Division St & S Bello Dr	Lockport	8		1		$ -	2028	WCDOT GM
CH75	E Division St & S Farrelll Rd	Lockport			1		$ -		
CH75	E Division St & S Farrelll Rd	Lockport			1		$ -		
CH75	E Division St & S Farrelll Rd	Lockport			1		$ -		
CH75	E Division St & S Farrelll Rd	Lockport			1		$ -		
CH75	W 167th St & Driveway	Lockport	7	9	2		$ -	2028	WCDOT GM
CH75	W 167th St & Driveway	Lockport	2		2		$ -	2028	WCDOT GM
CH75	W 167th St & Driveway	Lockport	5	14	2		$ -	2028	WCDOT GM
CH75	W 167th St & Driveway	Lockport	9		2		$ -	2028	WCDOT GM
CH75	W 167th St & S Finley Pkwy	Lockport	8	17	1		$ -	2028	WCDOT GM
CH75	W 167th St & S Finley Pkwy	Lockport	9		1		$ -	2028	WCDOT GM

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH75	W 167th St & S Blackfoot Dr	Lockport	6	14	1		$ -	2028	WCDOT GM
CH75	W 167th St & S Blackfoot Dr	Lockport	8		1		$ -	2028	WCDOT GM
CH75	W 167th St & W Long Meadow Dr	Lockport	4	41	1		$ -	2028	WCDOT GM
CH75	W 167th St & W Long Meadow Dr	Lockport	7		1		$ -	2028	WCDOT GM
CH75	W 167th St & W Long Meadow Dr	Lockport	6		1		$ -	2028	WCDOT GM
CH75	W 167th St & W Long Meadow Dr	Lockport	8		1		$ -	2028	WCDOT GM
CH75	W 167th St & W Long Meadow Dr	Lockport	7		1		$ -	2028	WCDOT GM
CH75	W 167th St & W Long Meadow Dr	Lockport	9		1		$ -	2028	WCDOT GM
CH75	W 167th St & S Windsor Ln	Lockport	4	16	1		$ -	2028	WCDOT GM
CH75	W 167th St & S Windsor Ln	Lockport	5		1		$ -	2028	WCDOT GM
CH75	W 167th St & S Windsor Ln	Lockport	4		1		$ -	2028	WCDOT GM
CH75	W 167th St & S Windsor Ln	Lockport	3		1		$ -	2028	WCDOT GM
CH75	W 167th St & Driveway	Lockport	1	2	1		$ -	2028	WCDOT GM
CH75	W 167th St & Driveway	Lockport	1		1		$ -	2028	WCDOT GM

* Project timelines are estimates only and may change due to change in project schedules.

** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH17	Manhattan Rd & W North St	Manhattan	4	14	2		$ -	2029	WCDOT GM
CH17	Manhattan Rd & W North St	Manhattan	1		1		$ -	2029	WCDOT GM
CH17	Manhattan Rd & W North St	Manhattan	7		2		$ -	2029	WCDOT GM
CH17	Manhattan Rd & W North St	Manhattan	2		2		$ -	2029	WCDOT GM
CH17	Manhattan Rd & Driveway	Manhattan	3	4	2		$ -	2029	WCDOT GM
CH17	Manhattan Rd & Driveway	Manhattan	1		2		$ -	2029	WCDOT GM
CH17	Manhattan Rd & Marion St	Manhattan	5	15	1		$ -	2029	WCDOT GM
CH17	Manhattan Rd & Marion St	Manhattan	5		1		$ -	2029	WCDOT GM
CH17	Manhattan Rd & Marion St	Manhattan	5		1		$ -	2029	WCDOT GM
CH17	Manhattan Rd & Fairview Dr	Manhattan	8	11	1		$ -	2029	WCDOT GM
CH17	Manhattan Rd & Fairview Dr	Manhattan	3		1		$ -	2029	WCDOT GM
CH17	Manhattan Rd & Driveway	Manhattan	3	3	1		$ -	2029	WCDOT GM
CH17	Manhattan Rd & S Gougar Rd	Manhattan	3	3	2		$ -	2029	WCDOT GM

* Project timelines are estimates only and may change due to change in project schedules.
** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH32	McEvilly Rd & Santos Ave	Minooka	7	45	1		$ -	2035	Local
CH32	McEvilly Rd & Santos Ave	Minooka	8		1		$ -	2035	Local
CH32	McEvilly Rd & Santos Ave	Minooka	9		1		$ -	2035	Local
CH32	McEvilly Rd & Santos Ave	Minooka	7		1		$ -	2035	Local
CH32	McEvilly Rd & Santos Ave	Minooka	7		1		$ -	2035	Local
CH32	McEvilly Rd & Santos Ave	Minooka	7		1		$ -	2035	Local
CH32	McEvilly Rd & Vista Ct	Minooka		2	1		$ -	2035	Local
CH32	McEvilly Rd & Vista Ct	Minooka	2		1		$ -	2035	Local

* Project timelines are estimates only and may change due to change in project schedules.
** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH38	W 187th St & Wolf Rd	Mokena	8	25	2		$ -	2035	Local
CH38	W 187th St & Wolf Rd	Mokena	6		2		$ -	2022	Local
CH38	W 187th St & Wolf Rd	Mokena	4		2		$ -	2022	Local
CH38	W 187th St & Wolf Rd	Mokena	7		2		$ -	2022	Local
CH38	W 187th St & S Mill Creek Dr	Mokena	6	9	2		$ -	2022	Local
CH38	W 187th St & S Mill Creek Dr	Mokena	3		2		$ -	2029	Local
CH38	W 187th St & 114th Ave	Mokena	8	16	1		$ -	2029	Local
CH38	W 187th St & 114th Ave	Mokena	8		1		$ -	2029	Local
CH38	W 187th St & Swan Dr	Mokena	10	48	1		$ -	2029	Local
CH38	W 187th St & Swan Dr	Mokena	11		1		$ -	2029	Local
CH38	W 187th St & Swan Dr	Mokena	4		1		$ -	2029	Local
CH38	W 187th St & Swan Dr	Mokena	7		1		$ -	2029	Local
CH38	W 187th St & Swan Dr	Mokena	9		1		$ -	2029	Local
CH38	W 187th St & Swan Dr	Mokena	7		1		$ -	2029	Local
CH38	W 187th St & Creekview Ln	Mokena	10	28	1		$ -	2024	Local
CH38	W 187th St & Creekview Ln	Mokena	10		1		$ -	2024	Local
CH38	W 187th St & Creekview Ln	Mokena	8		1		$ -	2024	Local
CH63	N Schoolhouse Rd & Chatfield Rd	Mokena	8	21	1		$ -	2028	Local
CH63	N Schoolhouse Rd & Chatfield Rd	Mokena	4		1		$ -	2028	Local
CH63	N Schoolhouse Rd & Chatfield Rd	Mokena	3		1		$ -	2028	Local
CH63	N Schoolhouse Rd & Chatfield Rd	Mokena	6		1		$ -	2028	Local
CH63	N Schoolhouse Rd & Driveway	Mokena	2	3	1		$ -	2028	Local
CH63	N Schoolhouse Rd & Driveway	Mokena	1		1		$ -	2028	Local
CH64	Francis Rd & Snowmass Ln	Mokena	8	15	1		$ -	2024	Local
CH64	Francis Rd & Snowmass Ln	Mokena	7		1		$ -	2024	Local
CH64	Francis Rd & Breckenridge Dr	Mokena	2	17	1		$ -	2024	Local
CH64	Francis Rd & Breckenridge Dr	Mokena	6		1		$ -	2024	Local

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH64	Francis Rd & Breckenridge Dr	Mokena	4		1		$ -	2024	Local
CH64	Francis Rd & Breckenridge Dr	Mokena	5		1		$ -	2024	Local
CH64	Francis Rd & Dikran Rd	Mokena	1	2	1		$ -	2025	Local
CH64	Francis Rd & Dikran Rd	Mokena	1		1		$ -	2025	Local
CH64	Francis Rd & S Townline Rd	Mokena	8	23	1		$ -	2026	Local
CH64	Francis Rd & S Townline Rd	Mokena	9		1		$ -	2026	Local
CH64	Francis Rd & S Townline Rd	Mokena	3		1		$ -	2026	Local
CH64	Francis Rd & S Townline Rd	Mokena	3		1		$ -	2026	Local
CH64	Francis Rd & Driveway	Mokena	1	3	1		$ -	2028	Local
CH64	Francis Rd & Driveway	Mokena	2		1		$ -	2028	Local
CH64	Francis Rd & Driveway	Mokena	2	7	2		$ -	2028	Local
CH64	Francis Rd & Driveway	Mokena	5		2		$ -	2028	Local
CH64	Francis Rd & Glenell Ave	Mokena	4	9	1		$ -	2025	Local
CH64	Francis Rd & Glenell Ave	Mokena	5		1		$ -	2025	Local
CH64	Francis Rd & Greenview Ave	Mokena	4	11	1		$ -	2025	Local
CH64	Francis Rd & Greenview Ave	Mokena	7		1		$ -	2025	Local
CH64	Francis Rd & Woodhaven Dr	Mokena	6	11	1		$ -	2024	Local
CH64	Francis Rd & Woodhaven Dr	Mokena	5		2		$ -	2024	Local
CH84	191st St & Old Lagrange Rd	Mokena	6	13	1		$ -	2033	Local
CH84	191st St & Old Lagrange Rd	Mokena	7		1		$ -	2033	Local
CH84	191st St & Driveway	Mokena	7	14	1		$ -	2027	Local
CH84	191st St & Driveway	Mokena	7		1		$ -	2027	Local
CH84	W 191st St & Henry Dr	Mokena	9	20	1		$ -	2031	Local
CH84	W 191st St & Henry Dr	Mokena	5		1		$ -	2031	Local
CH84	W 191st St & Henry Dr	Mokena	6		1		$ -	2031	Local
CH84	W 191st St & Hickory Creek Dr	Mokena	7	51	1		$ -	2032	Local
CH84	W 191st St & Hickory Creek Dr	Mokena	6		1		$ -	2032	Local
CH84	W 191st St & Hickory Creek Dr	Mokena	5		1		$ -	2032	Local
CH84	W 191st St & Hickory Creek Dr	Mokena	6		1		$ -	2032	Local

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH84	W 191st St & Hickory Creek Dr	Mokena	7		1		$ -	2032	Local
CH84	W 191st St & Hickory Creek Dr	Mokena	7		1		$ -	2032	Local
CH84	W 191st St & Hickory Creek Dr	Mokena	7		1		$ -	2032	Local
CH84	W 191st St & Hickory Creek Dr	Mokena	6		1		$ -	2032	Local
CH84	W 191st St & Jodi Rd	Mokena	4	4	1		$ -	2032	Local
CH84	W 191st St & Darvin Dr	Mokena	7	11	1		$ -	2023	Local
CH84	W 191st St & Darvin Dr	Mokena	4		1		$ -	2023	Local
CH84	W 191st St & Driveway	Mokena	9	18	1		$ -	2028	Local
CH84	W 191st St & Driveway	Mokena	9		1		$ -	2028	Local
CH84	W 191st St & Driveway	Mokena	5	12	1		$ -	2028	Local
CH84	W 191st St & Driveway	Mokena	7		1		$ -	2028	Local
CH84	W 191st St & Driveway	Mokena	7	11	1		$ -	2030	Local
CH84	W 191st St & Driveway	Mokena	4		1		$ -	2030	Local
CH84	W 191st St & Driveway	Mokena	2	8	1		$ -	2030	Local
CH84	W 191st St & Driveway	Mokena	6		1		$ -	2030	Local
CH84	W 191st St & Driveway	Mokena	6	12	1		$ -	2031	Local
CH84	W 191st St & Driveway	Mokena	6		1		$ -	2031	Local
CH84	W 191st St & Driveway	Mokena	5	11	1		$ -	2031	Local
CH84	W 191st St & Driveway	Mokena	6		1		$ -	2031	Local
CH84	W 191st St & S 88th Ave	Mokena	3	21	1		$ -	2023	Local
CH84	W 191st St & S 88th Ave	Mokena	6		1		$ -	2023	Local
CH84	W 191st St & S 88th Ave	Mokena	6		1		$ -	2023	Local
CH84	W 191st St & S 88th Ave	Mokena	6		1		$ -	2023	Local
CH84	W 191st St & 85th Ct	Mokena	3	3	1		$ -	2027	Local
CH84	W 191st St & Driveway	Mokena	5	12	1		$ -	2028	Local
CH84	W 191st St & Driveway	Mokena	7		1		$ -	2028	Local
CH84	191st St & Driveway	Mokena	7	13	1		$ -	2028	Local
CH84	191st St & Driveway	Mokena	6		1		$ -	2028	Local
CH84	191st St & Driveway	Mokena	7	7	1		$ -	2030	Local
CH84	191st St & Driveway	Mokena			1		$ -	2030	Local

* Project timelines are estimates only and may change due to change in project schedules.

** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH10	S Will Center Rd & W Margaret St	Monee	2	2	1	No Remediation			

* Project timelines are estimates only and may change due to change in project schedules.
** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH37	W 143rd St & S Will Cook Rd	Multiple	4	17	2		$ -	2030	WCDOT GM
CH37	W 143rd St & S Will Cook Rd	Multiple			2		$ -	2030	WCDOT GM
CH37	W 143rd St & S Will Cook Rd	Multiple	8		2		$ -	2030	WCDOT GM
CH37	W 143rd St & S Will Cook Rd	Multiple	5		2		$ -	2030	WCDOT GM
CH4	S Cedar Rd & W Ashton Dr	Multiple	7	34	1		$ -	2027	WCDOT GM
CH4	S Cedar Rd & W Ashton Dr	Multiple	7		1		$ -	2027	WCDOT GM
CH4	S Cedar Rd & W Ashton Dr	Multiple	7		1		$ -	2027	WCDOT GM
CH4	S Cedar Rd & W Ashton Dr	Multiple	7		1		$ -	2027	WCDOT GM
CH4	S Cedar Rd & W Ashton Dr	Multiple	6		1		$ -	2027	WCDOT GM
CH36	Renwick Rd & Driveway	Multiple			2		$ -	2031	WCDOT GM
CH36	Renwick Rd & Driveway	Multiple			2		$ -	2031	WCDOT GM
CH36	Renwick Rd & Driveway	Multiple	1	1	2		$ -	2031	WCDOT GM
CH36	Renwick Rd & Driveway	Multiple			2		$ -	2031	WCDOT GM
CH36	W Renwick Rd & W Grand Haven Rd	Multiple	7	15	1		$ -	2031	WCDOT GM
CH36	W Renwick Rd & W Grand Haven Rd	Multiple	8		1		$ -	2031	WCDOT GM
CH36	W Renwick Rd & Gaylord Rd	Multiple	1	1	1		$ -	2033	Local
CH36	W Renwick Rd & Old Renwick Trl	Multiple	3	4	1		$ -	2033	Local
CH36	W Renwick Rd & Old Renwick Trl	Multiple	1		1		$ -	2033	Local
CH83	80th Ave & 183rd St	Multiple	9	13	1		$ -	2023	5 Year Plan
CH83	80th Ave & 183rd St	Multiple	4		1		$ -	2023	5 Year Plan
CH88	N Weber Rd & Lakeview Dr	Multiple					$ -		
CH88	N Weber Rd & Rodeo Dr	Multiple			1		$ -		
CH88	N Weber Rd & Rodeo Dr	Multiple			1		$ -		
CH88	N Weber Rd & Rodeo Dr	Multiple			1		$ -		
CH88	N Weber Rd & Remington Blvd	Multiple			1		$ -		
CH88	N Weber Rd & Remington Blvd	Multiple			1		$ -		
CH88	N Weber Rd & Remington Blvd	Multiple			1		$ -		

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH88	N Weber Rd & Remington Blvd	Multiple			1		$ -		
CH88	N Weber Rd & Remington Blvd	Multiple			1		$ -		

* Project timelines are estimates only and may change due to change in project schedules.
** MEP=Maximum Extents Practicable

Intersection	Jurisdiction Breakdown
W 143rd St & S Will Cook Rd	East Side is Orland Park, Cook County
Western Ave & W 34th St	North Side is Park Forest, Cook County
S Cedar Rd & W Ashton Dr	Lockport on West Side, Homer Glen on East Side
Renwick Rd & Driveway	Lockport on West Side, Homer Glen on East Side
W Renwick Rd & W Grand Haven Rd	Romeoville on North Side, Crest Hill on South Side
W Renwick Rd & Gaylord Rd	Romeoville on north, Joliet on southwest, Crest Hill on southeast
W Renwick Rd & Old Renwick Trl	Romeoville on North Side, Joliet on South Side
80th Ave & 183rd St	North Side is Tinley Park, Cook County
S Gougar Rd & W Maple Rd	Joliet on West Side, New Lenox on East Side
N Weber Rd & Lakeview Dr	Bolingbrook on West Side, Romeoville on East Side
N Weber Rd & Rodeo Dr	Bolingbrook on west side and northeast corner, Romeoville on southeast corner
N Weber Rd & Remington Blvd	Bolingbrook on West Side, Romeoville on East Side

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH89	95th St & Cheyenne Dr	Naperville	6	21	1		$ -	2025	Local
CH89	95th St & Cheyenne Dr	Naperville	3		1		$ -	2025	Local
CH89	95th St & Cheyenne Dr	Naperville	6		1		$ -	2025	Local
CH89	95th St & Cheyenne Dr	Naperville	6		1		$ -	2025	Local
CH89	95th St & Knoch Knolls Rd	Naperville	3	32	1		$ -	2025	Local
CH89	95th St & Knoch Knolls Rd	Naperville	4		1		$ -	2025	Local
CH89	95th St & Knoch Knolls Rd	Naperville	3		1		$ -	2025	Local
CH89	95th St & Knoch Knolls Rd	Naperville	2		1		$ -	2025	Local
CH89	95th St & Knoch Knolls Rd	Naperville	4		1		$ -	2025	Local
CH89	95th St & Knoch Knolls Rd	Naperville	2		1		$ -	2025	Local
CH89	95th St & Knoch Knolls Rd	Naperville	8		1		$ -	2025	Local
CH89	95th St & Knoch Knolls Rd	Naperville	6		1		$ -	2025	Local
CH89	95th St & Eagle Brook Ln	Naperville	5	11	1		$ -	2025	Local
CH89	95th St & Eagle Brook Ln	Naperville	4		1		$ -	2025	Local
CH89	95th St & Eagle Brook Ln	Naperville	1		1		$ -	2025	Local
CH89	95th St & Eagle Brook Ln	Naperville	1		1		$ -	2025	Local
CH14	Plainfield-Naperville Rd & 87th St	Naperville (DuPage County)	8	47	1		$ -		
CH14	Plainfield-Naperville Rd & 87th St	Naperville (DuPage County)	5		1		$ -		
CH14	Plainfield-Naperville Rd & 87th St	Naperville	4		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & 87th St	Naperville	8		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & 87th St	Naperville	6		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & 87th St	Naperville	3		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & 87th St	Naperville (DuPage County)	7		1		$ -		
CH14	Plainfield-Naperville Rd & 87th St	Naperville (DuPage County)	6		1		$ -		

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH14	Plainfield-Naperville Rd & HillView Rd	Naperville	2	3	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & HillView Rd	Naperville	1		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Plainview Dr	Naperville	3	3	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Plainview Dr	Naperville			1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Meadow Dr	Naperville		1	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Meadow Dr	Naperville	1		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Countryview Dr	Naperville	4	4	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Countryview Dr	Naperville			1		$ -		
CH14	Plainfield-Naperville Rd & Rock Spring Rd	Naperville	3	8	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Rock Spring Rd	Naperville	5		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Leverenz Rd	Naperville	9	68	1		$ -	2024	Local
CH14	Plainfield-Naperville Rd & Leverenz Rd	Naperville	9		1		$ -	2024	Local
CH14	Plainfield-Naperville Rd & Leverenz Rd	Naperville	8		1		$ -	2024	Local
CH14	Plainfield-Naperville Rd & Leverenz Rd	Naperville	8		1		$ -	2024	Local
CH14	Plainfield-Naperville Rd & Leverenz Rd	Naperville	6		1		$ -	2024	Local
CH14	Plainfield-Naperville Rd & Leverenz Rd	Naperville	9		2		$ -	2024	Local
CH14	Plainfield-Naperville Rd & Leverenz Rd	Naperville	8		2		$ -	2024	Local
CH14	Plainfield-Naperville Rd & Leverenz Rd	Naperville	11		1		$ -	2024	Local

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH14	Plainfield-Naperville Rd & Driveway	Naperville	9	17	2		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Driveway	Naperville	8		2		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Gateshead Dr	Naperville	11	77	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Gateshead Dr	Naperville	9		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Gateshead Dr	Naperville	7		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Gateshead Dr	Naperville	7		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Gateshead Dr	Naperville	5		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Gateshead Dr	Naperville	13		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Gateshead Dr	Naperville	13		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Gateshead Dr	Naperville	12		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Breckenridge Ln	Naperville	1	2	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Breckenridge Ln	Naperville	1		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & 95th St	Naperville		12	1		$ -	2025	Local
CH14	Plainfield-Naperville Rd & 95th St	Naperville	2		2		$ -	2025	Local
CH14	Plainfield-Naperville Rd & 95th St	Naperville	3		2		$ -	2025	Local
CH14	Plainfield-Naperville Rd & 95th St	Naperville	1		2		$ -	2025	Local
CH14	Plainfield-Naperville Rd & 95th St	Naperville	2		2		$ -	2025	Local
CH14	Plainfield-Naperville Rd & 95th St	Naperville	1		2		$ -	2025	Local
CH14	Plainfield-Naperville Rd & 95th St	Naperville	3		2		$ -	2025	Local
CH14	Plainfield-Naperville Rd & 95th St	Naperville			1		$ -	2025	Local

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH14	Plainfield-Naperville Rd & Driveway	Naperville	1	3	2		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Driveway	Naperville	2		2		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Timber Creek Ln	Naperville	1	1	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Timber Creek Ln	Naperville			1		$ -		
CH14	Plainfield-Naperville Rd & Conan Doyle Rd	Naperville	7	23	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Conan Doyle Rd	Naperville	10		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Conan Doyle Rd	Naperville			1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Conan Doyle Rd	Naperville	6		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Hamlet Rd	Naperville	6	13	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Hamlet Rd	Naperville	7		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Tramore Ct	Naperville	8	13	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Tramore Ct	Naperville	5		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Saratoga Rd	Naperville	3	10	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Saratoga Rd	Naperville	7		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Driveway	Naperville	6	12	2		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Driveway	Naperville	6		2		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & 104th St	Naperville	5	20	2		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & 104th St	Naperville	7		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & 104th St	Naperville	5		2		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & 104th St	Naperville	3		2		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Driveway	Naperville	6	15	1		$ -	2023	WCDOT GM

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH14	Plainfield-Naperville Rd & Driveway	Naperville	9		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Driveway	Naperville	6	10	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Driveway	Naperville	4		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Preserve Ave	Naperville	3	13	1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Preserve Ave	Naperville	3		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Preserve Ave	Naperville	3		1		$ -	2023	WCDOT GM
CH14	Plainfield-Naperville Rd & Preserve Ave	Naperville	4		1		$ -	2023	WCDOT GM
CH14	S Naperville Rd & Driveway	Naperville	5	7	3		$ -	2023	WCDOT GM
CH14	S Naperville Rd & Driveway	Naperville	2		3		$ -	2023	WCDOT GM
CH14	S Naperville Rd & Driveway	Naperville	4	8	2		$ -	2023	WCDOT GM
CH14	S Naperville Rd & Driveway	Naperville	4		3		$ -	2023	WCDOT GM
CH14	S Naperville Rd & Driveway	Naperville	7	11	1		$ -	2023	WCDOT GM
CH14	S Naperville Rd & Driveway	Naperville	4		1		$ -	2023	WCDOT GM
CH66	111th St & Driveway	Naperville	4	7	2		$ -	2032	WCDOT GM
CH66	111th St & Driveway	Naperville	3		2		$ -	2032	WCDOT GM
CH66	111th St & Driveway	Naperville	5	9	2		$ -	2032	WCDOT GM
CH66	111th St & Driveway	Naperville	4		2		$ -	2032	WCDOT GM
CH66	111th St & Driveway	Naperville	3	12	1		$ -	2032	WCDOT GM
CH66	111th St & Driveway	Naperville	9		1		$ -	2032	WCDOT GM
CH66	111th St & Driveway	Naperville	10	13	1		$ -	2032	WCDOT GM
CH66	111th St & Driveway	Naperville	3		2		$ -	2032	WCDOT GM
CH66	111th St & Chokeberry Dr	Naperville	1	10	1		$ -	2024	Local
CH66	111th St & Chokeberry Dr	Naperville	2		1		$ -	2024	Local
CH66	111th St & Chokeberry Dr	Naperville			1		$ -	2024	Local
CH66	111th St & Chokeberry Dr	Naperville	1		1		$ -	2024	Local

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH66	111th St & Chokeberry Dr	Naperville	2		1		$ -	2024	Local
CH66	111th St & Chokeberry Dr	Naperville	4		1		$ -	2024	Local
CH66	111th St & Thatcher Dr	Naperville	4	12	1		$ -	2032	WCDOT GM
CH66	111th St & Thatcher Dr	Naperville	5		1		$ -	2032	WCDOT GM
CH66	111th St & Thatcher Dr	Naperville	1		1		$ -	2032	WCDOT GM
CH66	111th St & Thatcher Dr	Naperville	2		1		$ -	2032	WCDOT GM
CH66	111th St & Driveway	Naperville	10	19	1		$ -	2032	WCDOT GM
CH66	111th St & Driveway	Naperville	9		1		$ -	2032	WCDOT GM
CH66	111th St & Book Rd	Naperville	4	22	3		$ -	2032	WCDOT GM
CH66	111th St & Book Rd	Naperville	5		3		$ -	2032	WCDOT GM
CH66	111th St & Book Rd	Naperville	5		2		$ -	2032	WCDOT GM
CH66	111th St & Book Rd	Naperville	8		1		$ -	2032	WCDOT GM
CH66	111th St & Driveway	Naperville	6	12	2		$ -	2032	WCDOT GM
CH66	111th St & Driveway	Naperville	6		2		$ -	2032	WCDOT GM
CH66	111th St & Driveway	Naperville	3	6	2		$ -	2032	WCDOT GM
CH66	111th St & Driveway	Naperville	3		2		$ -	2032	WCDOT GM

* Project timelines are estimates only and may change due to change in project schedules.
** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH4	N Cedar Rd & W Francis Rd	New Lenox	7	9	2		$ -	2023	5 Year Plan
CH4	N Cedar Rd & W Francis Rd	New Lenox	2		2		$ -	2023	5 Year Plan
CH4	N Cedar Rd & Lenox St	New Lenox	3	3	1		$ -	2023	5 Year Plan
CH4	S Cedar Rd & W Illinois Hwy	New Lenox	3	9	2		$ -	2027	WCDOT GM
CH4	S Cedar Rd & W Illinois Hwy	New Lenox	6		2		$ -	2027	WCDOT GM
CH4	S Cedar Rd & Driveway	New Lenox	7	13	2		$ -	2027	WCDOT GM
CH4	S Cedar Rd & Driveway	New Lenox	6		2		$ -	2027	WCDOT GM
CH4	S Cedar Rd & Driveway	New Lenox		1	1		$ -		
CH4	S Cedar Rd & Driveway	New Lenox	1		1		$ -	2027	WCDOT GM
CH4	S Cedar Rd & Driveway	New Lenox	2	3	1		$ -	2027	WCDOT GM
CH4	S Cedar Rd & Driveway	New Lenox	1		2		$ -	2027	WCDOT GM
CH4	S Cedar Rd & W Otto Dr	New Lenox	2	5	1		$ -	2027	WCDOT GM
CH4	S Cedar Rd & W Otto Dr	New Lenox	2		1		$ -	2027	WCDOT GM
CH4	S Cedar Rd & W Otto Dr	New Lenox	1		1		$ -	2027	WCDOT GM
CH4	S Cedar Rd & W Otto Dr	New Lenox			1		$ -		
CH4	S Cedar Rd & Driveway	New Lenox	1	1	2		$ -	2027	WCDOT GM
CH4	S Cedar Rd & Driveway	New Lenox			1		$ -		
CH55	Cherry Hill Rd & Moss Ln	New Lenox	5	5	1		$ -	2028	5 Year Plan
CH55	Cherry Hill Rd & Haven Ave	New Lenox	3	7	1		$ -	2028	5 Year Plan
CH55	Cherry Hill Rd & Haven Ave	New Lenox	4		1		$ -	2028	5 Year Plan
CH52	S Gougar Rd & Berens Dr	New Lenox	2	2	2		$ -	2027	5 Year Plan
CH52	S Gougar Rd & Ellis Rd	New Lenox	2	2	2		$ -	2027	5 Year Plan
CH52	S Gougar Rd & W Haven Ave	New Lenox	4	4	2		$ -	2027	5 Year Plan
CH64	W Francis Rd & Creekside Ct	New Lenox	6	11	1		$ -	2028	WCDOT GM
CH64	W Francis Rd & Creekside Ct	New Lenox	5		1		$ -	2028	WCDOT GM
CH64	E Francis Rd & Driveway	New Lenox	2	4	2		$ -	2023	5 Year Plan
CH64	E Francis Rd & Driveway	New Lenox	2		2		$ -	2023	5 Year Plan
CH64	E Francis Rd & Edmonds Ave	New Lenox	9	18	1		$ -	2028	WCDOT GM
CH64	E Francis Rd & Edmonds Ave	New Lenox	1		1		$ -	2028	WCDOT GM
CH64	E Francis Rd & Edmonds Ave	New Lenox	8		1		$ -	2028	WCDOT GM

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH64	E Francis Rd & Hickory Creek Dr	New Lenox	1	19	1		$ -	2028	WCDOT GM
CH64	E Francis Rd & Hickory Creek Dr	New Lenox	10		1		$ -	2028	WCDOT GM
CH64	E Francis Rd & Hickory Creek Dr	New Lenox	7		1		$ -	2028	WCDOT GM
CH64	E Francis Rd & Hickory Creek Dr	New Lenox	1		1		$ -	2028	WCDOT GM
CH74	E Laraway Rd & S Schoolhouse Rd	New Lenox	1	1	1		$ -	2025	5 Year Plan
CH74	E Laraway Rd & Stonebridge Dr	New Lenox	1	4	1		$ -	2023	5 Year Plan
CH74	E Laraway Rd & Stonebridge Dr	New Lenox	3		1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Driveway	New Lenox	6	6	1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Nelson Rd	New Lenox	4	20	1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Nelson Rd	New Lenox	5		2		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Nelson Rd	New Lenox	6		2		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Nelson Rd	New Lenox	5		1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Driveway	New Lenox	7	27	1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Driveway	New Lenox	8		1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Driveway	New Lenox	6		1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Driveway	New Lenox	6		1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Driveway	New Lenox	3	4	1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Driveway	New Lenox	1		1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Foxwood Dr	New Lenox	7	27	1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Foxwood Dr	New Lenox			1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Foxwood Dr	New Lenox	5		1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Foxwood Dr	New Lenox	8		1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Foxwood Dr	New Lenox	7		1		$ -	2023	5 Year Plan

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH74	W Laraway Rd & Driveway	New Lenox			2		$ -	2024	5 Year Plan
CH74	W Laraway Rd & Driveway	New Lenox	5	12	2		$ -	2024	5 Year Plan
CH74	W Laraway Rd & Driveway	New Lenox	3		1		$ -	2024	5 Year Plan
CH74	W Laraway Rd & Driveway	New Lenox	2		2		$ -	2024	5 Year Plan
CH74	W Laraway Rd & Driveway	New Lenox	2		2		$ -	2024	5 Year Plan
CH74	W Laraway Rd & Calistoga Dr	New Lenox	3	12	1		$ -	2024	5 Year Plan
CH74	W Laraway Rd & Calistoga Dr	New Lenox	4		2		$ -	2024	5 Year Plan
CH74	W Laraway Rd & Calistoga Dr	New Lenox			2		$ -	2024	5 Year Plan
CH74	W Laraway Rd & Calistoga Dr	New Lenox	5		1		$ -	2024	5 Year Plan
CH74	W Laraway Rd & Driveway	New Lenox	5	10	1		$ -	2024	5 Year Plan
CH74	W Laraway Rd & Driveway	New Lenox	5		2		$ -	2024	5 Year Plan
CH74	E Laraway Rd & Whitehall Rd	New Lenox	2	3	1		$ -	2024	5 Year Plan
CH74	E Laraway Rd & Whitehall Rd	New Lenox	1		1		$ -	2024	5 Year Plan
CH74	E Laraway Rd & Whitehall Rd	New Lenox			1		$ -	2024	5 Year Plan
CH74	E Laraway Rd & Whitehall Rd	New Lenox			1		$ -	2024	5 Year Plan
CH74	E Laraway Rd & Rachel Ridge Dr	New Lenox	2	7	1		$ -	2024	5 Year Plan
CH74	E Laraway Rd & Rachel Ridge Dr	New Lenox	3		2		$ -	2024	5 Year Plan
CH74	E Laraway Rd & Rachel Ridge Dr	New Lenox	2		1		$ -	2024	5 Year Plan
CH74	E Laraway Rd & Driveway	New Lenox	7	11	1		$ -	2026	5 Year Plan
CH74	E Laraway Rd & Driveway	New Lenox	4		2		$ -	2026	5 Year Plan
CH74	E Laraway Rd & Driveway	New Lenox	2	6	2		$ -	2026	5 Year Plan
CH74	E Laraway Rd & Driveway	New Lenox	4		2		$ -	2026	5 Year Plan
CH74	E Laraway Rd & Tower Ln	New Lenox	6	6	1		$ -	2026	5 Year Plan
CH74	E Laraway Rd & Driveway	New Lenox	6	13	1		$ -	2026	5 Year Plan
CH74	E Laraway Rd & Driveway	New Lenox	7		1		$ -	2026	5 Year Plan
CH74	E Laraway Rd & Heather Glen Dr	New Lenox	2	9	1		$ -	2026	5 Year Plan

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH74	E Laraway Rd & Heather Glen Dr	New Lenox	3		1		$ -	2026	5 Year Plan
CH74	E Laraway Rd & Heather Glen Dr	New Lenox			1		$ -	2026	5 Year Plan
CH74	E Laraway Rd & Heather Glen Dr	New Lenox	4		1		$ -	2026	5 Year Plan
CH74	W Laraway Rd & Cardinal Dr	New Lenox	3	5	1		$ -	2023	5 Year Plan
CH74	W Laraway Rd & Cardinal Dr	New Lenox	2		1		$ -	2023	5 Year Plan

* Project timelines are estimates only and may change due to change in project schedules.
** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH53	Western Ave & W 34th St	Park Forest (Cook County)	3	13	1		$ -		
CH53	Western Ave & W 34th St	Park Forest (Cook County)	2		1		$ -		
CH53	Western Ave & W 34th St	Park Forest	2		1		$ -	2028	WCDOT GM
CH53	Western Ave & W 34th St	Park Forest	2		1		$ -	2028	WCDOT GM
CH53	Western Ave & W 34th St	Park Forest	2		1		$ -	2028	WCDOT GM
CH53	Western Ave & W 34th St	Park Forest	2		1		$ -	2028	WCDOT GM
CH48	Monee Rd & Tamarack St	Park Forest	7	9	1		$ -	2023	Local
CH48	Monee Rd & Tamarack St	Park Forest	2		1		$ -	2023	Local
CH48	Monee Rd & Tampa St	Park Forest	6	6	1		$ -	2028	WCDOT GM
CH48	Monee Rd & Indianwood Blvd	Park Forest	1	2	1		$ -	2028	WCDOT GM
CH48	Monee Rd & Indianwood Blvd	Park Forest	1		1		$ -	2028	WCDOT GM
CH48	Monee Rd & Niagara St	Park Forest	11	15	1		$ -	2028	WCDOT GM
CH48	Monee Rd & Niagara St	Park Forest	4		1		$ -	2028	WCDOT GM
CH48	Monee Rd & S Orchard Dr	Park Forest	1	12	1		$ -	2023	Local
CH48	Monee Rd & S Orchard Dr	Park Forest	11		1		$ -	2023	Local
CH48	Monee Rd & Monee Ct	Park Forest	4	11	1		$ -	2028	WCDOT GM
CH48	Monee Rd & Monee Ct	Park Forest	7		1		$ -	2028	WCDOT GM
CH48	Monee Rd & Blackhawk Dr	Park Forest	4	10	1		$ -	2028	WCDOT GM
CH48	Monee Rd & Blackhawk Dr	Park Forest	6		1		$ -	2028	WCDOT GM
CH48	Monee Rd & Driveway	Park Forest	4	4	1		$ -	2028	WCDOT GM

* Project timelines are estimates only and may change due to change in project schedules.

** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH25	W Wilmington-Peotone Rd & Division St	Peotone	6	15	1		$ -	2028	5 Year Plan
CH25	W Wilmington-Peotone Rd & Division St	Peotone	9		1		$ -	2028	5 Year Plan
CH25	W Wilmington-Peotone Rd & S Rathje Rd	Peotone	3	14	1		$ -	2028	5 Year Plan
CH25	W Wilmington-Peotone Rd & S Rathje Rd	Peotone	1		1		$ -	2028	5 Year Plan
CH25	W Wilmington-Peotone Rd & S Rathje Rd	Peotone	7		1		$ -	2028	5 Year Plan
CH25	W Wilmington-Peotone Rd & S Rathje Rd	Peotone	3		1		$ -	2028	5 Year Plan
CH25	W Wilmington-Peotone Rd & S Gullview Dr	Peotone		4	1		$ -	2028	Local
CH25	W Wilmington-Peotone Rd & S Gullview Dr	Peotone	4		1		$ -	2028	Local
CH25	W Wilmington-Peotone Rd & Driveway	Peotone		1	1		$ -	2028	Local
CH25	W Wilmington-Peotone Rd & Driveway	Peotone	1		1		$ -	2028	Local
CH25	W Wilmington-Peotone Rd & Driveway	Peotone	1	1	1		$ -	2028	Local
CH25	W Wilmington-Peotone Rd & Driveway	Peotone			1		$ -	2028	Local
CH25	W Wilmington-Peotone Rd & Driveway	Peotone	2	2	1		$ -	2028	Local
CH25	W Wilmington-Peotone Rd & Driveway	Peotone			1		$ -	2028	Local
CH25	W Wilmington-Peotone Rd & Meadow Ln	Peotone	6	16	2		$ -	2028	Local
CH25	W Wilmington-Peotone Rd & Meadow Ln	Peotone	5		2		$ -	2028	Local
CH25	W Wilmington-Peotone Rd & Meadow Ln	Peotone	3		1		$ -	2028	Local
CH25	W Wilmington-	Peotone	2		1		$ -	2028	Local

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
	Peotone Rd & Meadow Ln								

* Project timelines are estimates only and may change due to change in project schedules.
** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH14	S Naperville Rd & Driveway	Plainfield	7	11	1		$ -	2023	WCDOT GM
CH14	S Naperville Rd & Driveway	Plainfield	4		1		$ -	2023	WCDOT GM
CH36	E Renwick Rd & Waterfront Cir	Plainfield	10	20	1		$ -	2028	WCDOT GM
CH36	E Renwick Rd & Waterfront Cir	Plainfield	10		1		$ -	2028	WCDOT GM
CH36	E Renwick Rd & Driveway	Plainfield	1	2	1		$ -	2028	WCDOT GM
CH36	E Renwick Rd & Driveway	Plainfield	1		2		$ -	2028	WCDOT GM
CH36	E Renwick Rd & Driveway	Plainfield	1	2	1		$ -	2028	WCDOT GM
CH36	E Renwick Rd & Driveway	Plainfield	1		2		$ -	2028	WCDOT GM

* Project timelines are estimates only and may change due to change in project schedules.

** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH36	W Renwick Rd & Driveway	Romeoville	4	8	1		$ -	2028	WCDOT GM
CH36	W Renwick Rd & Driveway	Romeoville	4		1		$ -	2028	WCDOT GM
CH36	W Renwick Rd & Driveway	Romeoville	5	12	1		$ -	2028	WCDOT GM
CH36	W Renwick Rd & Driveway	Romeoville	7		1		$ -	2028	WCDOT GM
CH36	W Renwick Rd & Zachary Dr	Romeoville	3	8	1		$ -	2028	WCDOT GM
CH36	W Renwick Rd & Zachary Dr	Romeoville	5		1		$ -	2028	WCDOT GM
CH88	S Weber Rd & Driveway	Romeoville	6	25	2		$ -	2024	5 Year Plan
CH88	S Weber Rd & Driveway	Romeoville	5		2		$ -	2024	5 Year Plan
CH88	S Weber Rd & Driveway	Romeoville	7		2		$ -	2024	5 Year Plan
CH88	S Weber Rd & Driveway	Romeoville	7		2		$ -	2024	5 Year Plan
CH88	S Weber Rd & W Highpoint Dr	Romeoville	7	7	2		$ -	2024	5 Year Plan
CH88	S Weber Rd & Driveway	Romeoville	6	9	2		$ -	2024	5 Year Plan
CH88	S Weber Rd & Driveway	Romeoville	3		2		$ -	2024	5 Year Plan
CH88	S Weber Rd & Creekside Dr	Romeoville	6	13	2		$ -	2024	5 Year Plan
CH88	S Weber Rd & Creekside Dr	Romeoville	7		2		$ -	2024	5 Year Plan
CH88	S Weber Rd & Driveway	Romeoville	4	4	2		$ -	2024	5 Year Plan
CH88	S Weber Rd & Driveway	Romeoville	6	11	2		$ -	2024	5 Year Plan
CH88	S Weber Rd & Driveway	Romeoville	5		2		$ -	2024	5 Year Plan
CH88	S Weber Rd & Driveway	Romeoville	5	6	2		$ -	2029	WCDOT GM
CH88	S Weber Rd & Driveway	Romeoville			2		$ -	2029	WCDOT GM
CH88	S Weber Rd & Driveway	Romeoville	1	6	2		$ -	2029	WCDOT GM
CH88	S Weber Rd & Driveway	Romeoville	4		2		$ -	2029	WCDOT GM
CH88	S Weber Rd & Driveway	Romeoville			2		$ -	2029	WCDOT GM
CH88	S Weber Rd & Driveway	Romeoville	1		2		$ -	2029	WCDOT GM
CH88	S Weber Rd & Driveway	Romeoville			2		$ -	2029	WCDOT GM
CH88	S Weber Rd & Driveway	Romeoville			2		$ -	2029	WCDOT GM
CH88	S Weber Rd & Driveway	Romeoville	1	1	2		$ -	2029	WCDOT GM
CH88	S Weber Rd & W Grand Haven Cir	Romeoville	1	5	2		$ -	2029	WCDOT GM
CH88	S Weber Rd & W Grand Haven Cir	Romeoville	4		2		$ -	2029	WCDOT GM
CH88	S Weber Rd & Driveway	Romeoville	2	3	2		$ -	2029	WCDOT GM

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH88	S Weber Rd & Driveway	Romeoville	1		2		$ -	2029	WCDOT GM
CH88	N Weber Rd & W 135th St	Romeoville			2		$ -		
CH88	N Weber Rd & W 135th St	Romeoville			2		$ -		
CH88	N Weber Rd & W 135th St	Romeoville			2		$ -		
CH88	N Weber Rd & W 135th St	Romeoville			2		$ -		
CH88	N Weber Rd & W 135th St	Romeoville			2		$ -		
CH88	N Weber Rd & W 135th St	Romeoville			2		$ -		
CH88	N Weber Rd & W 135th St	Romeoville			2		$ -		
CH88	N Weber Rd & Driveway	Romeoville			2		$ -		
CH88	N Weber Rd & Driveway	Romeoville			2		$ -		
CH88	N Weber Rd & Driveway	Romeoville			2		$ -		
CH88	N Weber Rd & Driveway	Romeoville			2		$ -		
CH88	N Weber Rd & Driveway	Romeoville			2		$ -		
CH88	N Weber Rd & Driveway	Romeoville			2		$ -		

* Project timelines are estimates only and may change due to change in project schedules.
** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH73	S Symerton St & W South St	Symerton	6	12	1		$ -	2028	WCDOT GM
CH73	S Symerton St & W South St	Symerton	6		1		$ -	2028	WCDOT GM
CH73	S Symerton Rd & Driveway	Symerton	1	2	1		$ -	2028	WCDOT GM
CH73	S Symerton Rd & Driveway	Symerton	1		1		$ -	2028	WCDOT GM
CH73	S Symerton Rd & W Commercial St	Symerton		2	1		$ -	2028	WCDOT GM
CH73	S Symerton Rd & W Commercial St	Symerton	2		1		$ -	2028	WCDOT GM

* Project timelines are estimates only and may change due to change in project schedules.
** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH83	80th Ave & Driveway	Tinley Park	3	12	1		$ -	2023	5 Year Plan
CH83	80th Ave & Driveway	Tinley Park	3		1		$ -	2023	5 Year Plan
CH83	80th Ave & Driveway	Tinley Park	3		1		$ -	2023	5 Year Plan
CH83	80th Ave & Driveway	Tinley Park	3		1		$ -	2023	5 Year Plan
CH83	80th Ave & Driveway	Tinley Park	5	11	1		$ -	2023	5 Year Plan
CH83	80th Ave & Driveway	Tinley Park	6		1		$ -	2023	5 Year Plan
CH83	80th Ave & Driveway	Tinley Park	8	10	1		$ -	2023	5 Year Plan
CH83	80th Ave & Driveway	Tinley Park	2		1		$ -	2023	5 Year Plan
CH84	W 191st St & Driveway	Tinley Park	3	3	1		$ -	2023	5 Year Plan
CH88	W 191st St & Driveway	Tinley Park	6	11	1		$ -	2028	Local
CH88	W 191st St & Driveway	Tinley Park	5		1		$ -	2028	Local
CH84	W 191st St & Brookside Glen Dr	Tinley Park	9	18	1		$ -	2028	Local
CH84	W 191st St & Brookside Glen Dr	Tinley Park	9		1		$ -	2028	Local
CH84	W 191st St & Driveway	Tinley Park	5	5	1		$ -	2028	Local
CH84	W 191st Dr & Driveway	Tinley Park	6	6	1		$ -	2028	Local

* Project timelines are estimates only and may change due to change in project schedules.
** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH53	S Western Ave & Doral Ter	University Park	3	3	1		$ -	2023	WCDOT GM
CH53	S Western Ave & Doral Ter	University Park			1		$ -	2023	WCDOT GM
CH53	S Western Ave & Hickok Ave	University Park	3	19	1		$ -	2023	WCDOT GM
CH53	S Western Ave & Hickok Ave	University Park	4		1		$ -	2023	WCDOT GM
CH53	S Western Ave & Hickok Ave	University Park	12		1		$ -	2023	WCDOT GM
CH53	S Western Ave & Ashridge Ln	University Park	8	8	1		$ -	2023	WCDOT GM

* Project timelines are estimates only and may change due to change in project schedules.
** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH44	River Rd & S IL 53	Wilmington	2	2	1		$	2030	WCDOT GM
CH25	W Peotone Rd & Ski Nautique Dr	Wilmington	5	11	1		$	2030	WCDOT GM
CH25	W Peotone Rd & Ski Nautique Dr	Wilmington	7		1		$	2030	WCDOT GM

* Project timelines are estimates only and may change due to change in project schedules.
** MEP=Maximum Extents Practicable

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH43	S Cedar Rd & W Joliet Rd	Wilton Township	8	8	1		$ -	2030	Township GM

County Highway Number	Mainline & Cross Street	Jurisdiction	Number of Ramp Violations	Overall Intersection Violations	"Use" Prioritization Category (1 Low - 4 High)	Required Barrier Remediation(s)	Estimated Cost	Estimated Year of Improvement	Program
CH51	Mills Rd & Bartel Rd	Joliet Township	1	4	1		$ -	2030	Township GM
CH51	Mills Rd & Bartel Rd	Joliet Township	1		1		$ -	2030	Township GM
CH51	Mills Rd & Bartel Rd	Joliet Township	1		1		$ -	2030	Township GM
CH51	Mills Rd & Bartel Rd	Joliet Township	1		1		$ -	2030	Township GM
CH51	Mills Rd & Karner Dr	Joliet Township	1	2	1		$ -	2030	Township GM
CH51	Mills Rd & Karner Dr	Joliet Township	1		1		$ -	2030	Township GM

* Project timelines are estimates only and may change due to change in project schedules.

** MEP=Maximum Extents Practicable

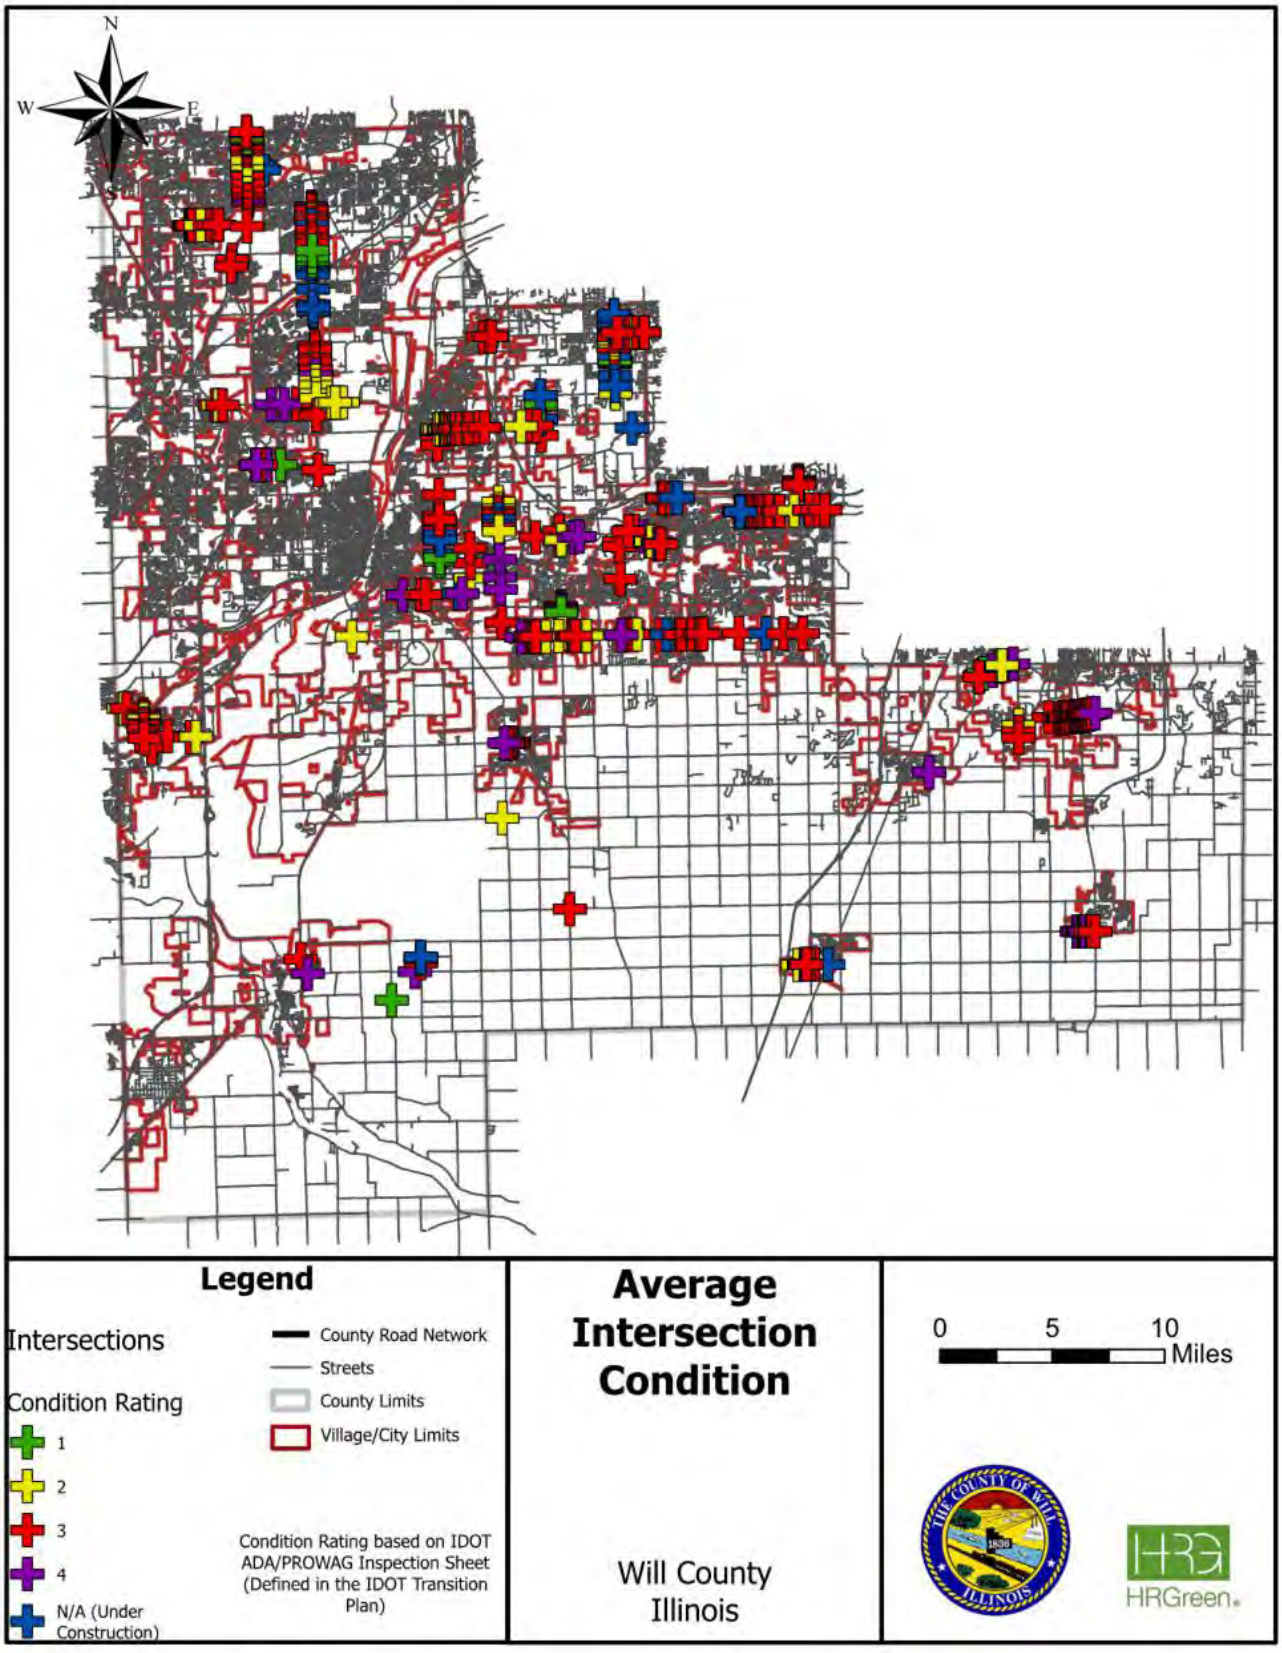
N
W
E
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
Will County Illinois
0
5
10
Miles
HRGreen.

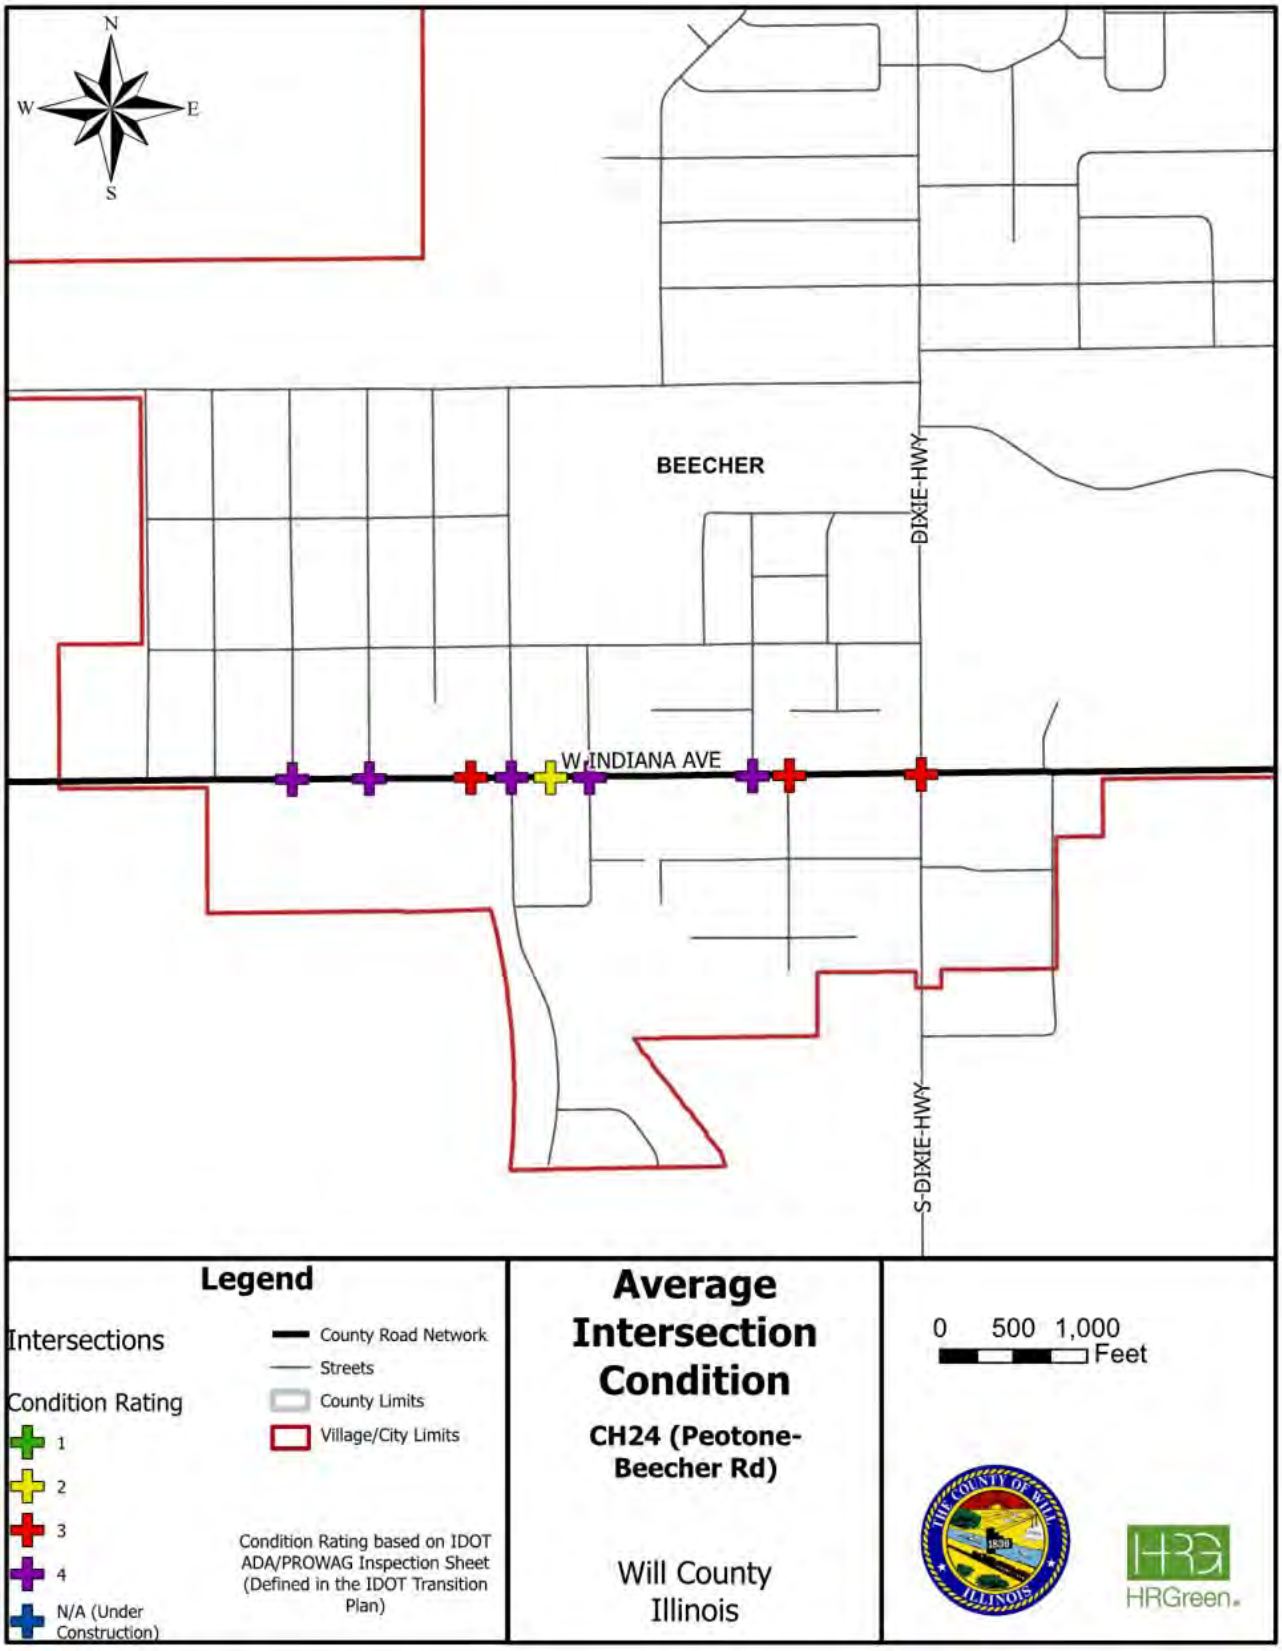
N
W
E
S
BEECHER
DIXIE HWY
W INDIANA AVE
S DIXIE HWY
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH24 (Peotone-Beecher Rd)
Will County Illinois
0 500 1,000
Feet
HRGreen

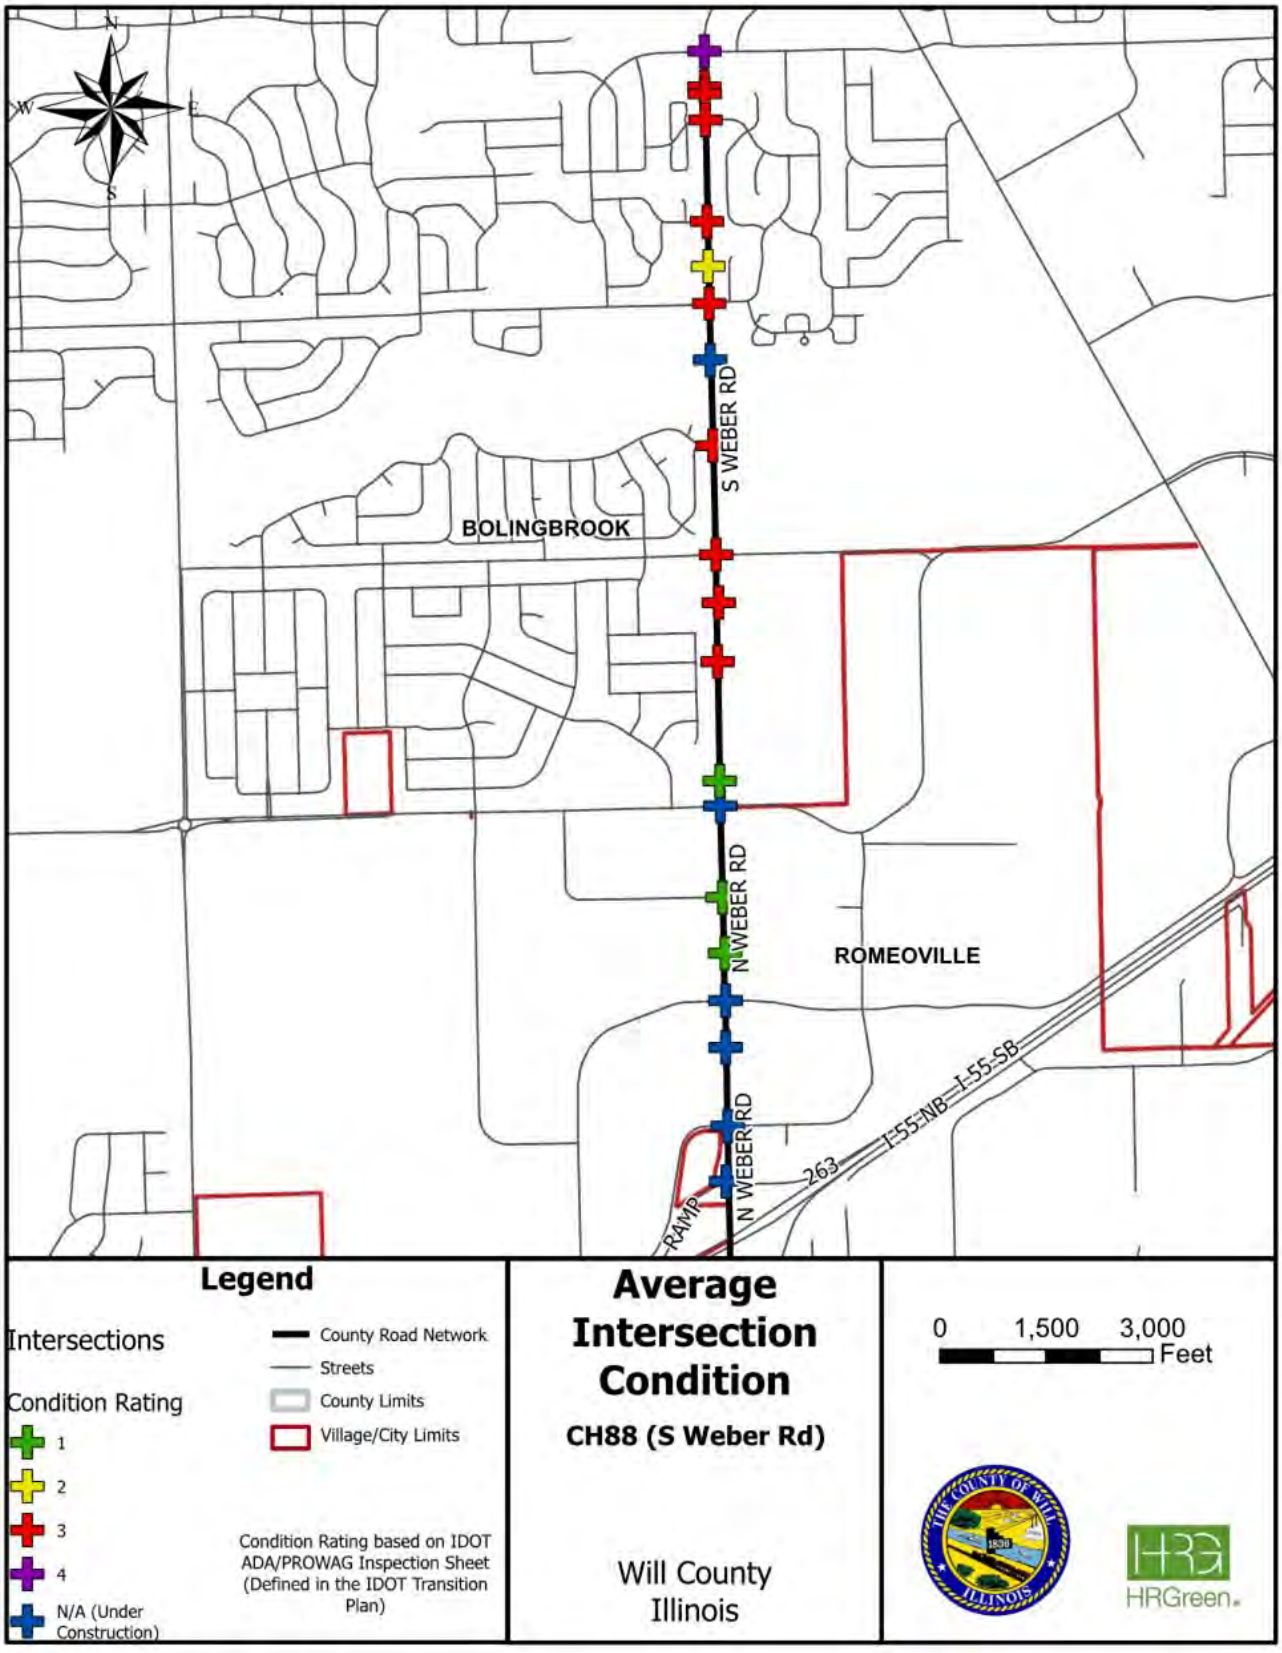
N
W
E
S
S WEBER RD
BOLINGBROOK
N WEBER RD
ROMEOVILLE
N WEBER RD
RAMP
263
I-55-NB
I-55-SB
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH88 (S Weber Rd)
Will County Illinois
0
1,500
3,000
Feet
HRGreen

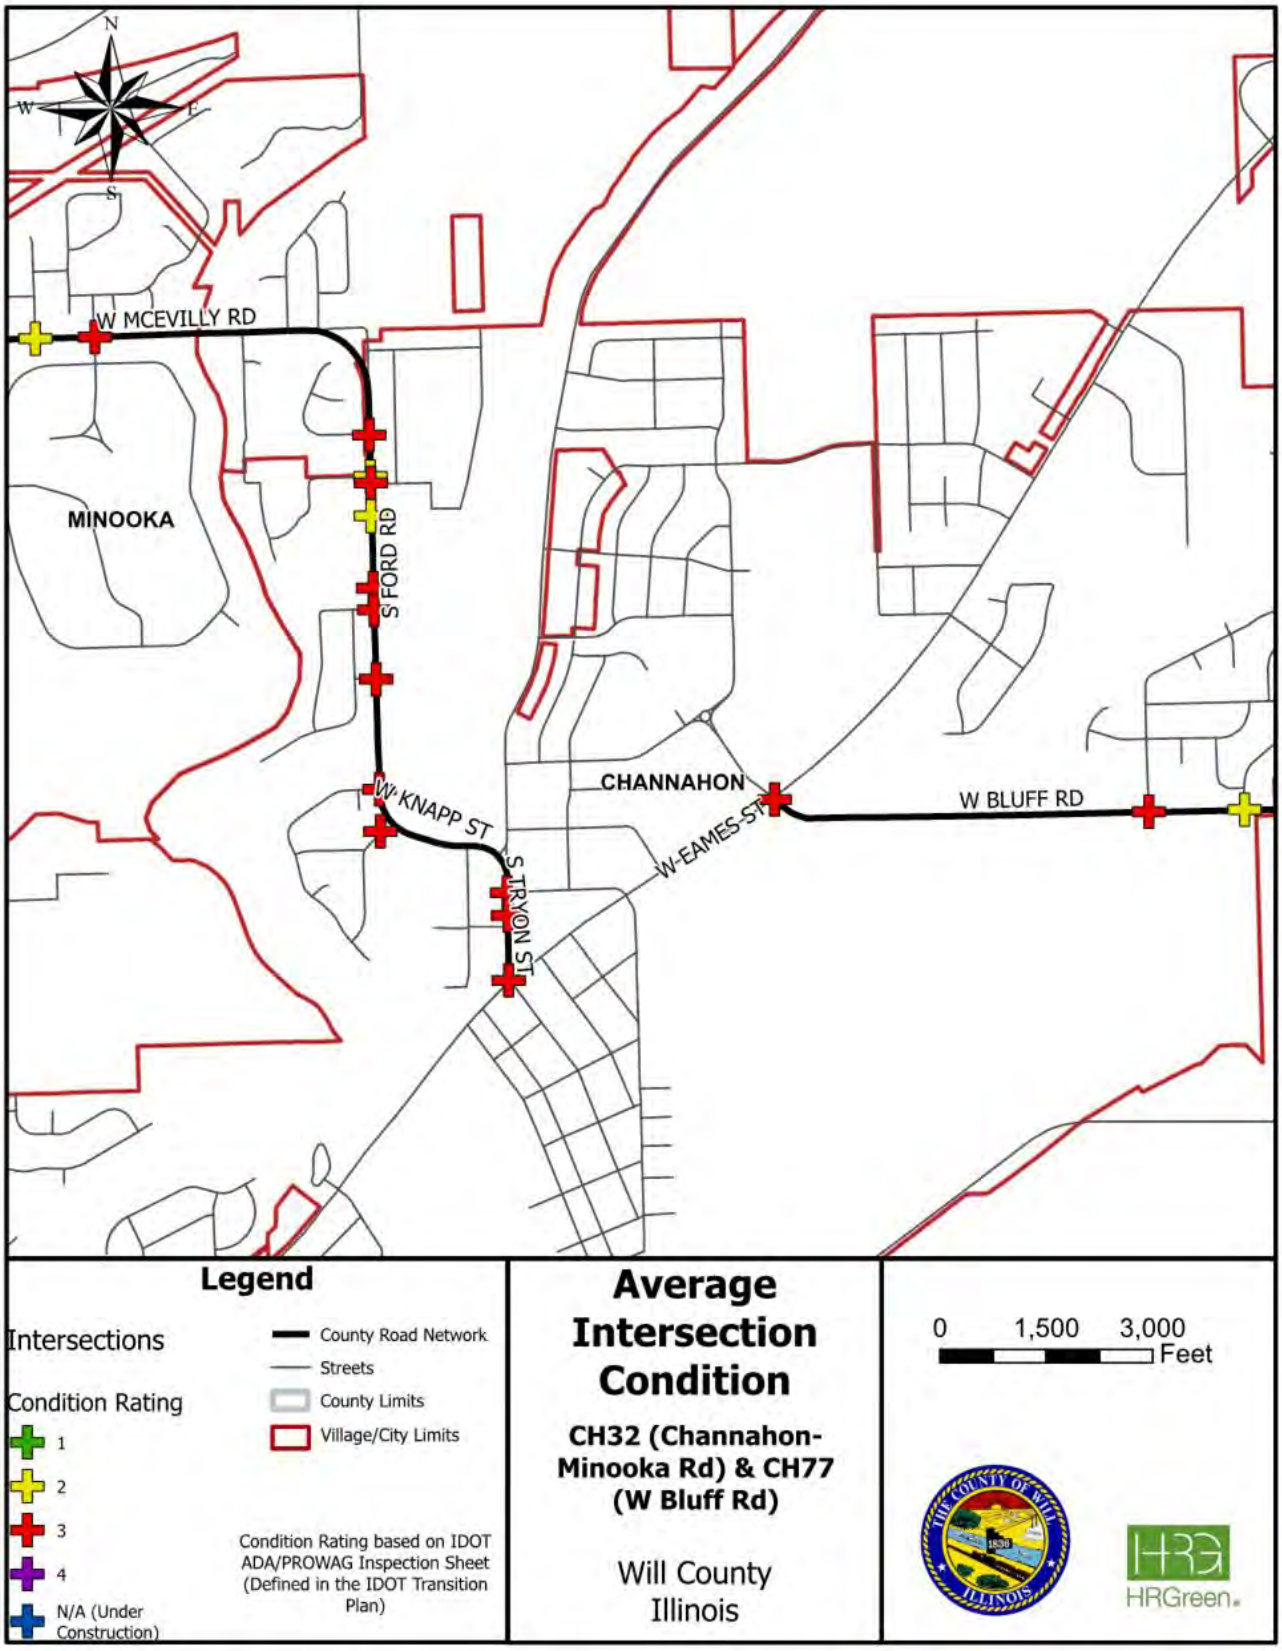
N
W
E
S
W MCEVILLY RD
MINOOKA
S FORD RD
W KNAPP ST
S TRYON ST
CHANNAHON
W EAMES ST
W BLUFF RD
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH32 (Channahon-Minooka Rd) & CH77 (W Bluff Rd)
Will County Illinois
0
1,500
3,000
Feet
HRGreen

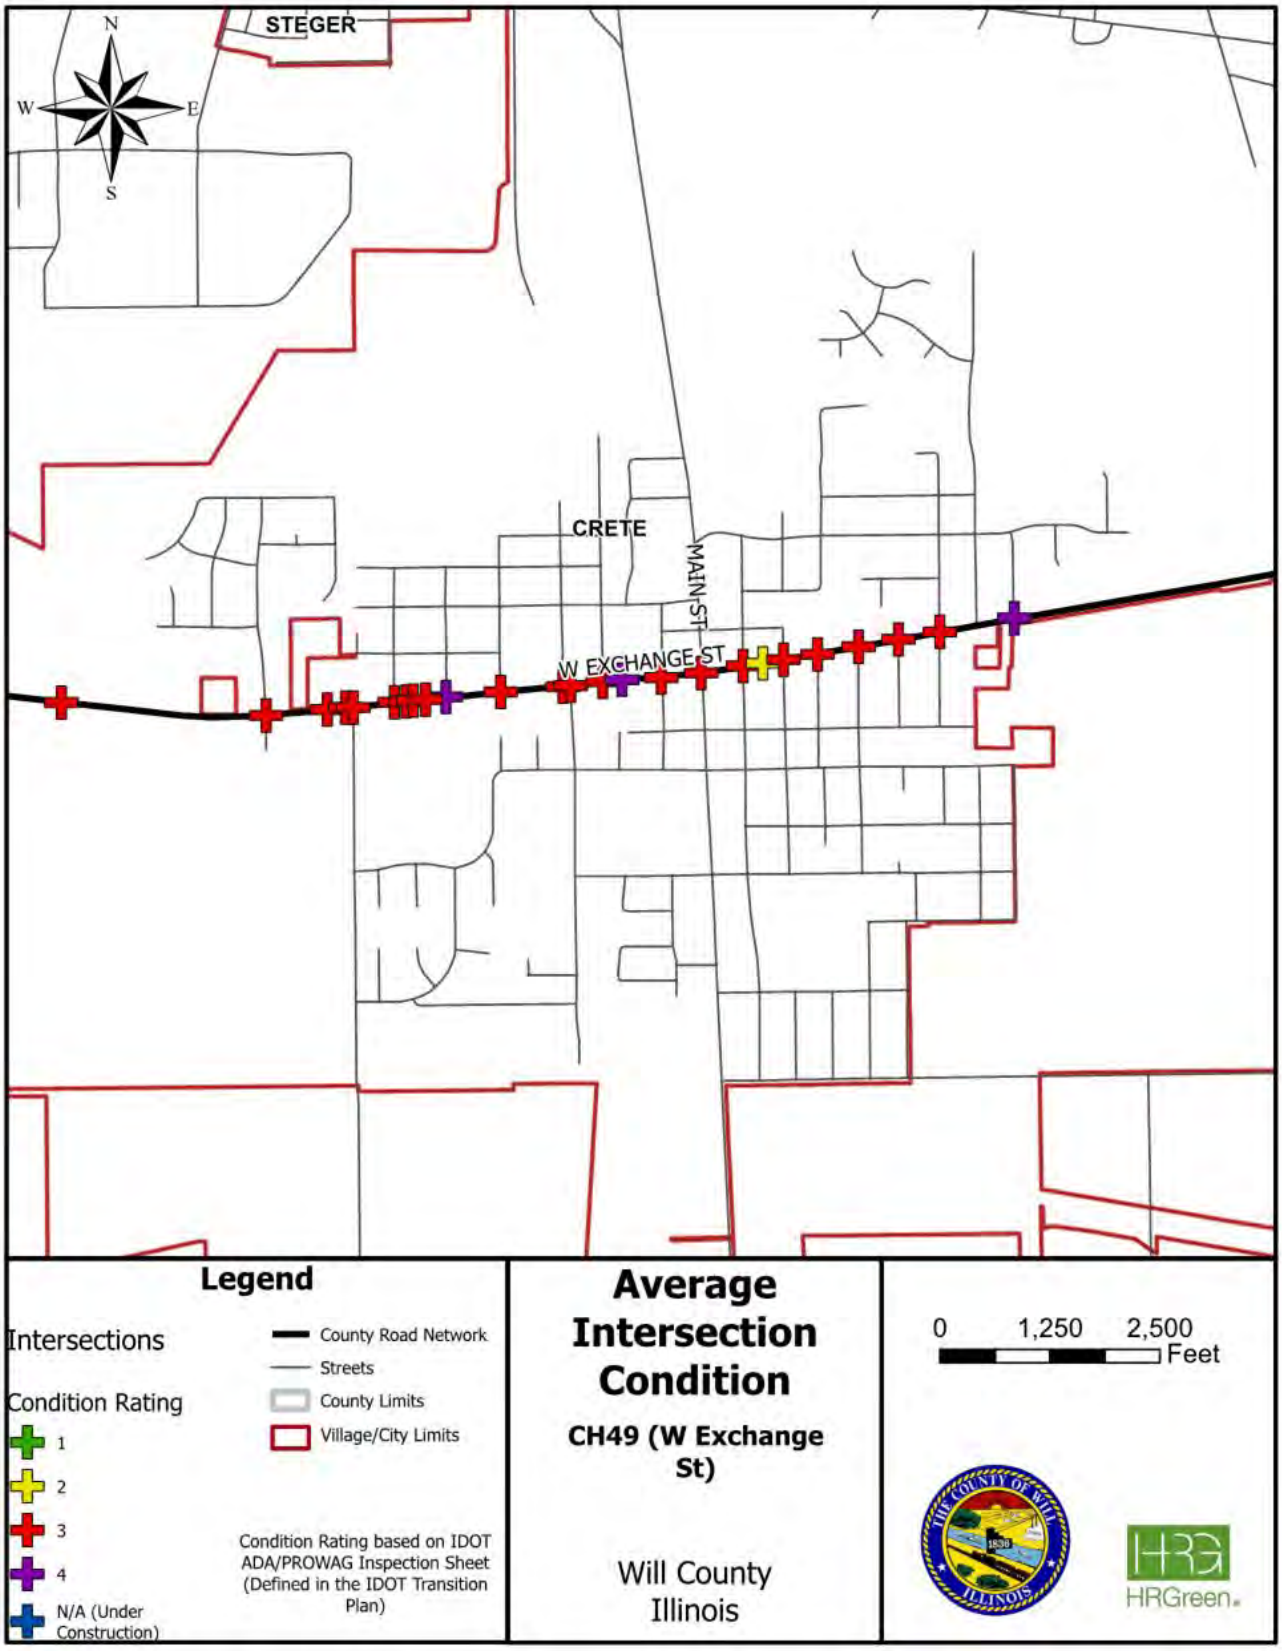
N
W
E
S
STEGER
CRETE
MAIN ST
W EXCHANGE ST
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH49 (W Exchange St)
Will County Illinois
0
1,250
2,500
Feet
HRGreen

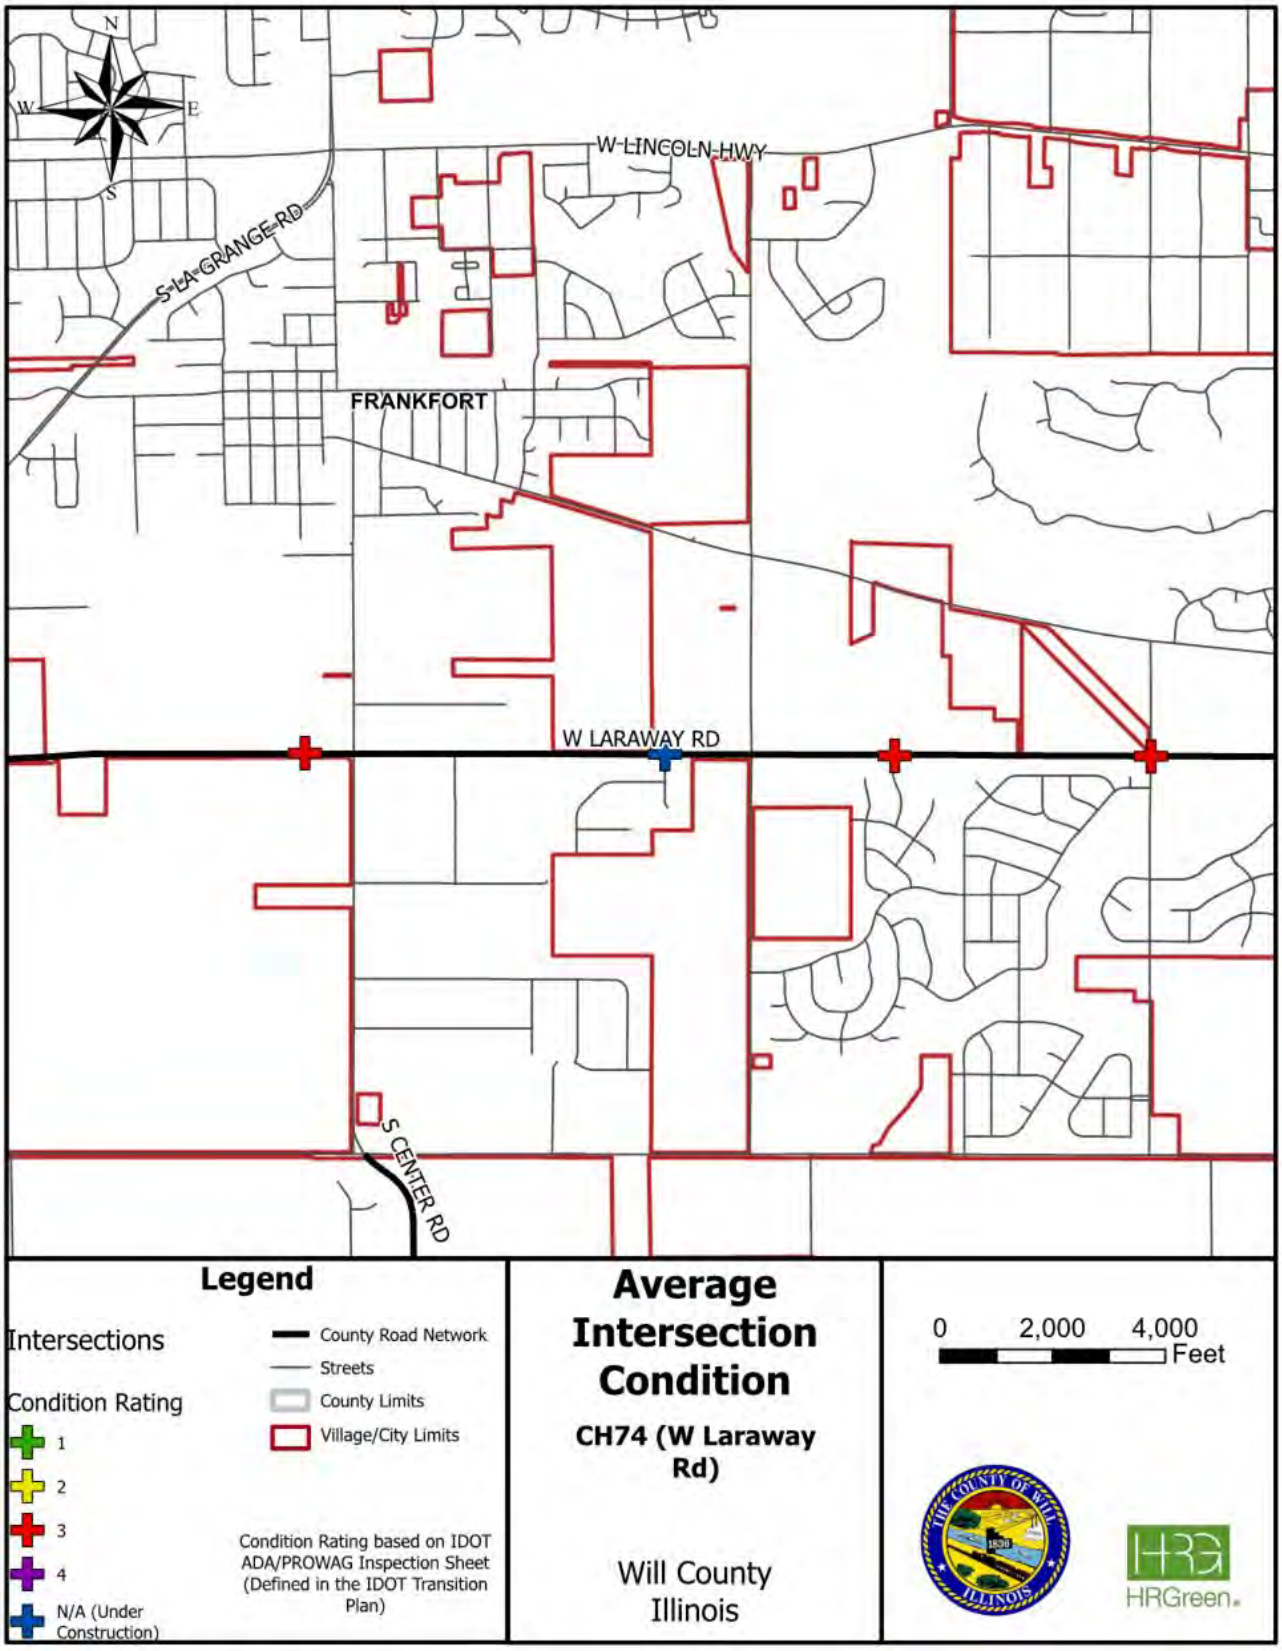
N
W
E
S
W LINCOLN HWY
S LA GRANGE RD
FRANKFORT
W LARAWAY RD
S CENTER RD
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH74 (W Laraway Rd)
Will County Illinois
0
2,000
4,000
Feet
HRGreen

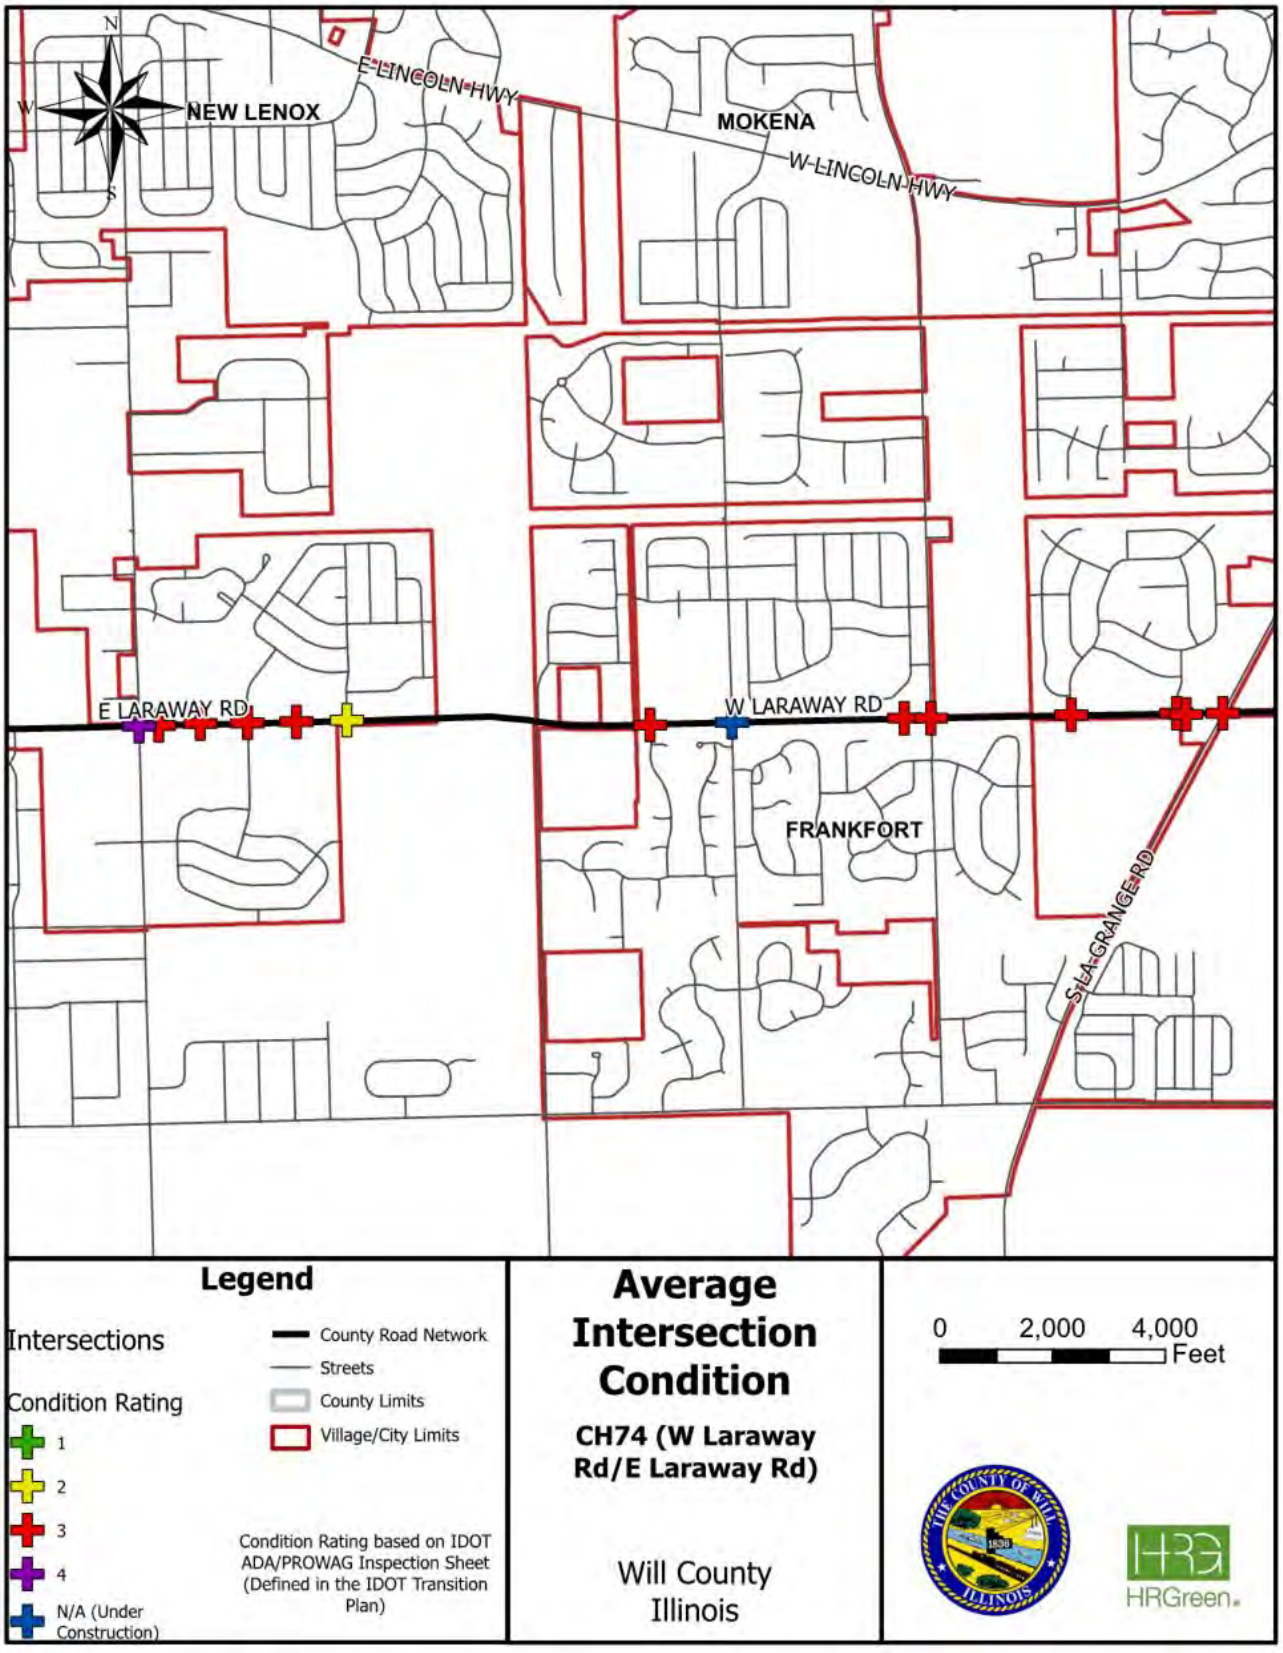
N
W
S
NEW LENOX
E LINCOLN HWY
MOKENA
W LINCOLN HWY
E LARAWAY RD
W LARAWAY RD
FRANKFORT
S LA GRANGE RD
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH74 (W Laraway Rd/E Laraway Rd)
Will County Illinois
0
2,000
4,000
Feet
HRGreen

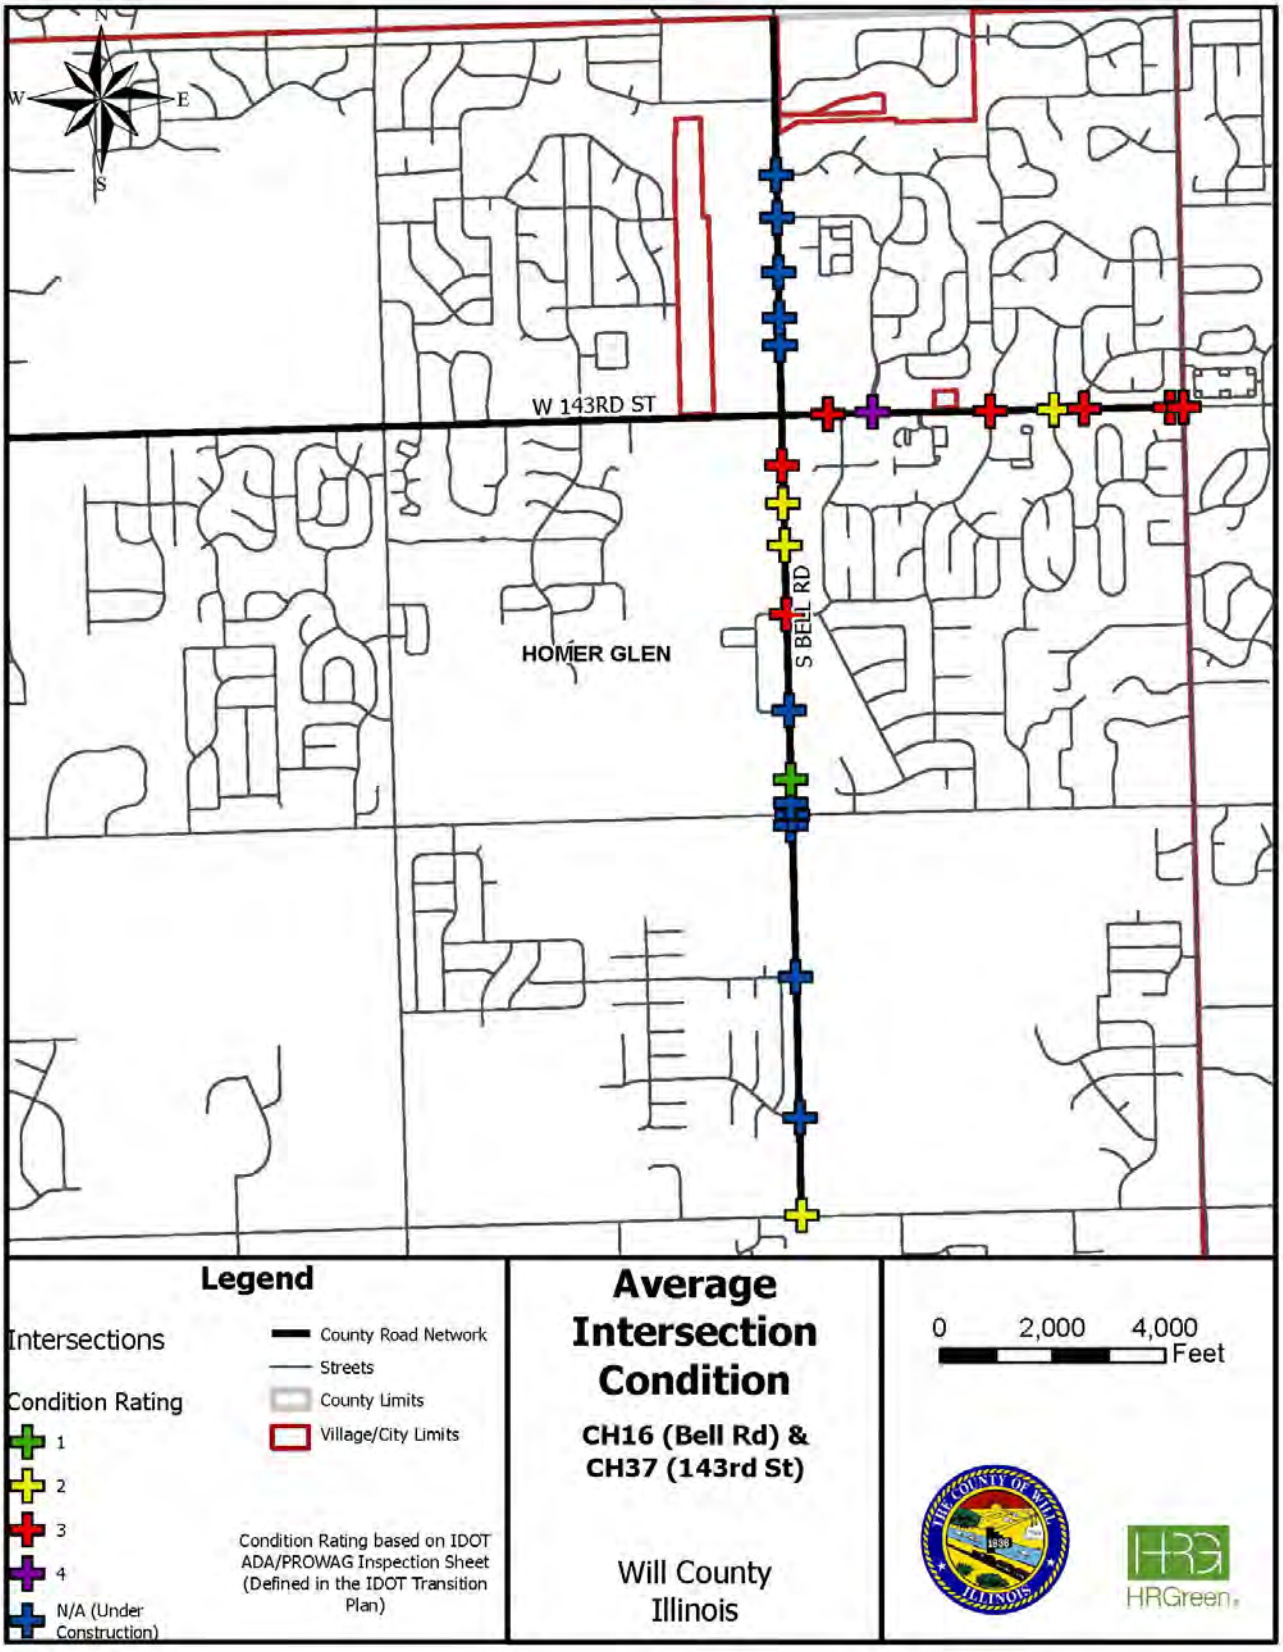
N
W
E
S
W 143RD ST
S BELL RD
HOMER GLEN
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH16 (Bell Rd) & CH37 (143rd St)
Will County Illinois
0
2,000
4,000
Feet
HRGreen

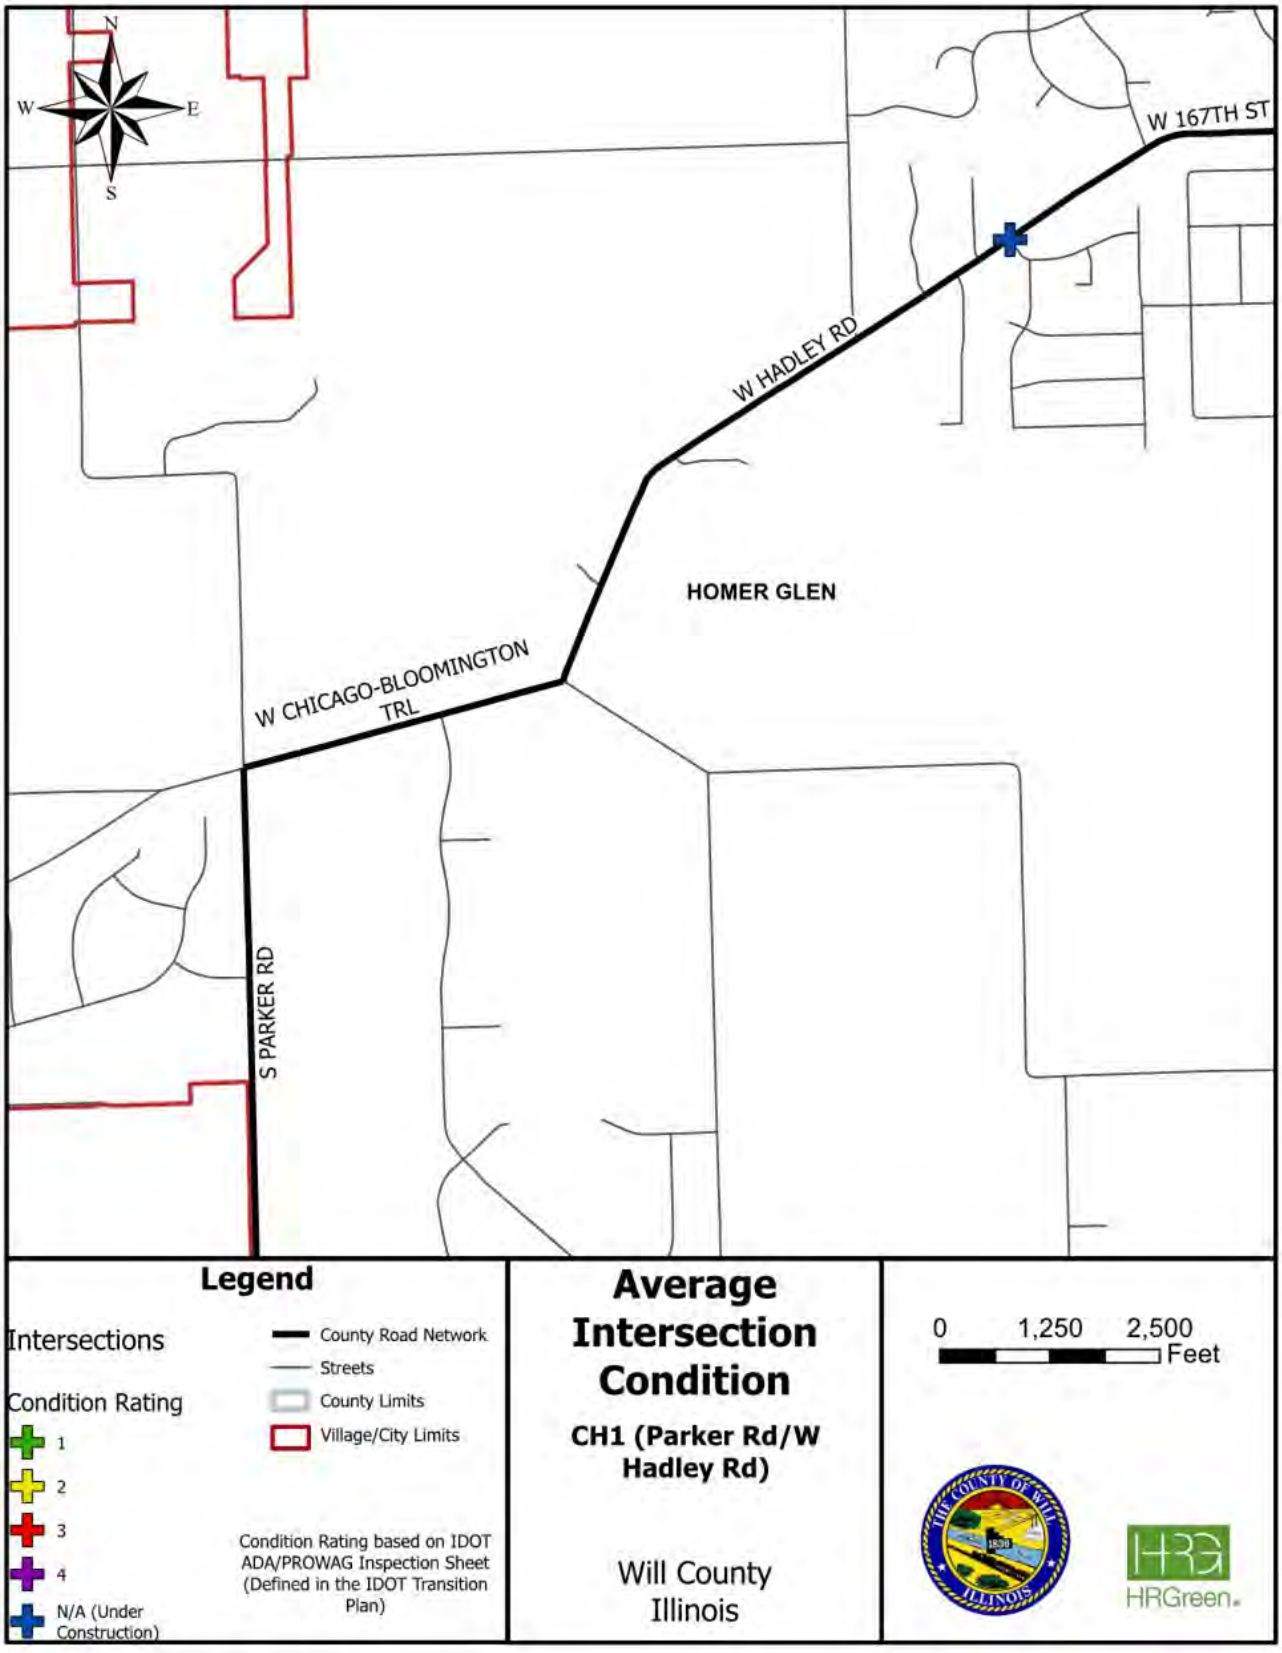
N
W
E
S
W 167TH ST
W HADLEY RD
HOMER GLEN
W CHICAGO-BLOOMINGTON TRL
S PARKER RD
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH1 (Parker Rd/W Hadley Rd)
Will County Illinois
0
1,250
2,500
Feet
HRGreen

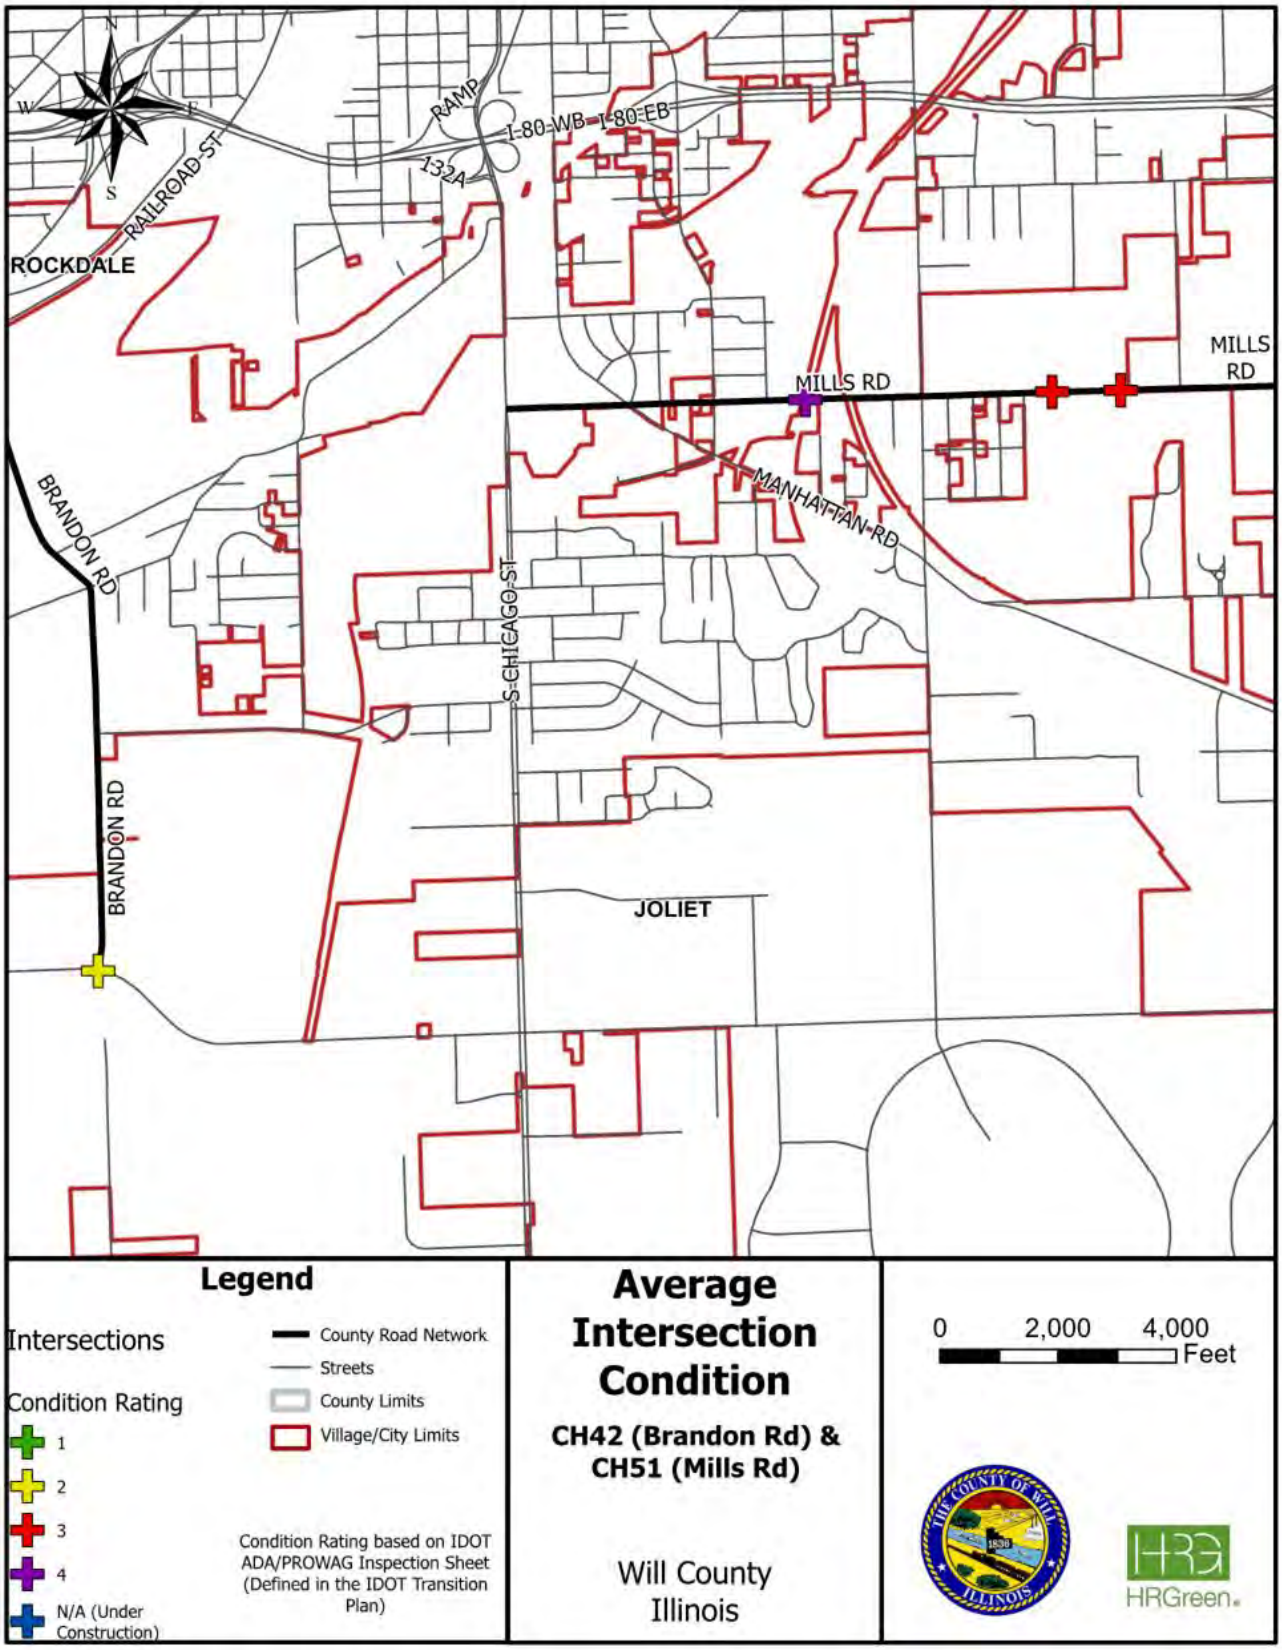
N
W
E
S
RAMP
I-80-WB
I-80-EB
132A
RAILROAD ST
ROCKDALE
MILLS RD
MILLS RD
BRANDON RD
MANHATTAN RD
S CHICAGO ST
BRANDON RD
JOLIET
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH42 (Brandon Rd) & CH51 (Mills Rd)
Will County Illinois
0
2,000
4,000
Feet
HRGreen.

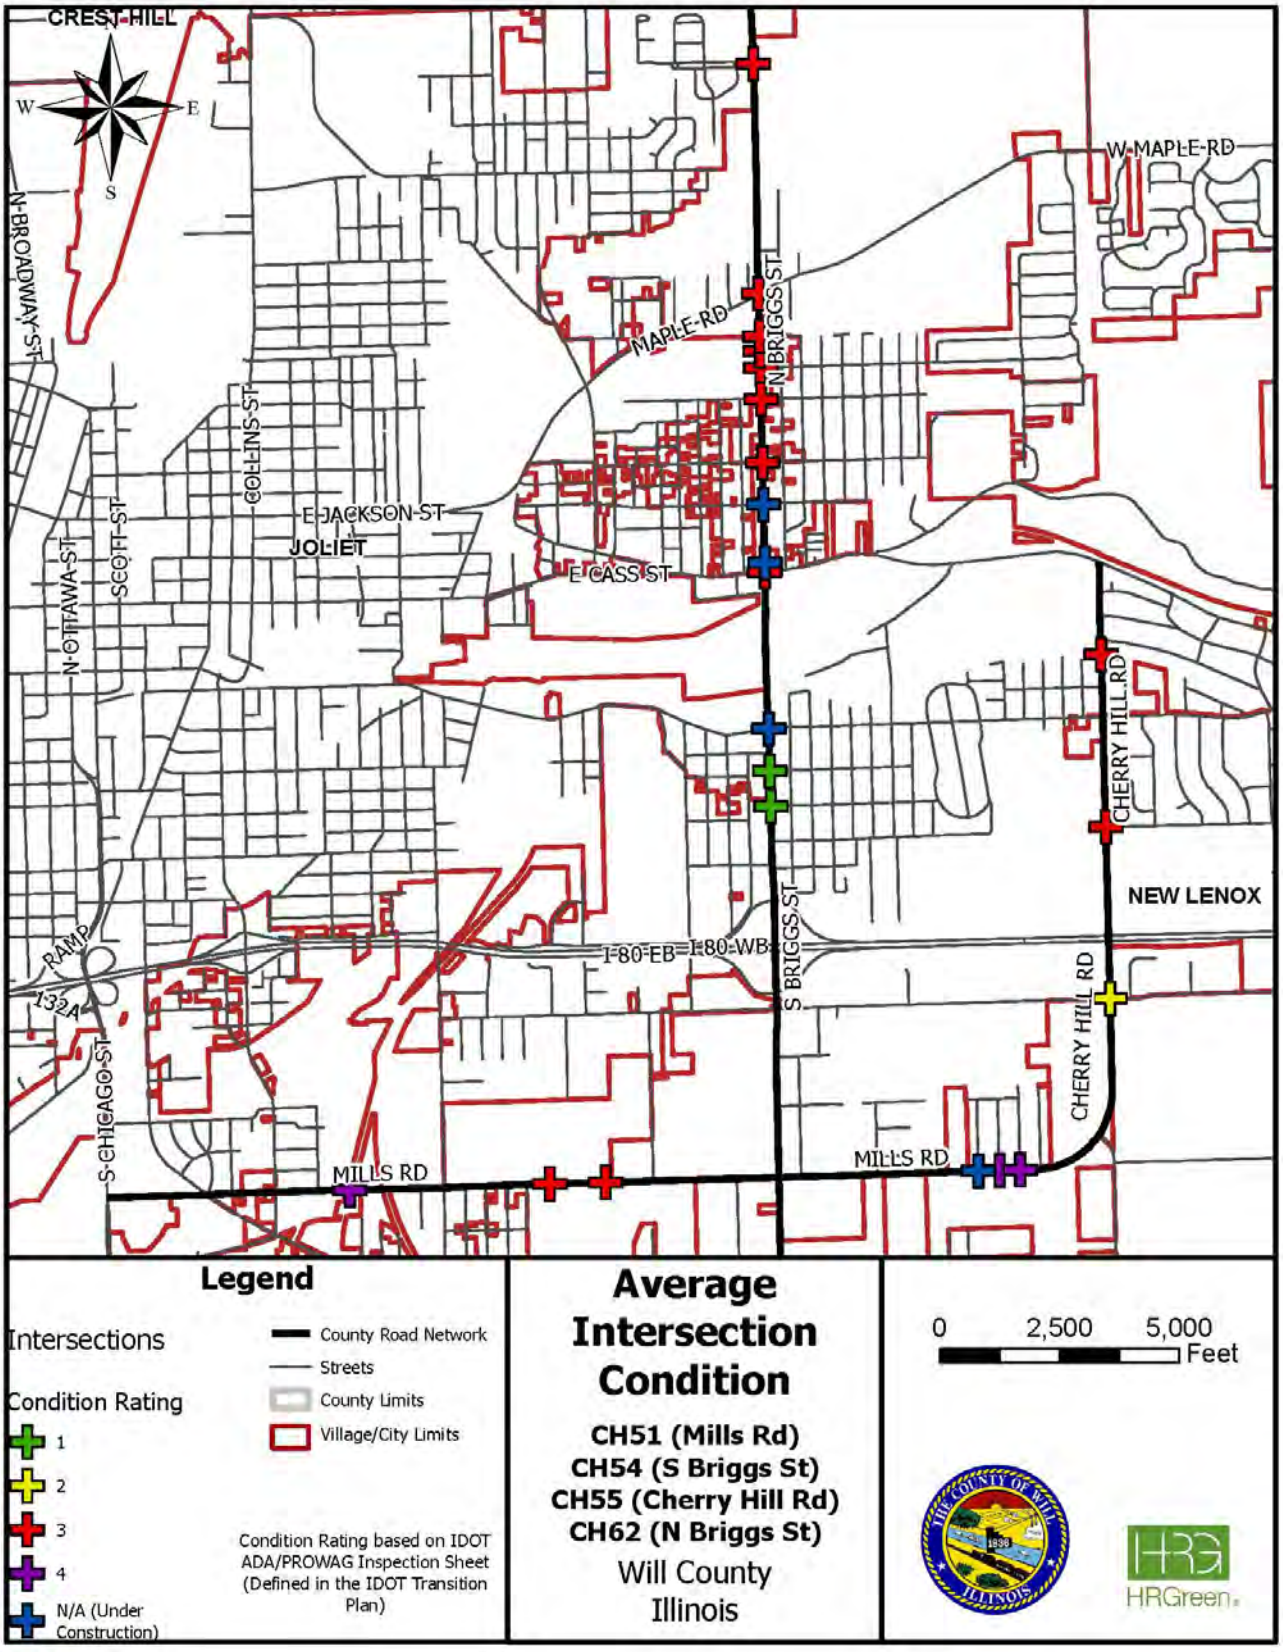
CREST HILL
W
E
S
N BROADWAY ST
COLLINS ST
SCOTT ST
N OTTAWA ST
E JACKSON ST
JOLIET
MAPLE RD
N BRIGGS ST
W MAPLE RD
E CASS ST
CHERRY HILL RD
NEW LENOX
S BRIGGS ST
I-80 EB
I-80 WB
RAMP
132A
S CHICAGO ST
MILLS RD
CHERRY HILL RD
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH51 (Mills Rd)
CH54 (S Briggs St)
CH55 (Cherry Hill Rd)
CH62 (N Briggs St)
Will County
Illinois
0
2,500
5,000
Feet
HRGreen

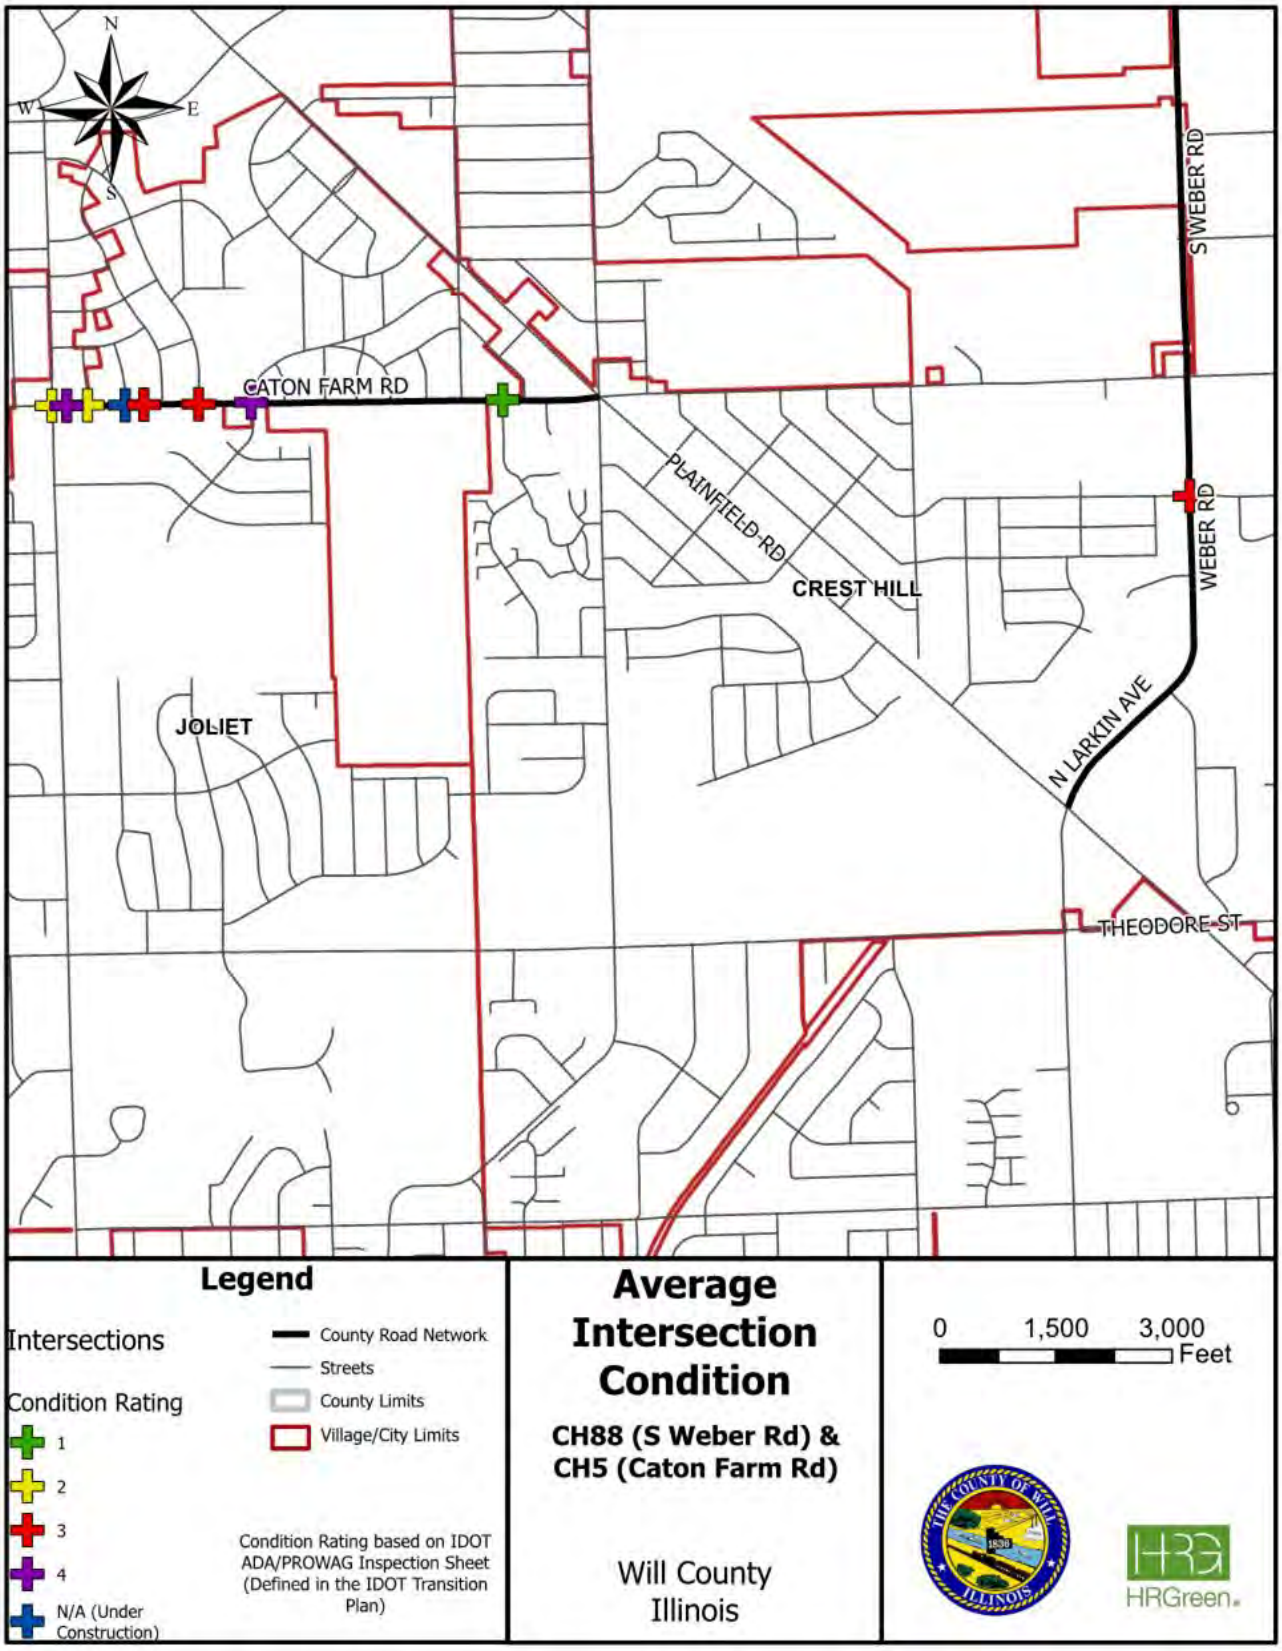
N
W
E
S
CATON FARM RD
S WEBER RD
WEBER RD
PLAINFIELD RD
CREST HILL
JOLIET
N LARKIN AVE
THEODORE ST
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH88 (S Weber Rd) & CH5 (Caton Farm Rd)
Will County Illinois
0
1,500
3,000
Feet
HRGreen

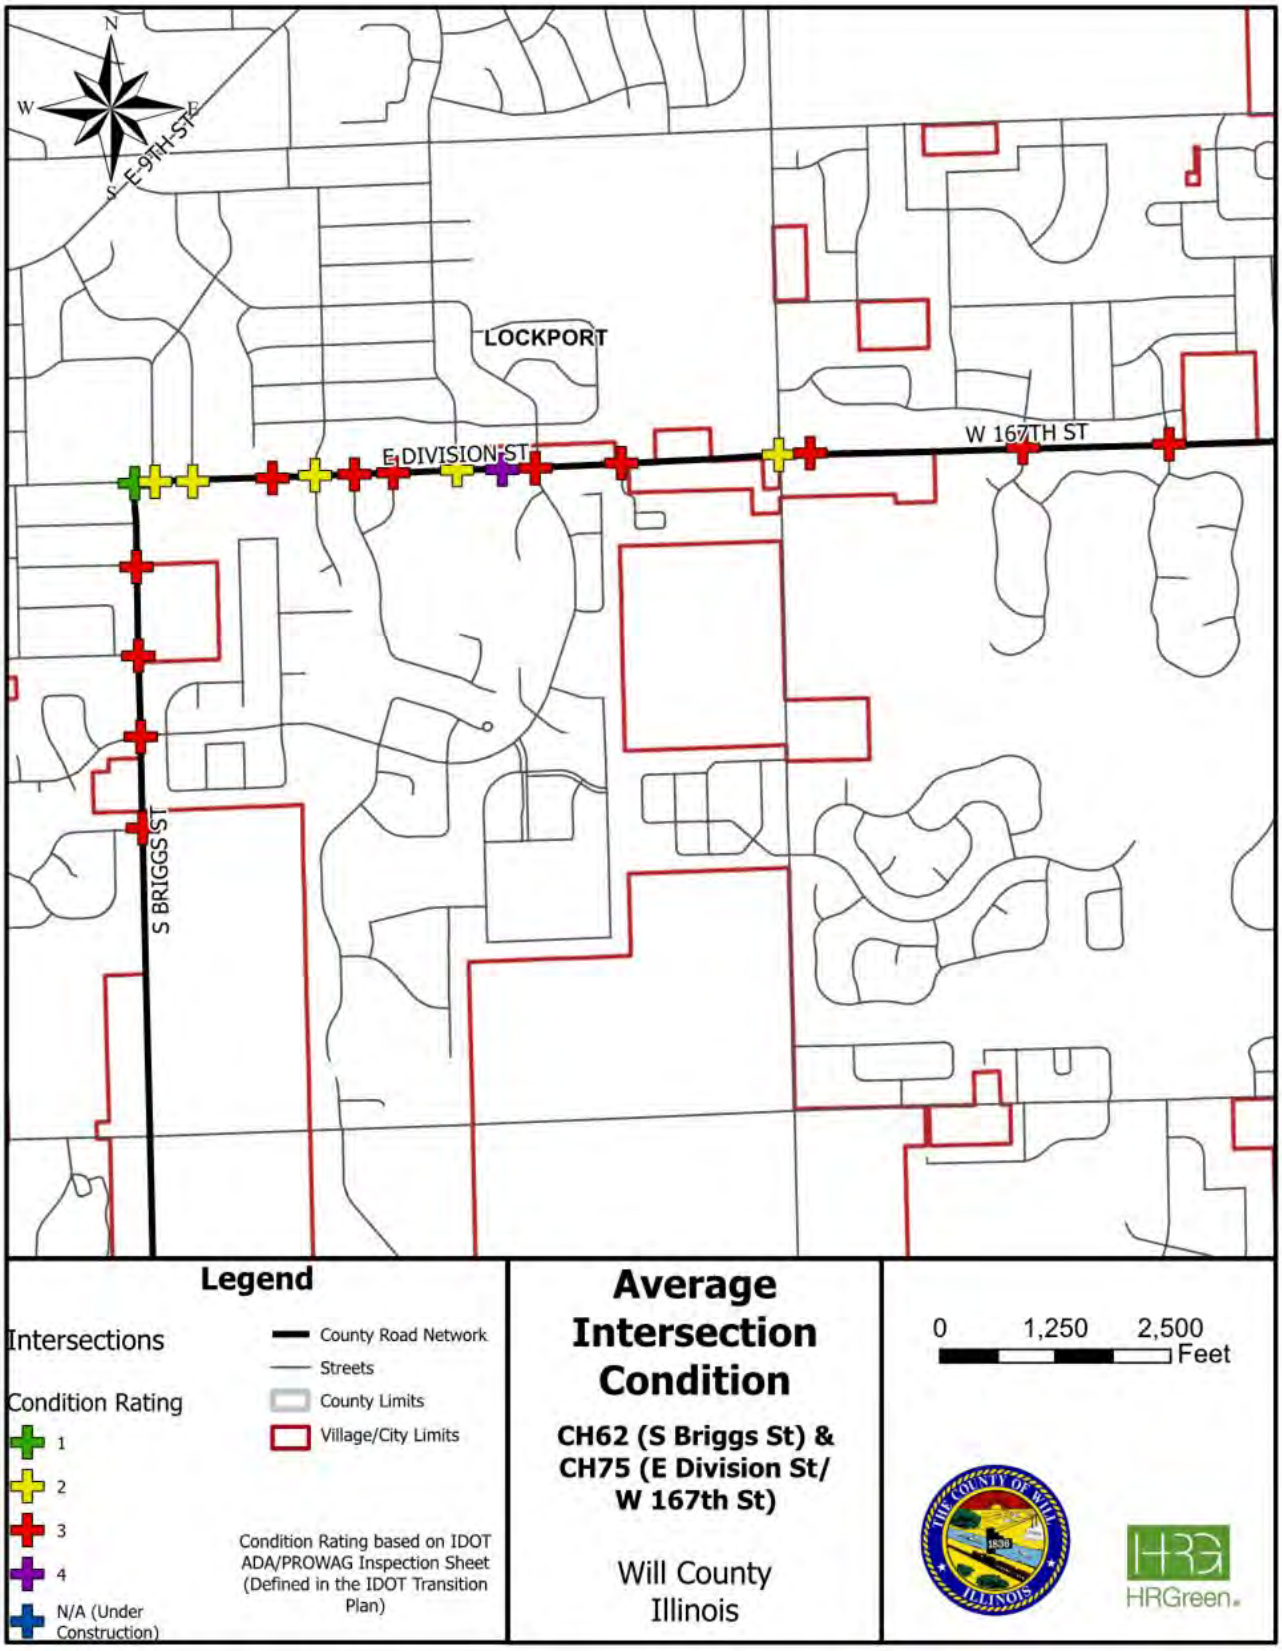
N
W
E
S
E 9TH ST
LOCKPORT
E DIVISION ST
W 167TH ST
S BRIGGS ST
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH62 (S Briggs St) & CH75 (E Division St/ W 167th St)
Will County Illinois
0
1,250
2,500
Feet
HRGreen

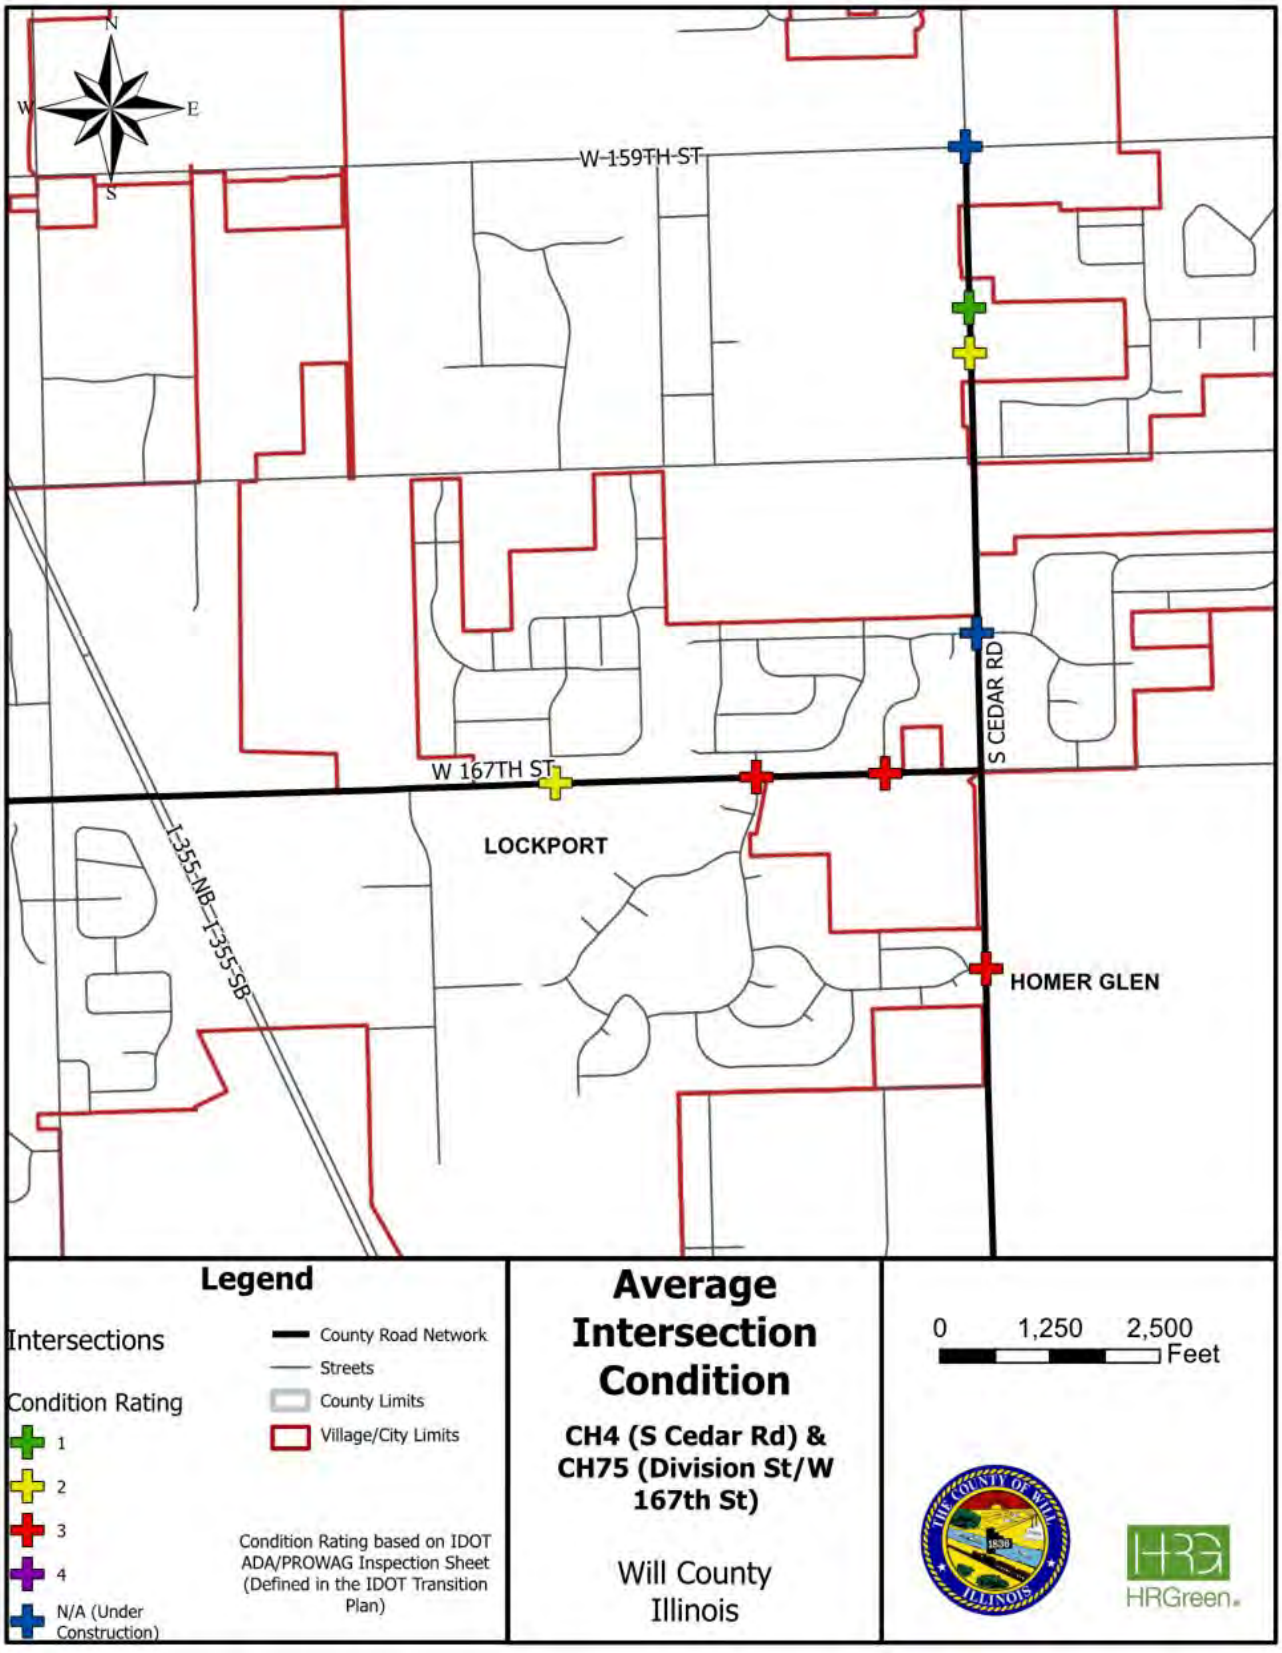
N
W
E
S
W-159TH-ST
W 167TH ST
S CEDAR RD
I-355-NB-I-355-SB
LOCKPORT
HOMER GLEN
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH4 (S Cedar Rd) & CH75 (Division St/W 167th St)
Will County Illinois
0
1,250
2,500
Feet
HRGreen

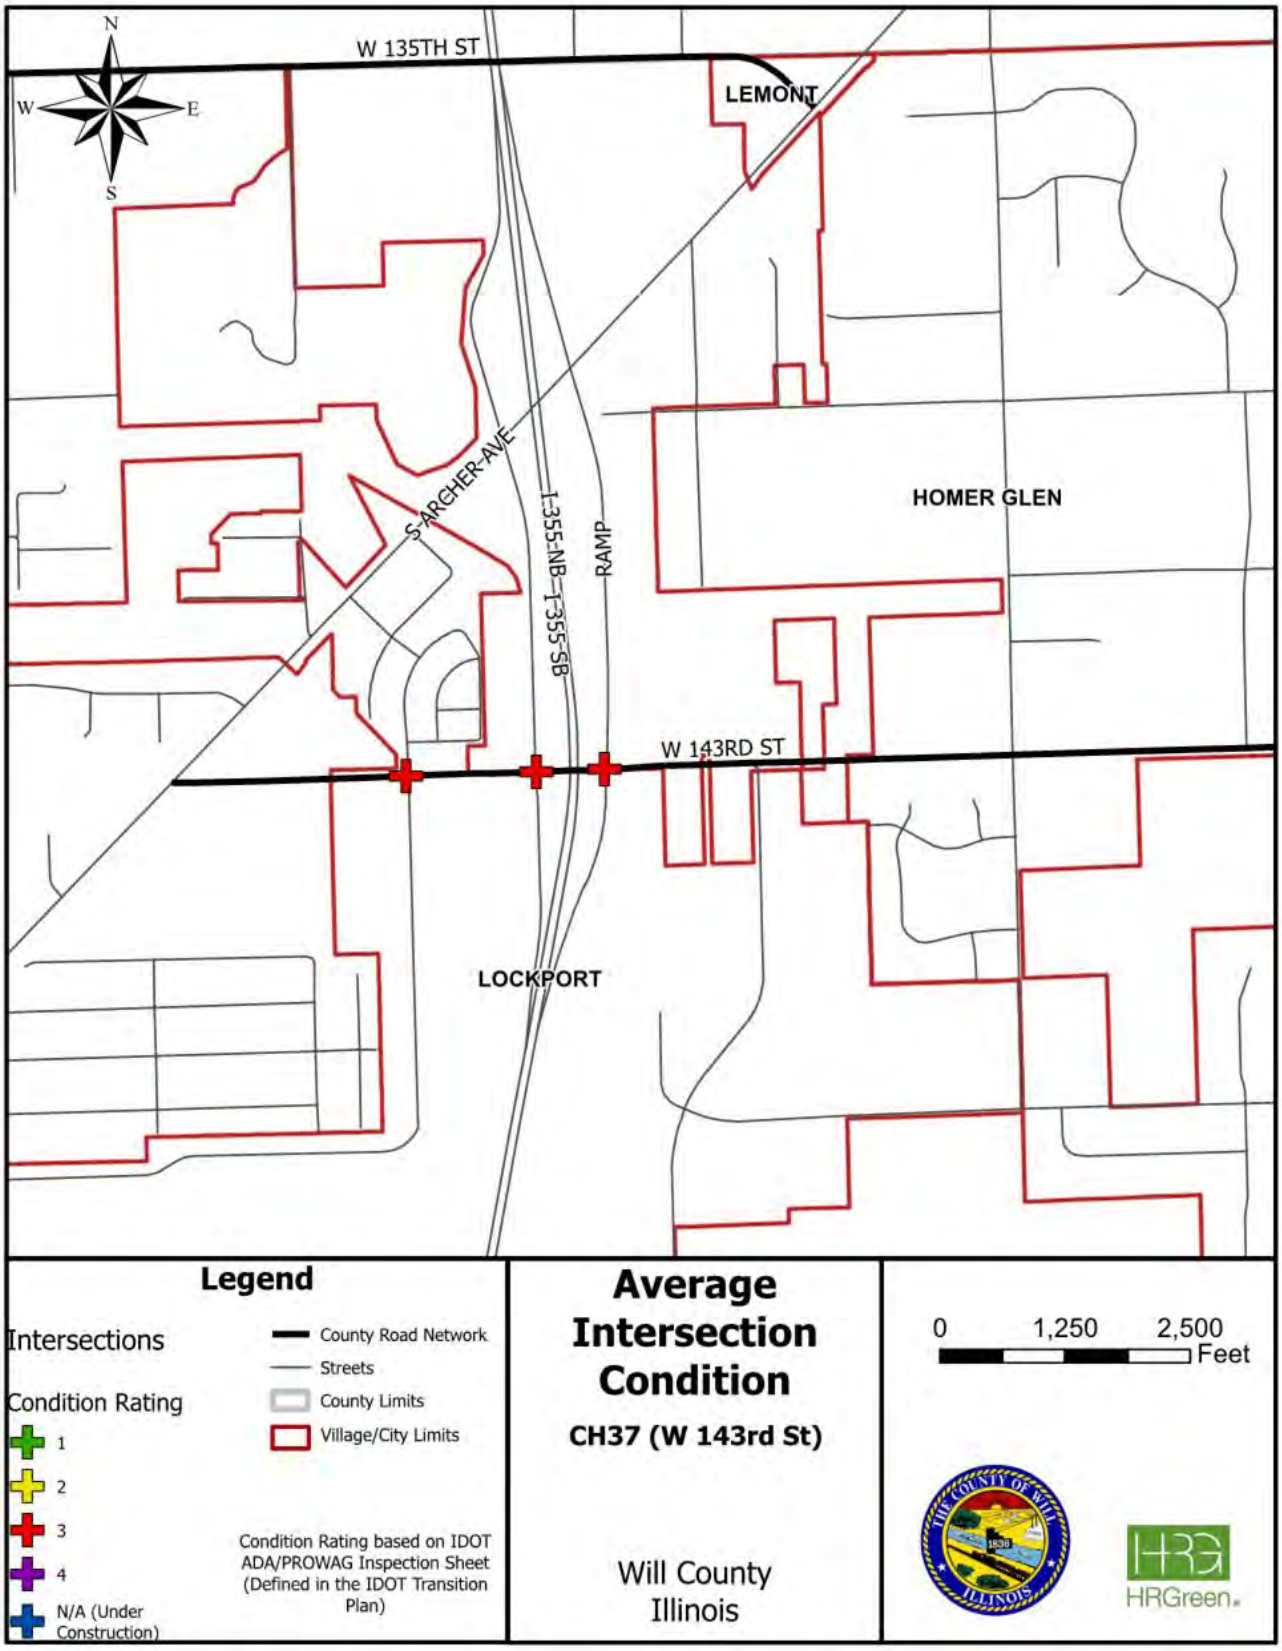
N
W
E
S
W 135TH ST
LEMONT
S ARCHER AVE
I-355 NB
I-355 SB
RAMP
HOMER GLEN
W 143RD ST
LOCKPORT
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH37 (W 143rd St)
Will County Illinois
0
1,250
2,500
Feet
HRGreen

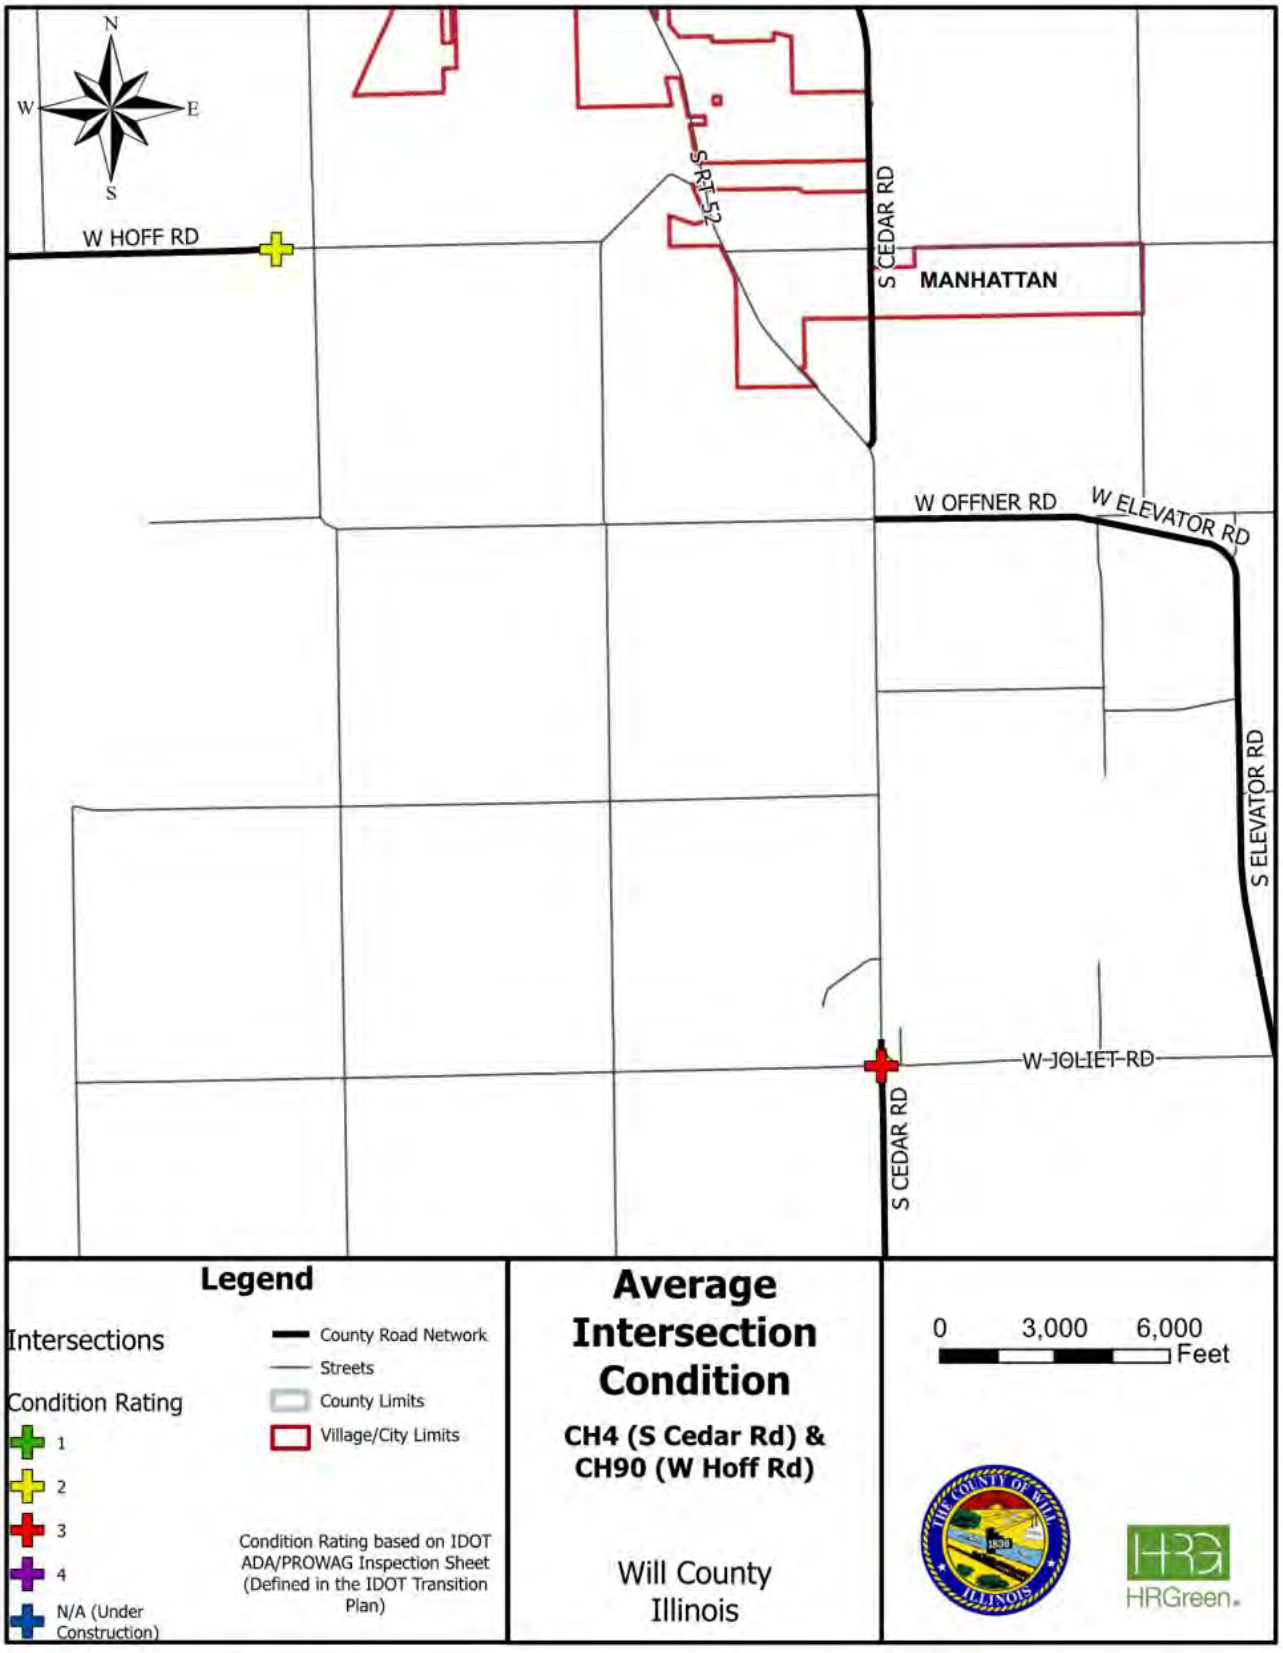
N
W
E
S
W HOFF RD
IL-52
S CEDAR RD
MANHATTAN
W OFFNER RD
W ELEVATOR RD
S ELEVATOR RD
W JOLIET RD
S CEDAR RD
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH4 (S Cedar Rd) & CH90 (W Hoff Rd)
Will County Illinois
0
3,000
6,000
Feet
HRGreen

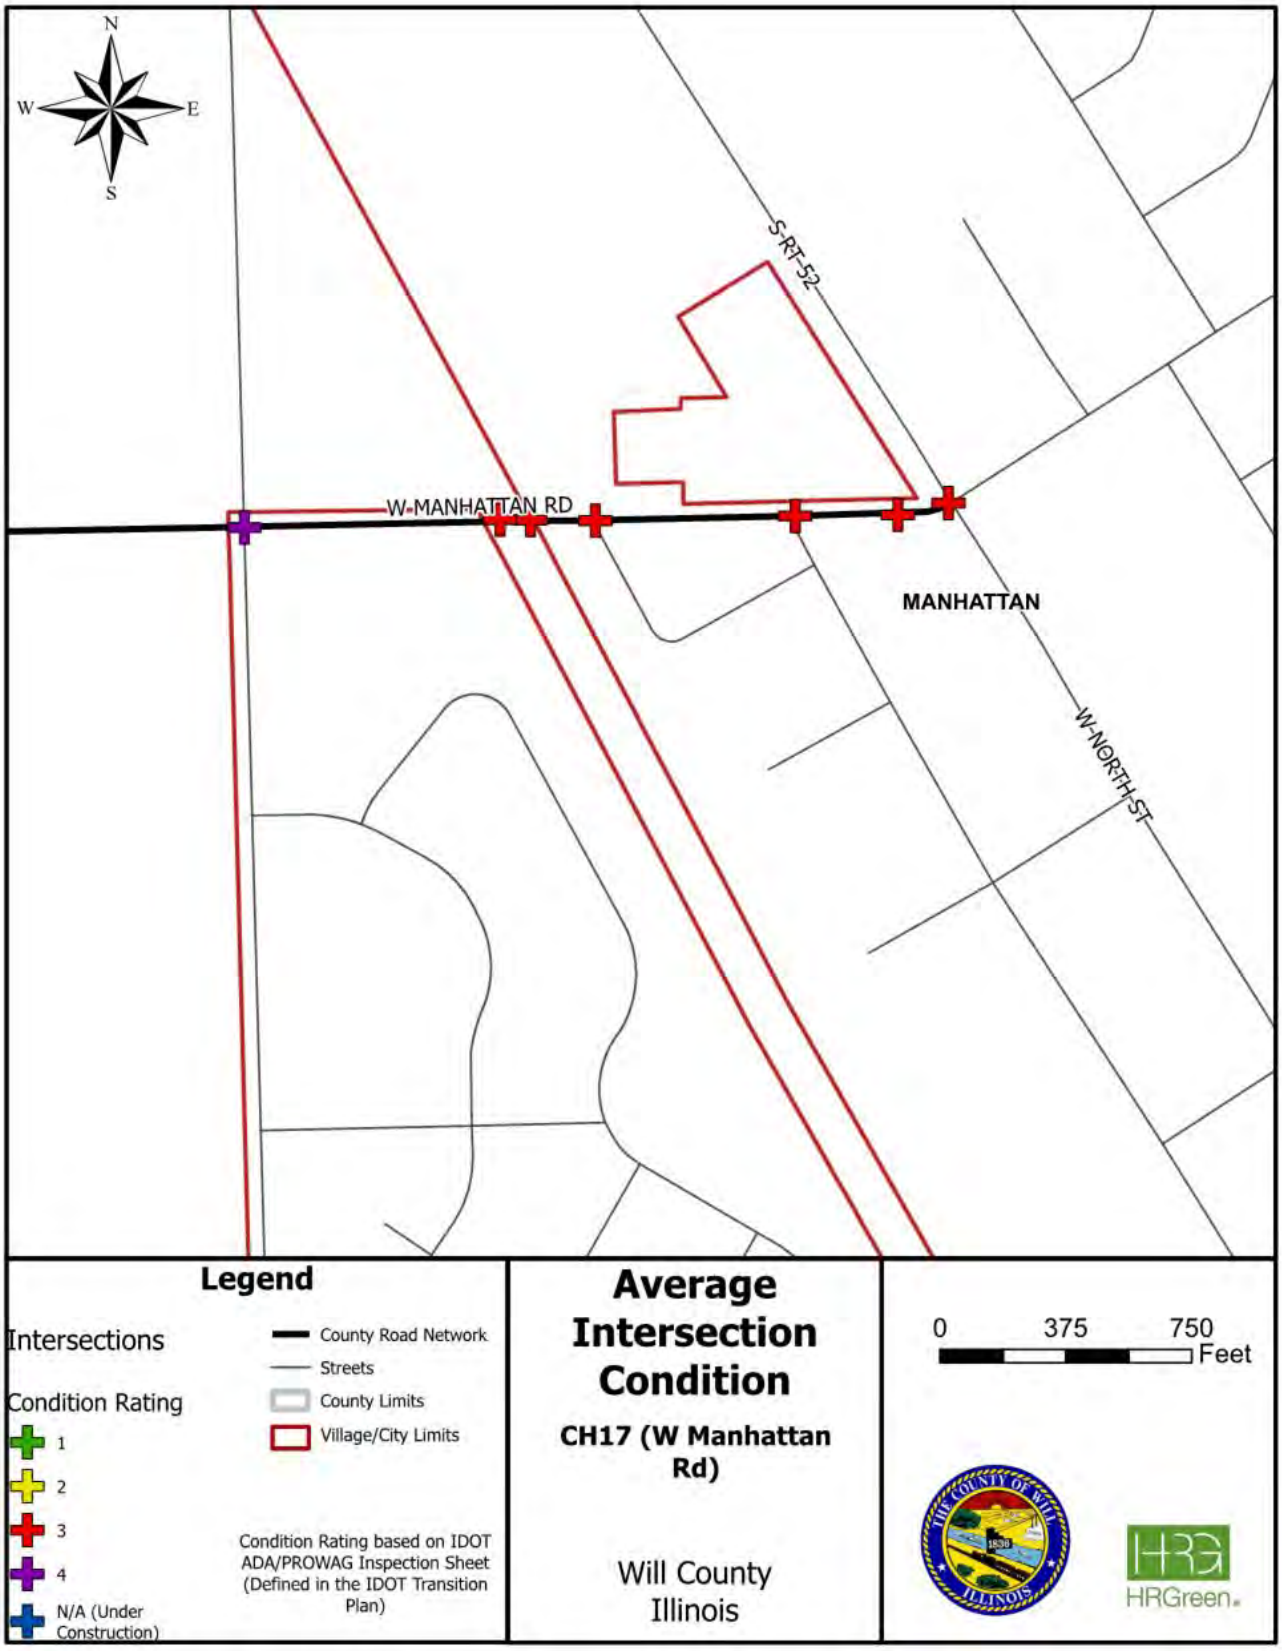
N
W
E
S
S-RT-52
W-MANHATTAN RD
MANHATTAN
W-NORTH-ST
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH17 (W Manhattan Rd)
Will County Illinois
0
375
750
Feet
HRGreen

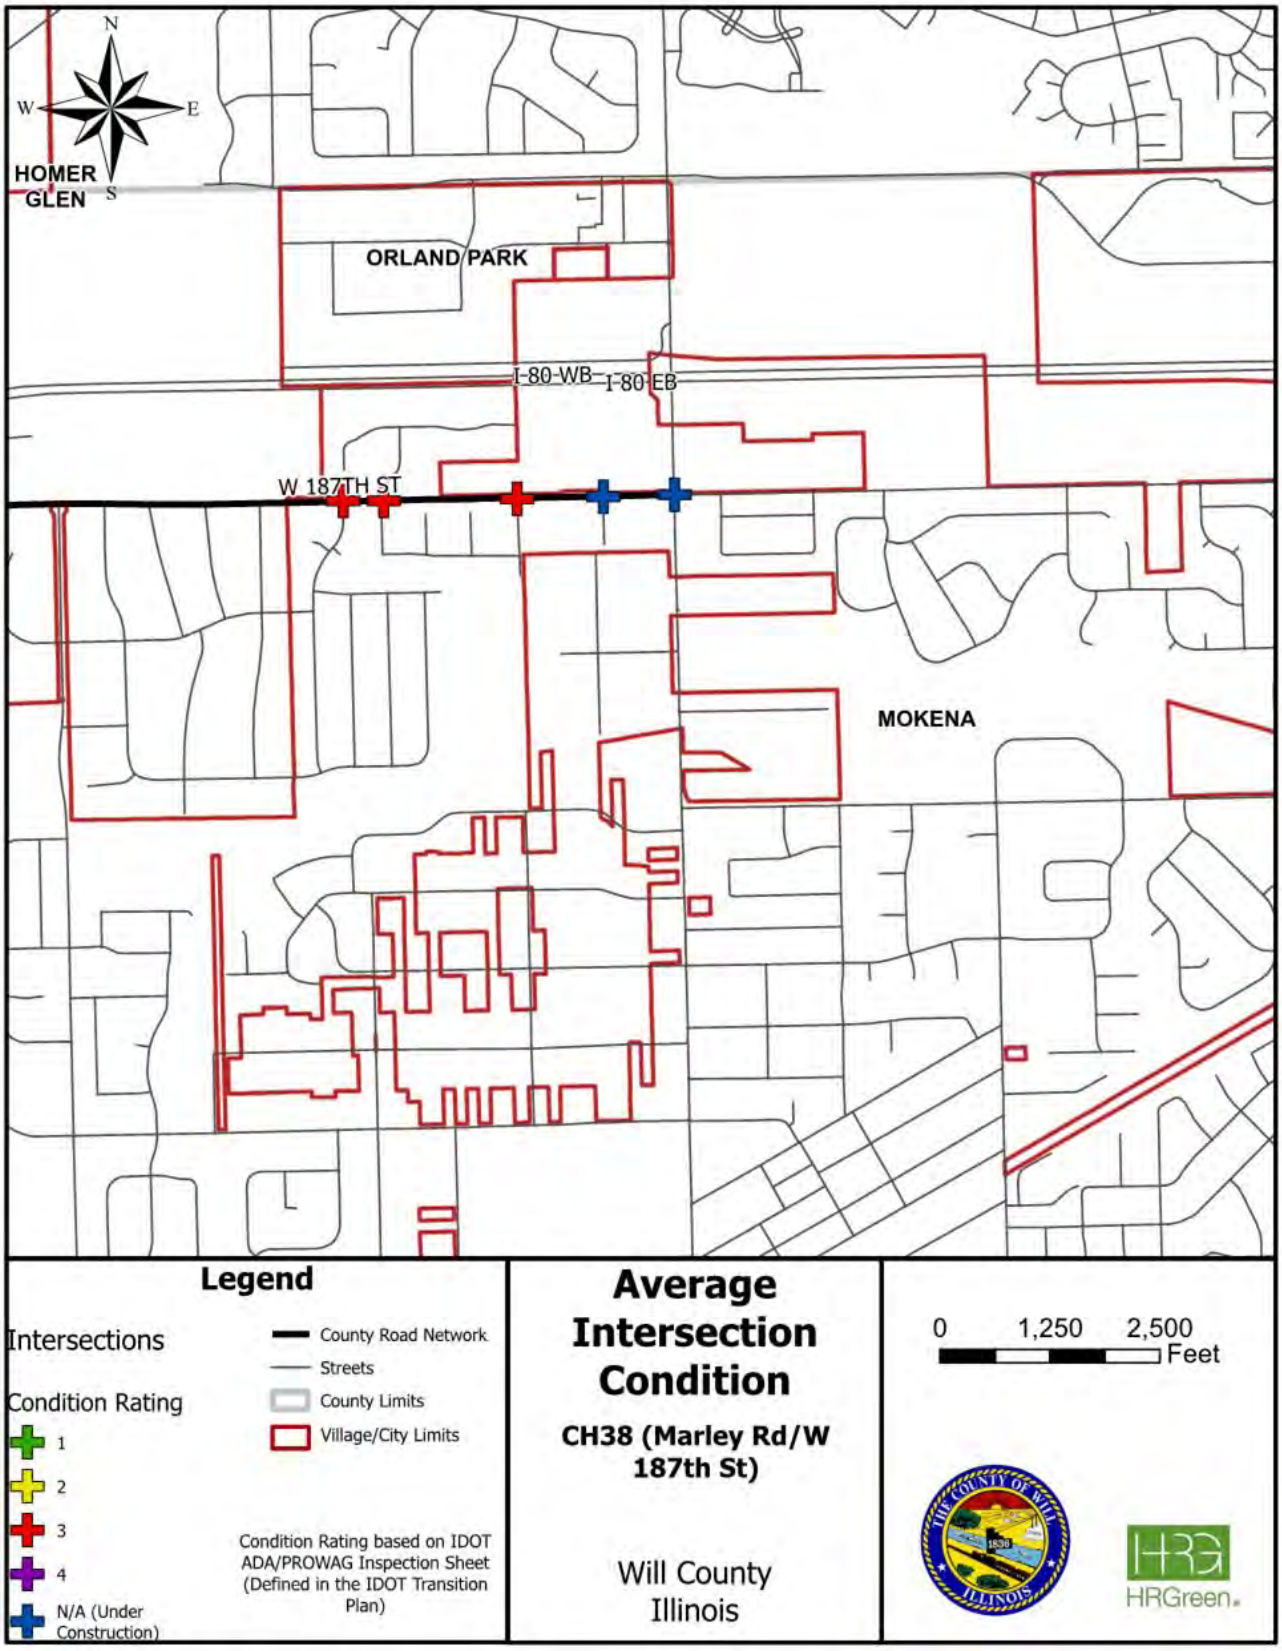
N
W
E
S
HOMER GLEN
ORLAND PARK
I-80-WB
I-80-EB
W 187TH ST
MOKENA
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH38 (Marley Rd/W 187th St)
Will County Illinois
0
1,250
2,500
Feet
HRGreen

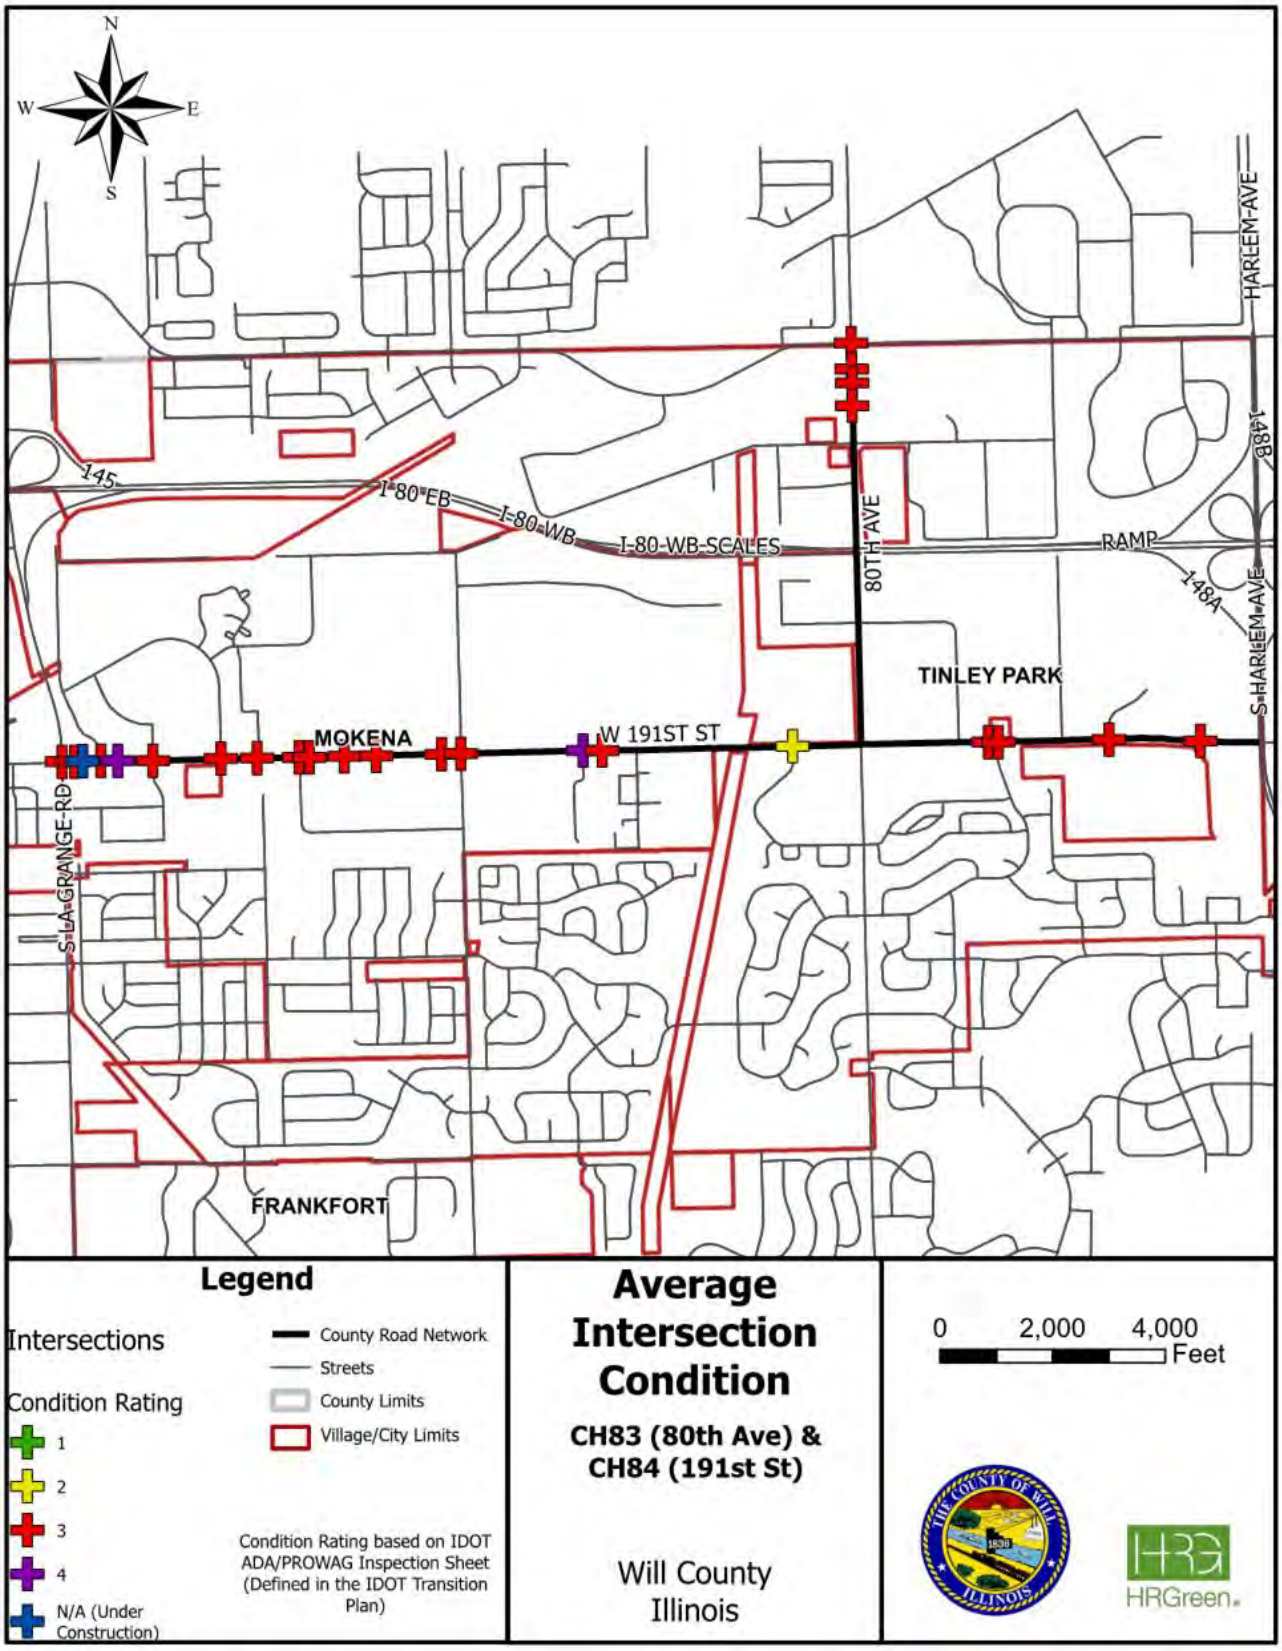
N
W
E
S
145
I-80-EB
I-80-WB
I-80-WB-SCALES
RAMP
80TH AVE
HARLEM AVE
S HARLEM AVE
148
148A
TINLEY PARK
MOKENA
W 191ST ST
S LA GRANGE RD
FRANKFORT
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH83 (80th Ave) & CH84 (191st St)
Will County Illinois
0
2,000
4,000
Feet
HRGreen

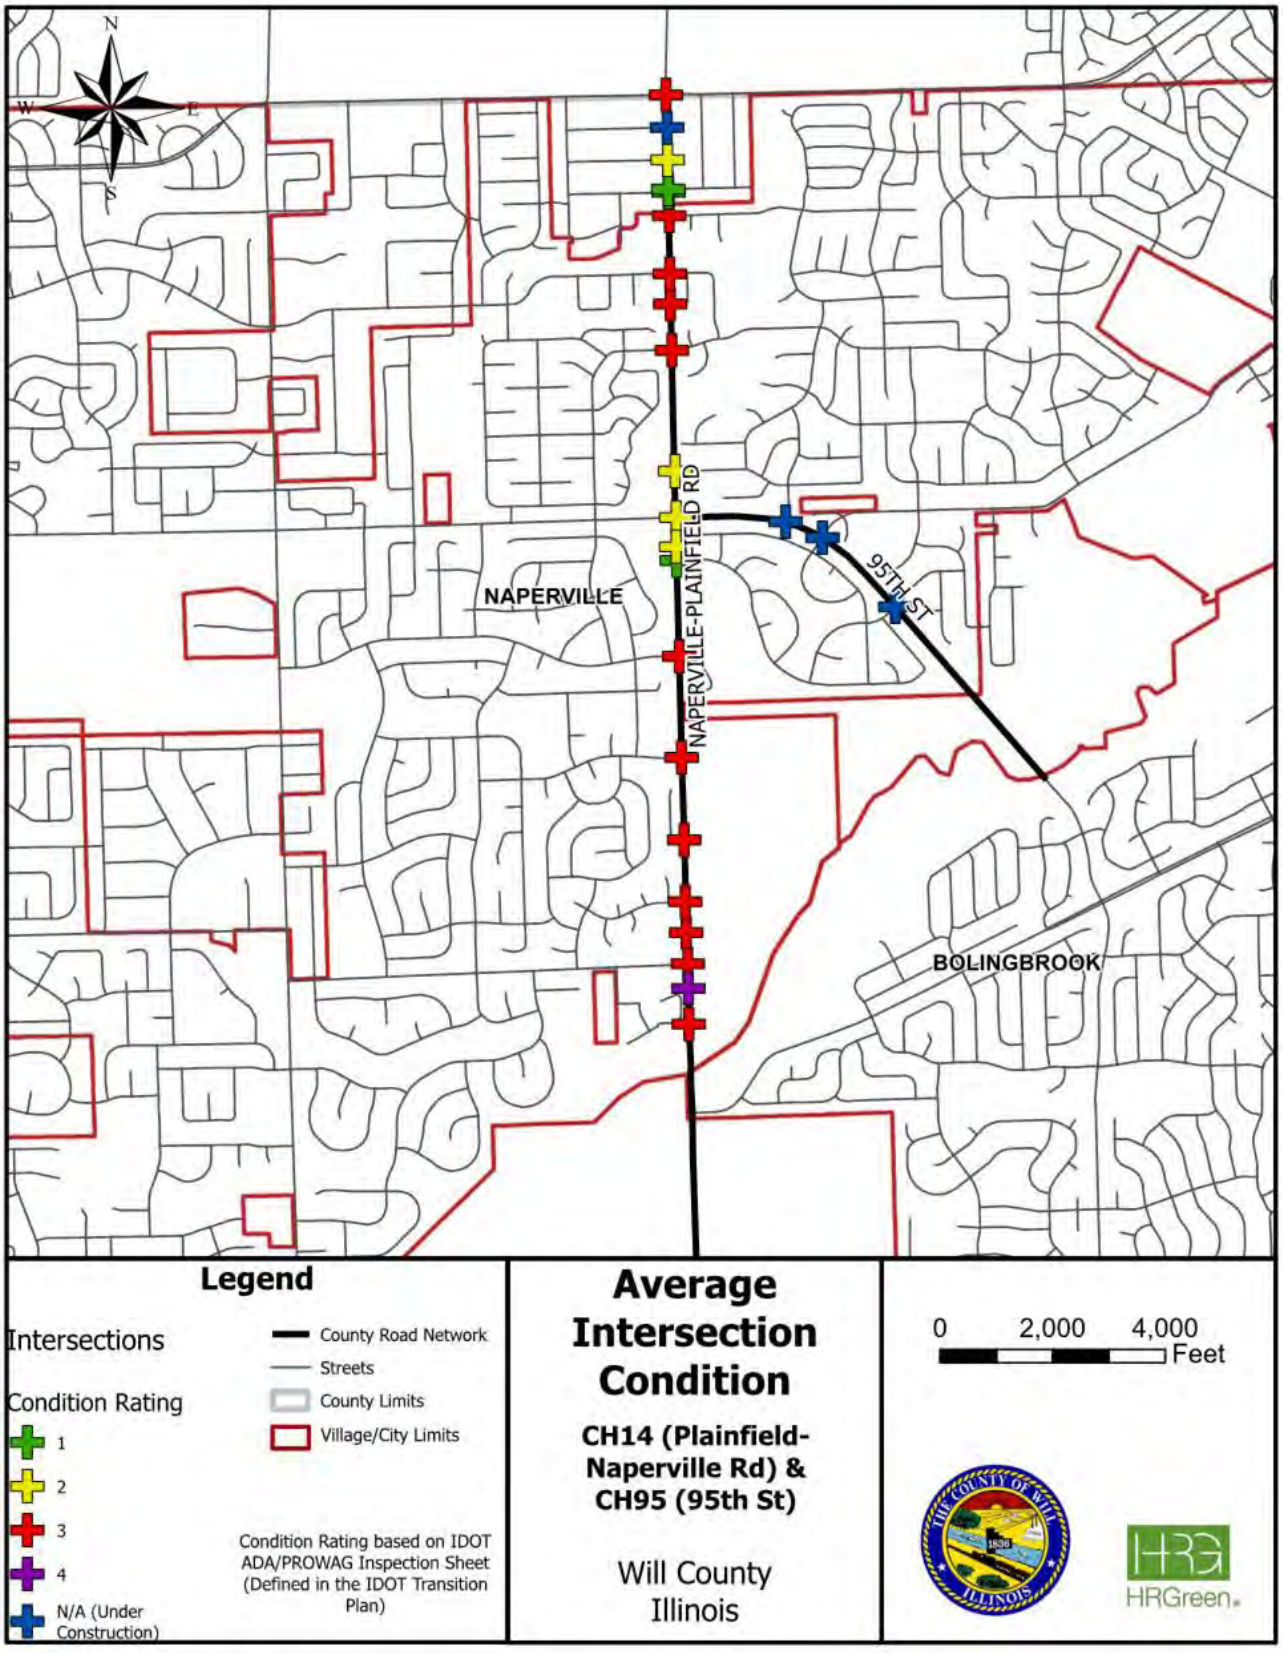
N
W
E
S
NAPERVILLE
NAPERVILLE-PLAINFIELD RD
95TH ST
BOLINGBROOK
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH14 (Plainfield-Naperville Rd) & CH95 (95th St)
Will County Illinois
0
2,000
4,000
Feet
HRGreen

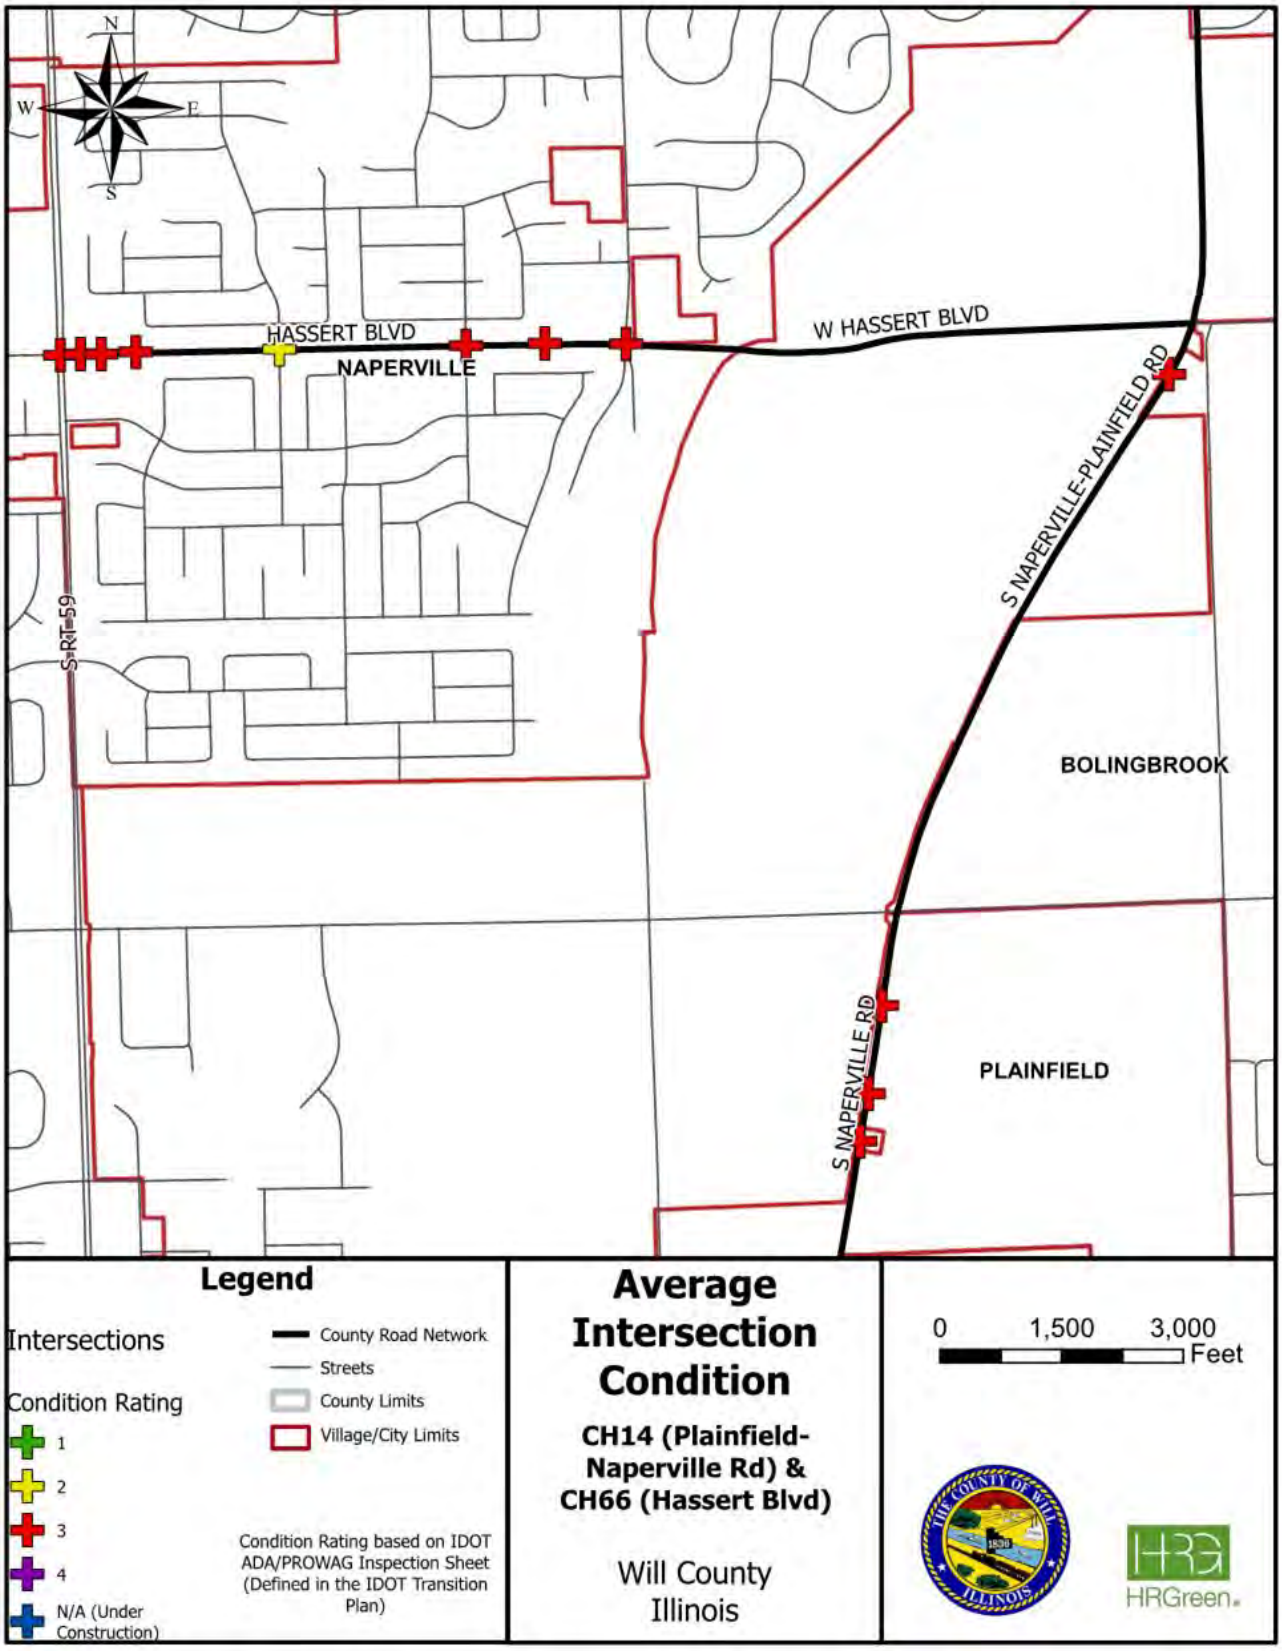
N
W
E
S
HASSERT BLVD
NAPERVILLE
W HASSERT BLVD
S NAPERVILLE-PLAINFIELD RD
S RT 59
BOLINGBROOK
S NAPERVILLE RD
PLAINFIELD
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH14 (Plainfield-Naperville Rd) & CH66 (Hassert Blvd)
Will County Illinois
0
1,500
3,000
Feet
HRGreen

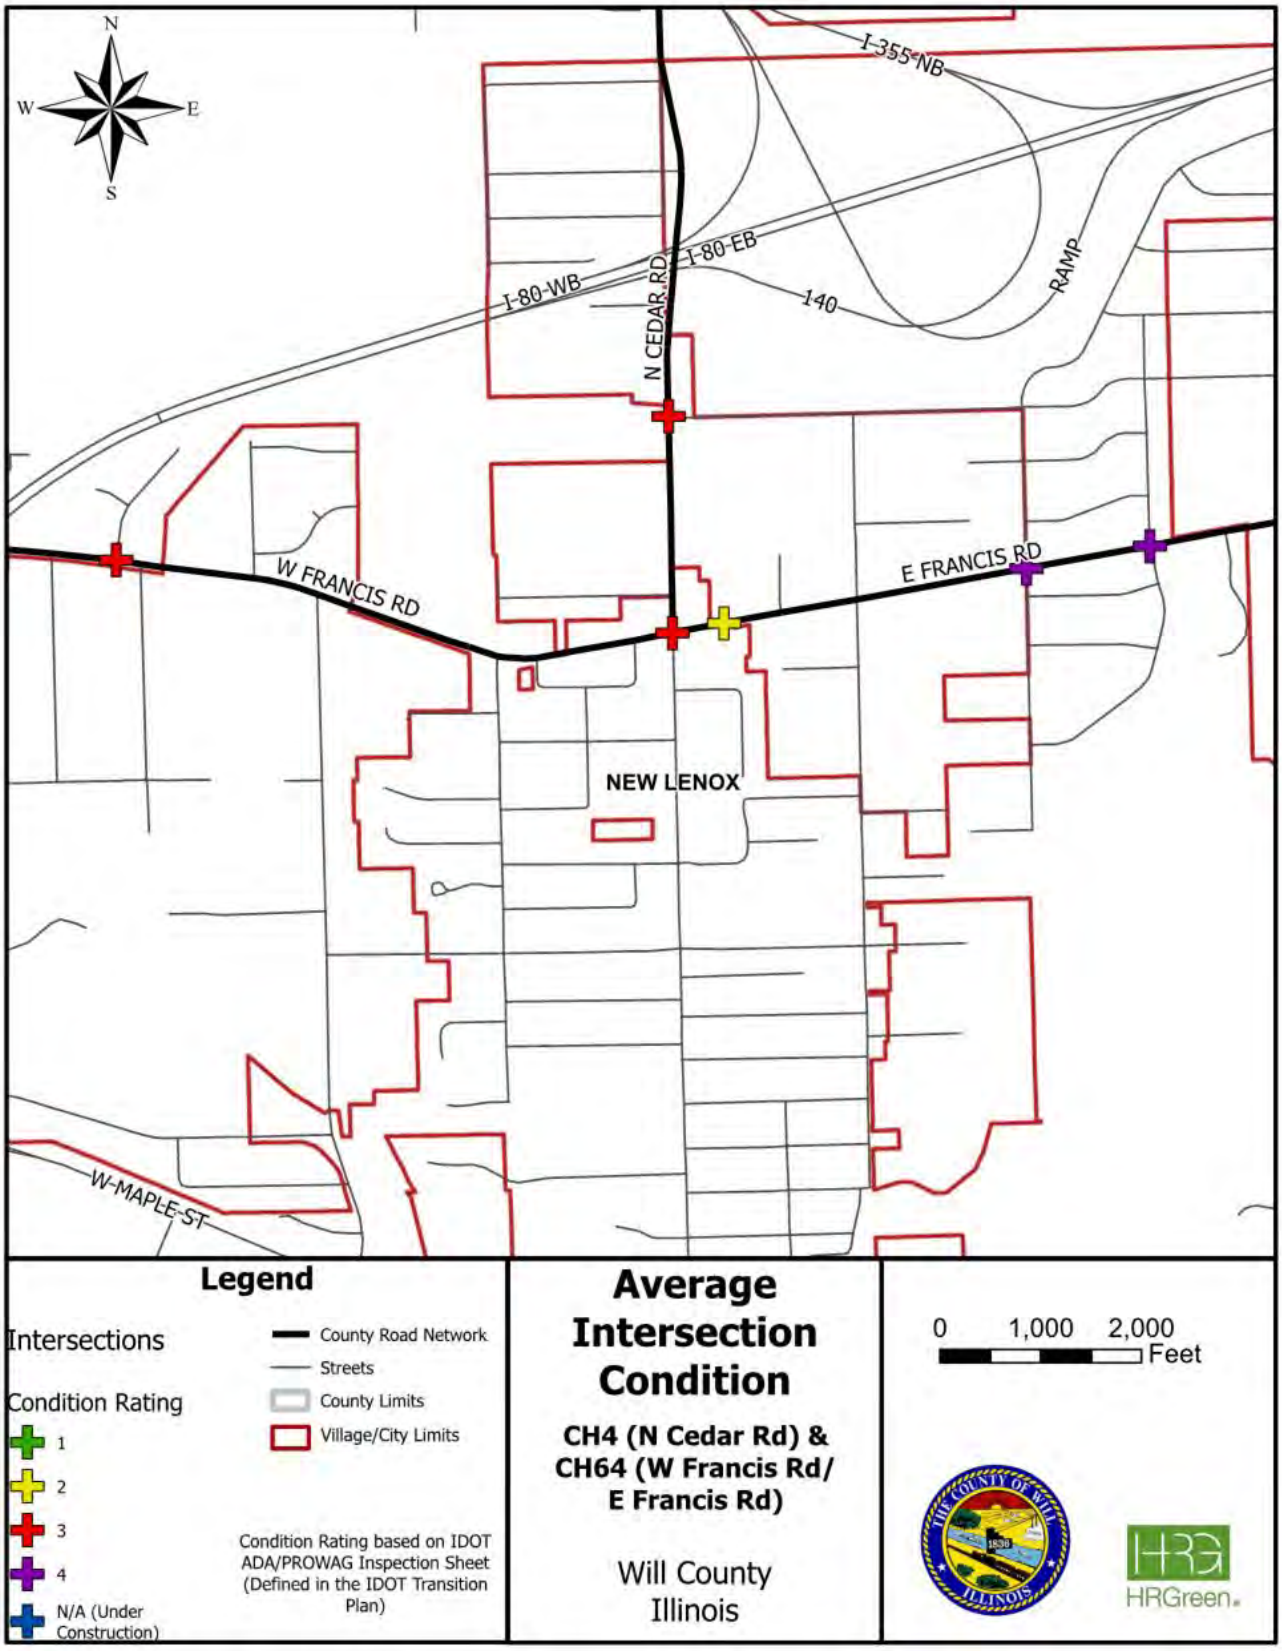
N
W
E
S
I-355-NB
I-80-WB
I-80-EB
N CEDAR RD
140
RAMP
W FRANCIS RD
E FRANCIS RD
NEW LENOX
W-MAPLE-ST
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH4 (N Cedar Rd) & CH64 (W Francis Rd/ E Francis Rd)
Will County Illinois
0
1,000
2,000
Feet
HRGreen

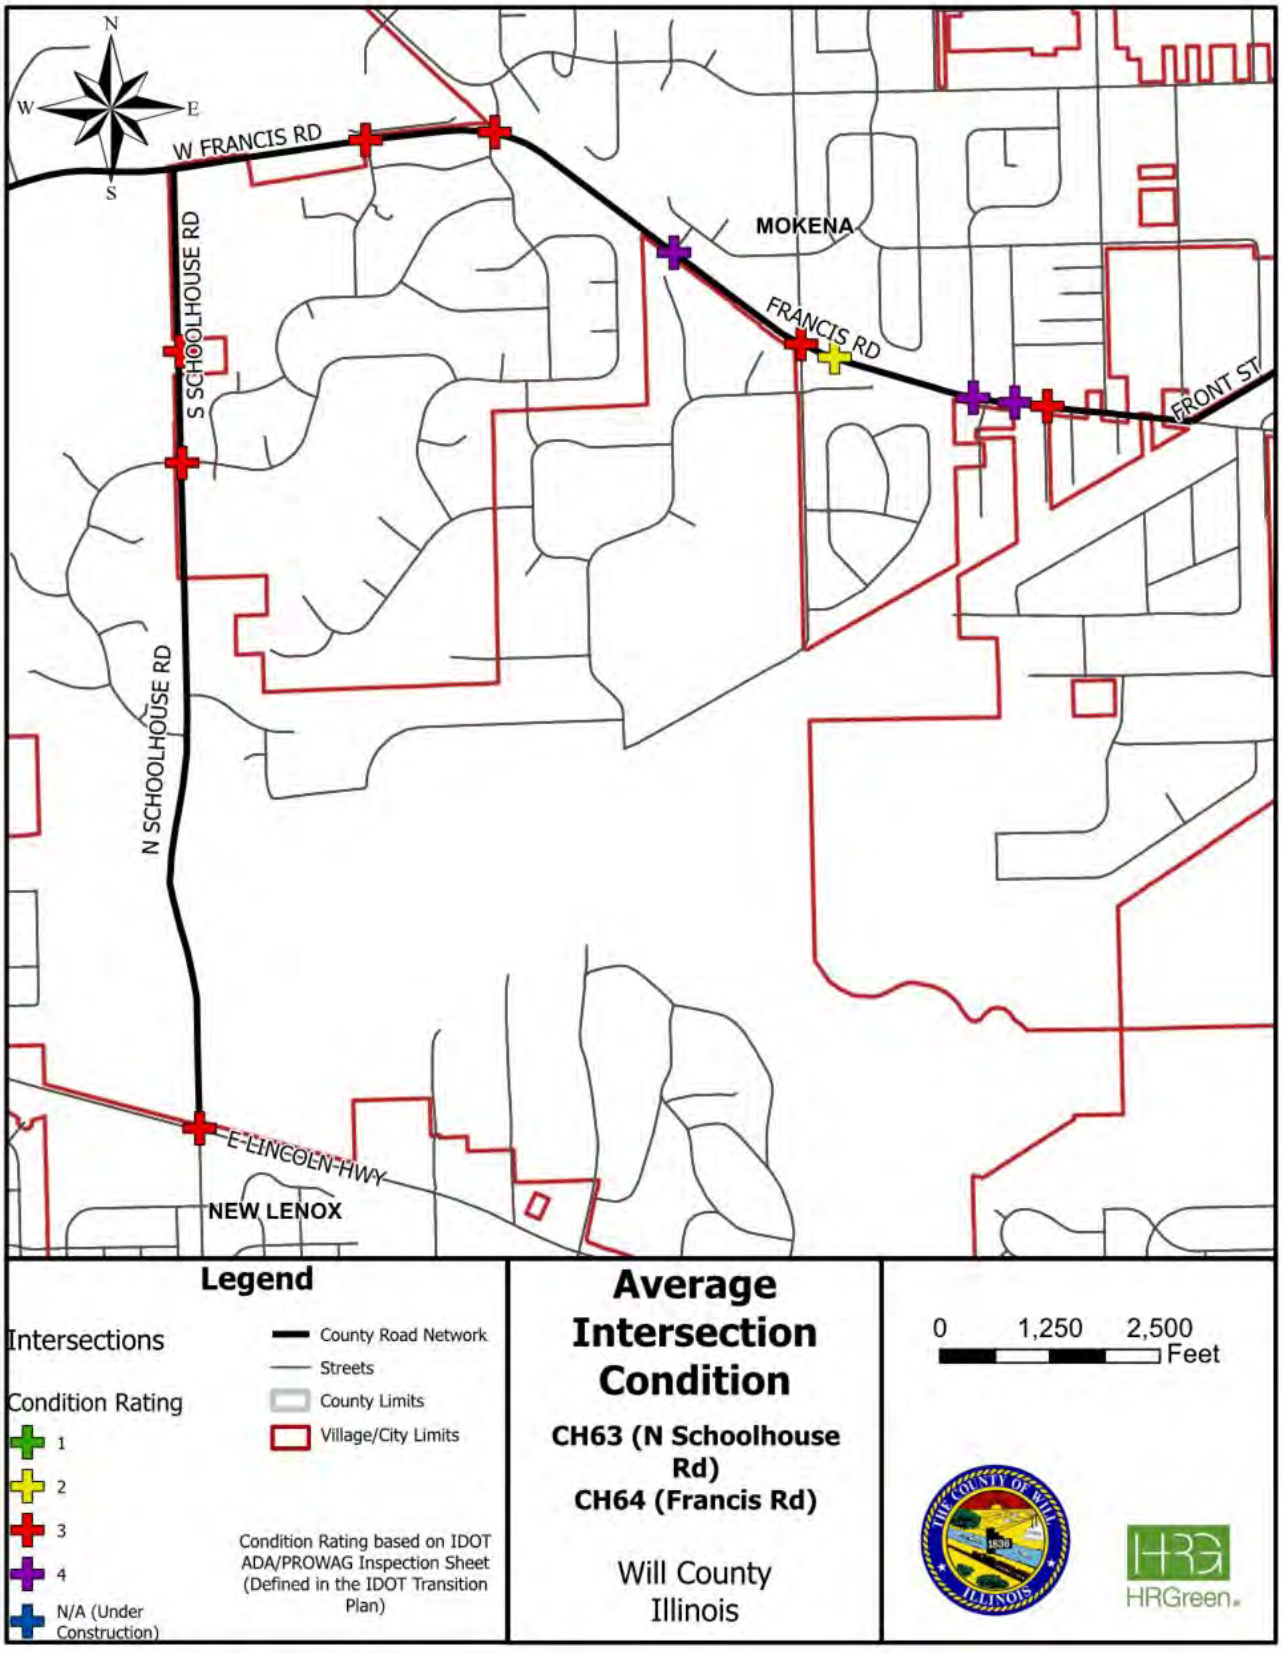
N
W
E
S
W FRANCIS RD
S SCHOOLHOUSE RD
MOKENA
FRANCIS RD
FRONT ST
N SCHOOLHOUSE RD
E LINCOLN HWY
NEW LENOX
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH63 (N Schoolhouse Rd)
CH64 (Francis Rd)
Will County Illinois
0
1,250
2,500
Feet
HRGreen

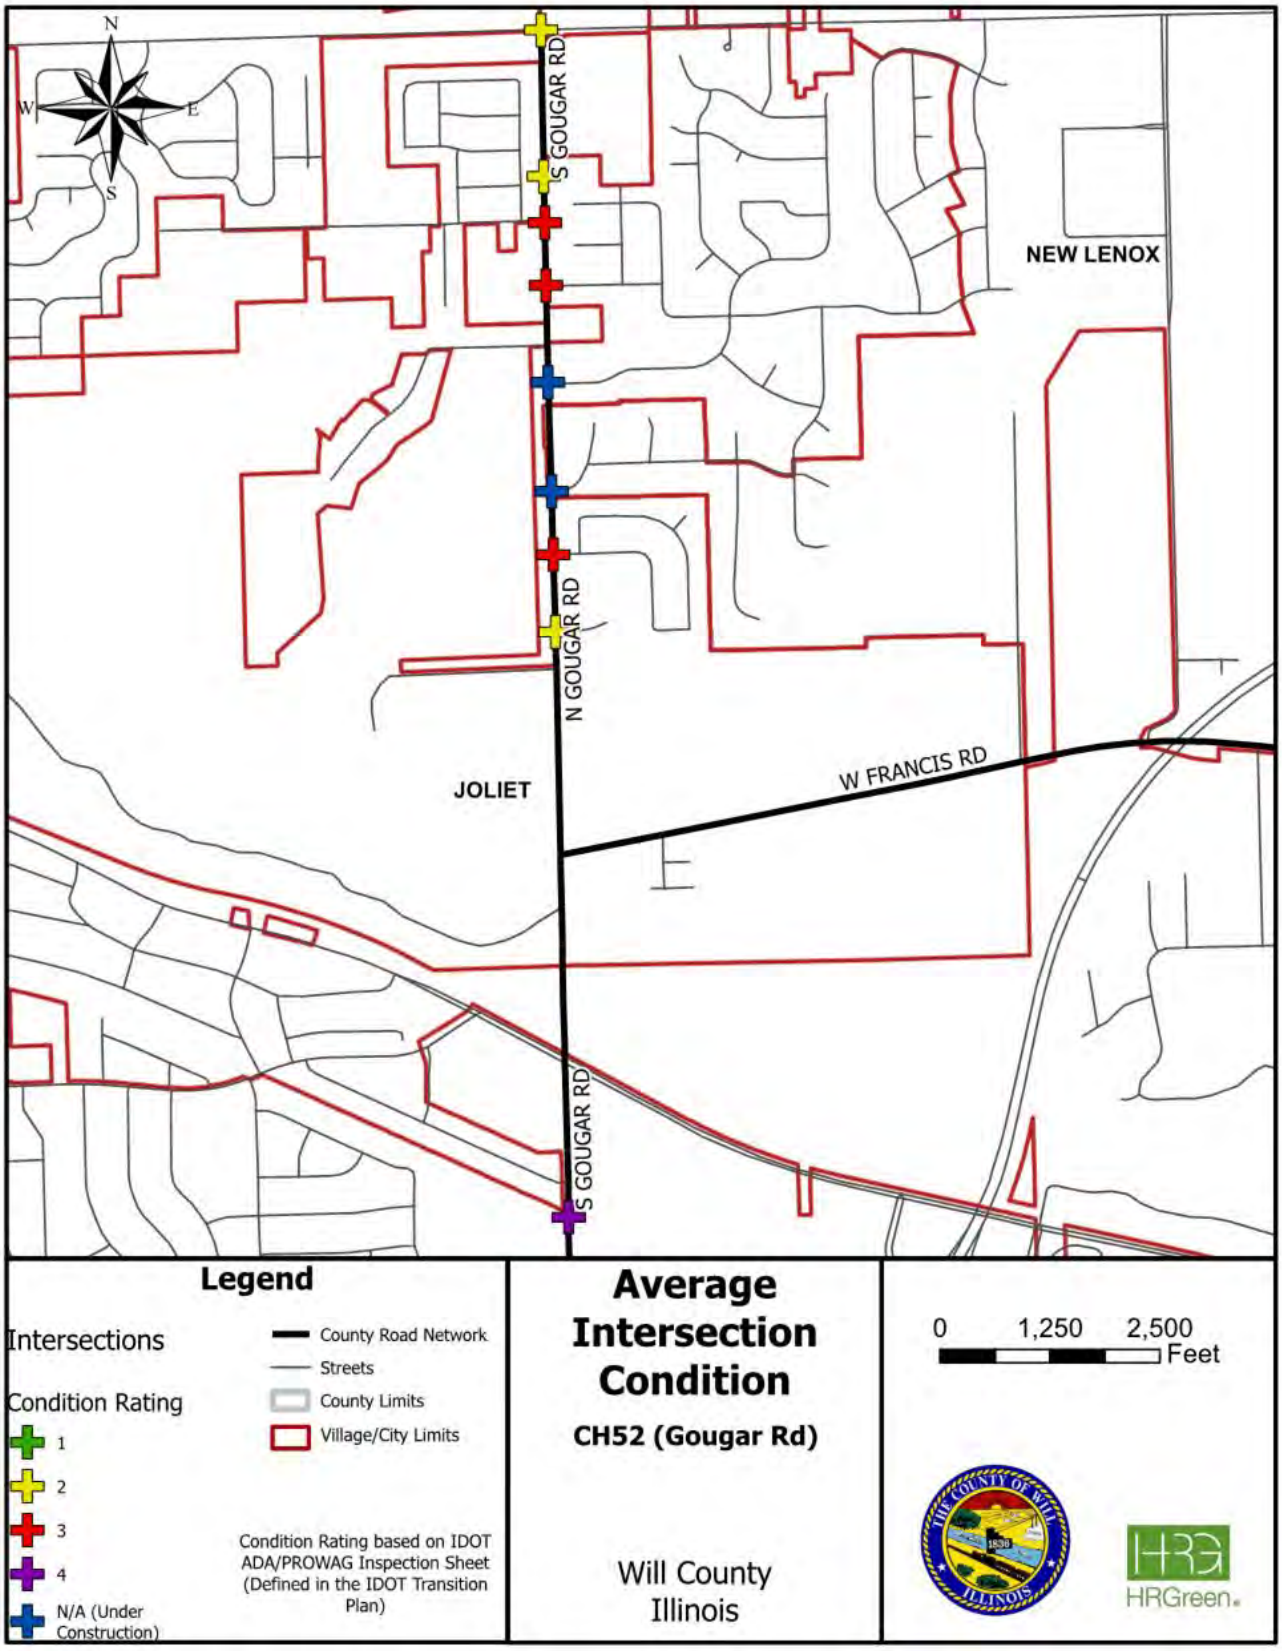
N
W
E
S
S GOUGAR RD
NEW LENOX
N GOUGAR RD
JOLIET
W FRANCIS RD
S GOUGAR RD
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH52 (Gougar Rd)
Will County Illinois
0
1,250
2,500
Feet
HRGreen

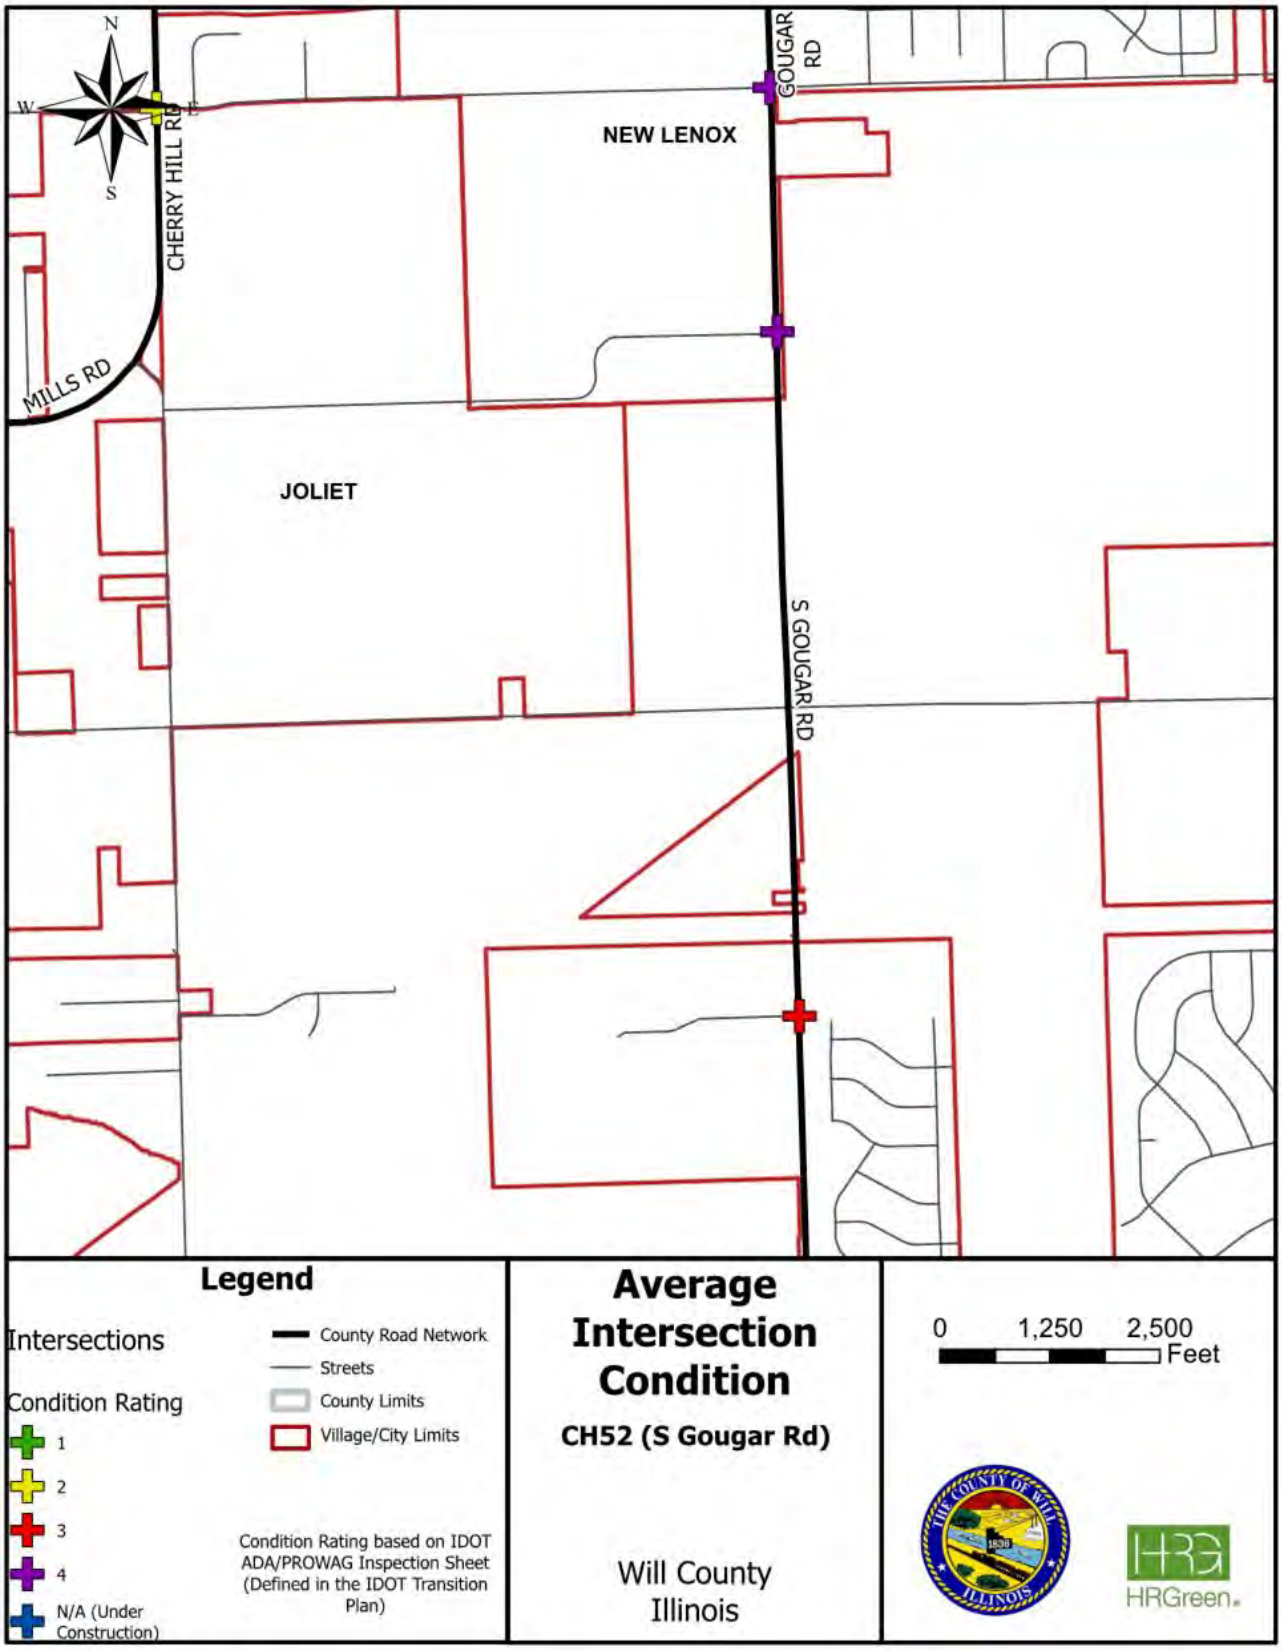
N
W
E
S
CHERRY HILL RD
GOUGAR RD
NEW LENOX
MILLS RD
JOLIET
S GOUGAR RD
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH52 (S Gougar Rd)
Will County Illinois
0
1,250
2,500
Feet
HRGreen

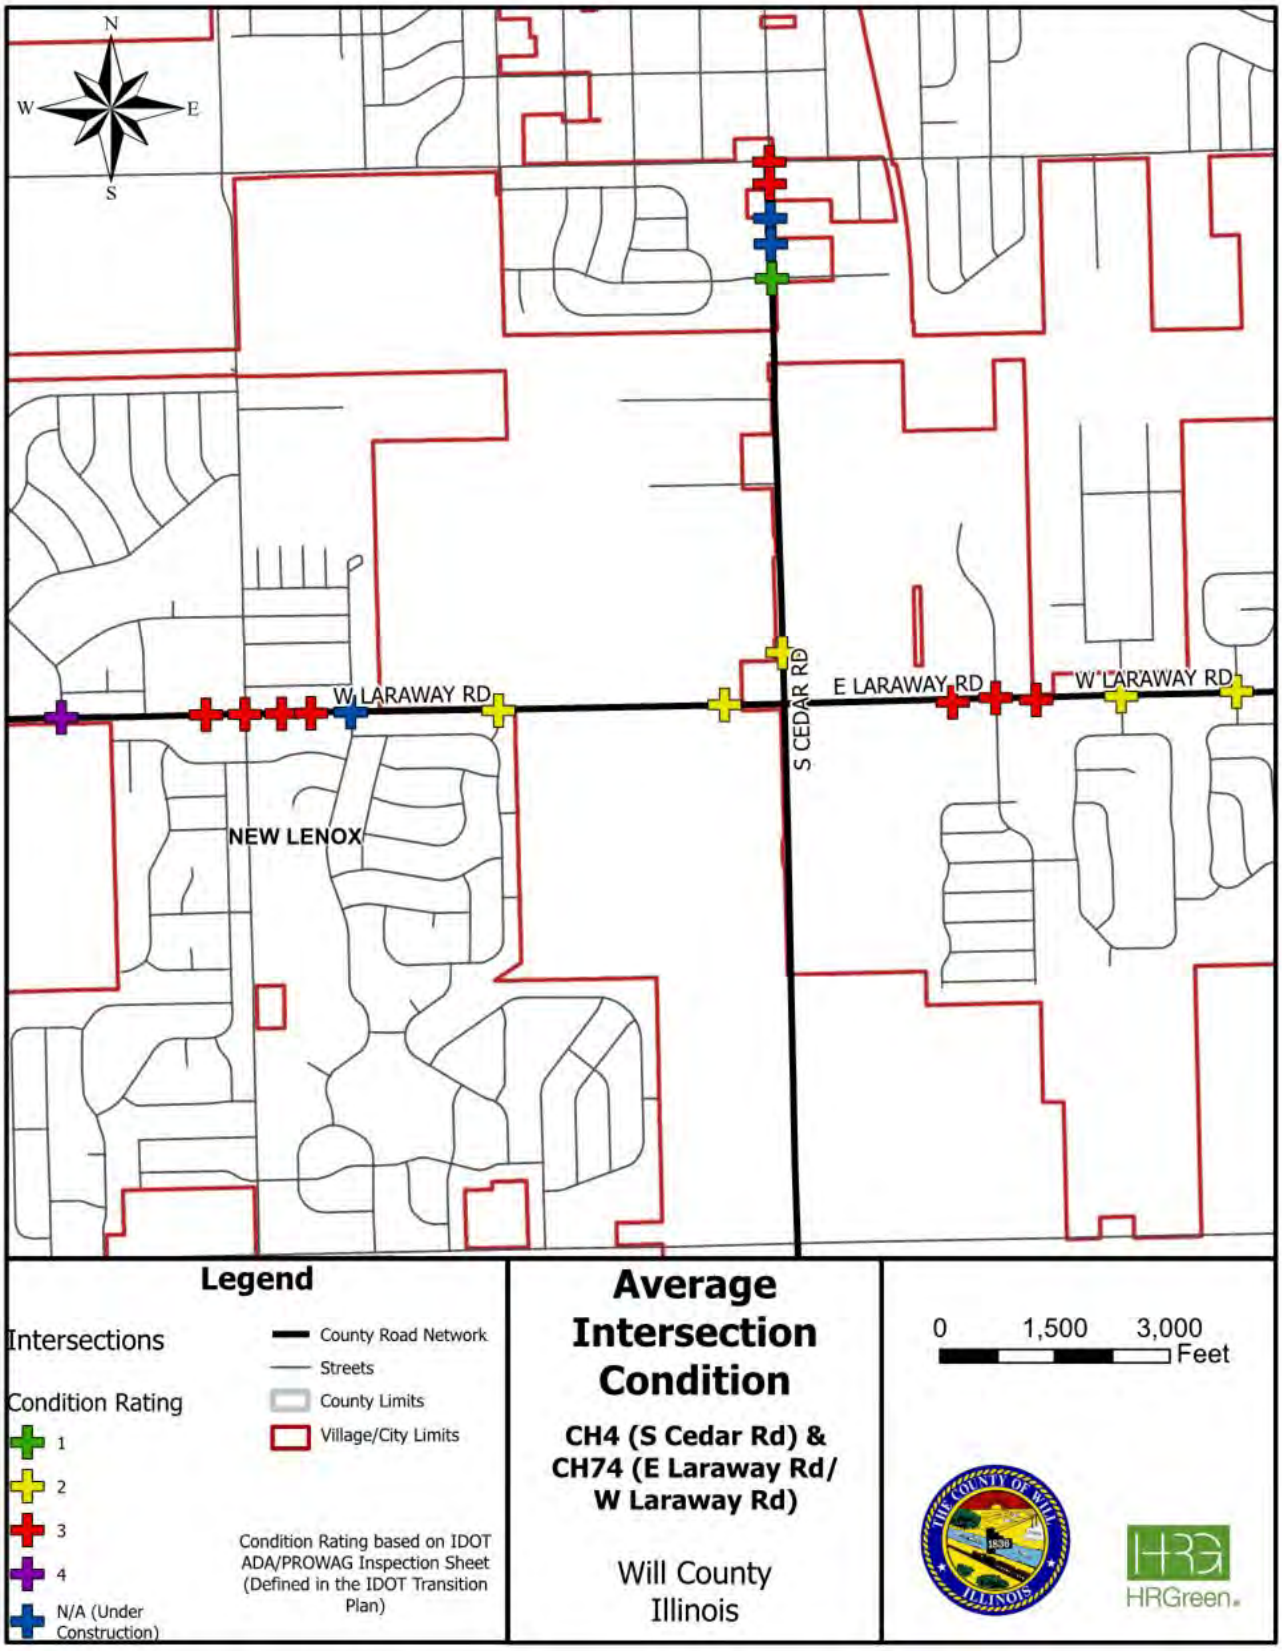
N
W
E
S
W LARAWAY RD
E LARAWAY RD
W LARAWAY RD
S CEDAR RD
NEW LENOX
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH4 (S Cedar Rd) & CH74 (E Laraway Rd/ W Laraway Rd)
Will County Illinois
0
1,500
3,000
Feet
HRGreen

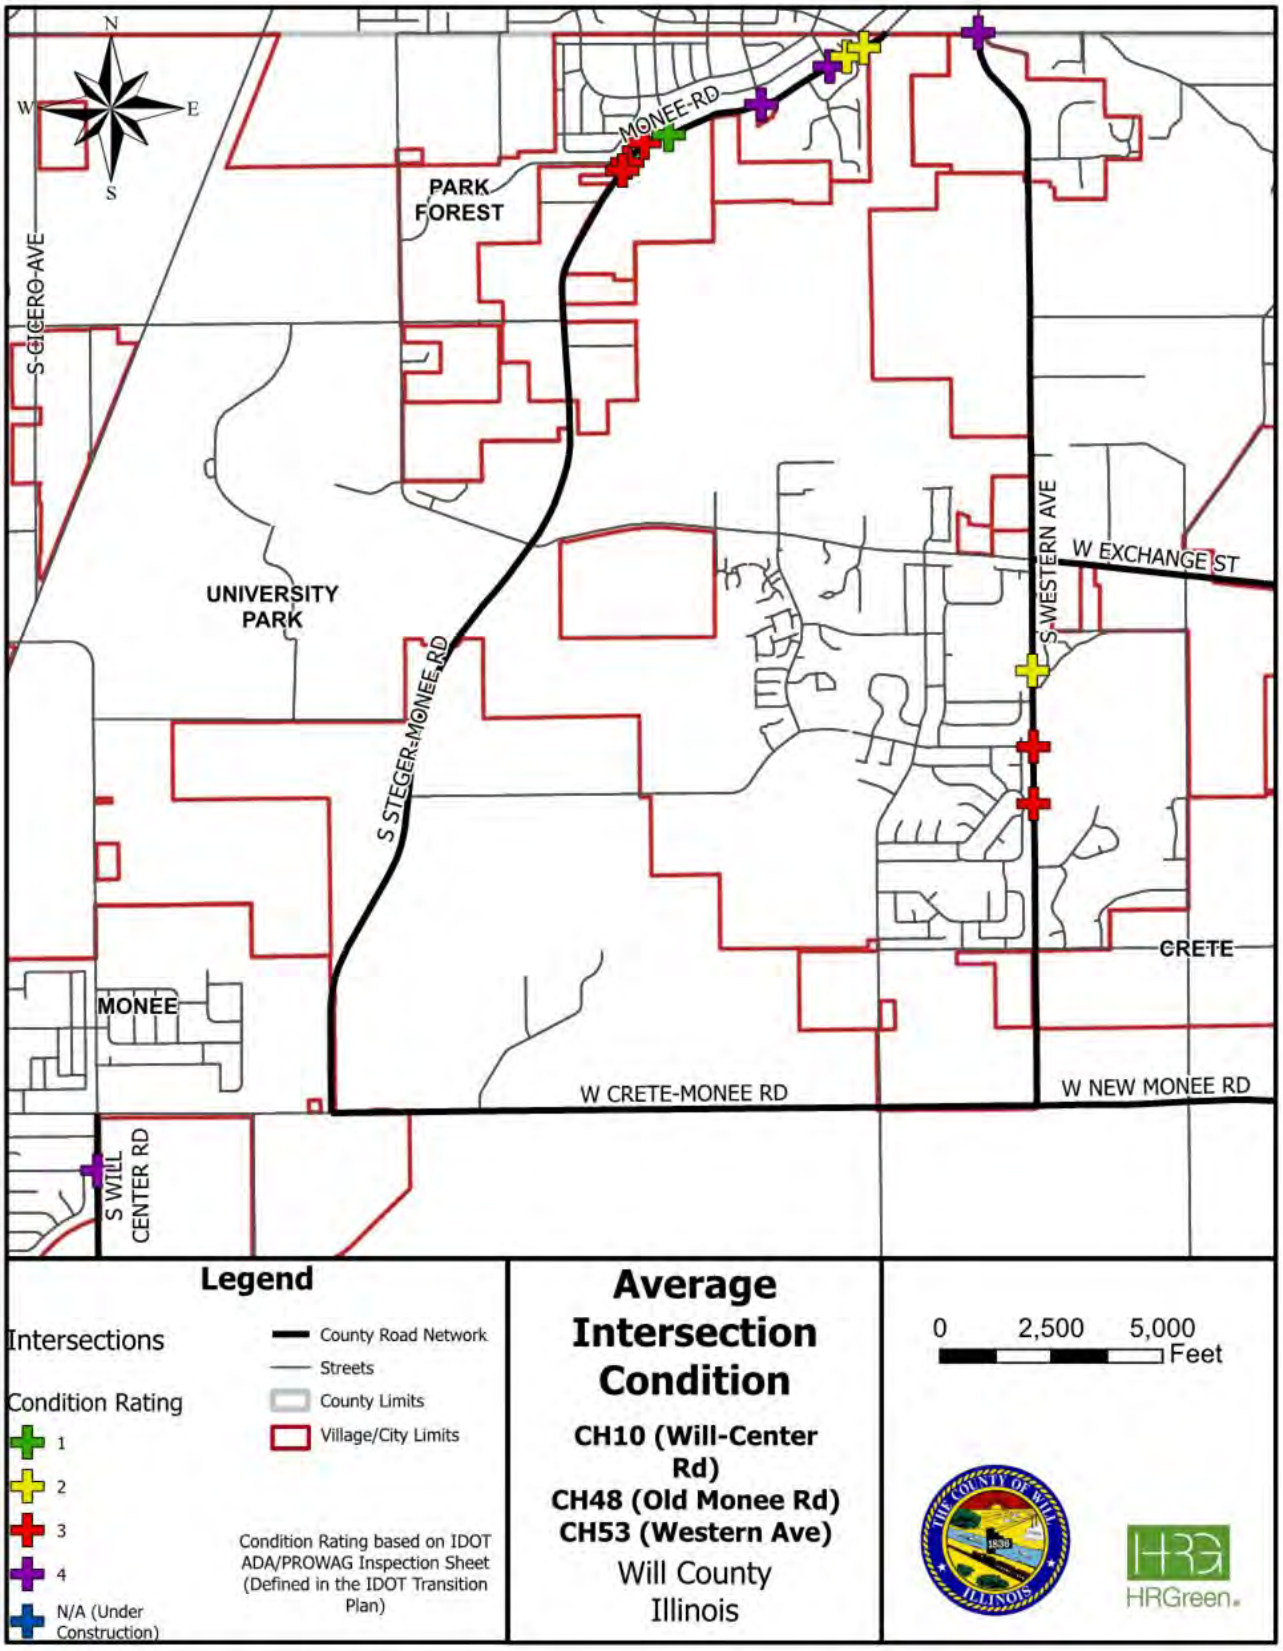
N
W
E
S
MONEE-RD
PARK FOREST
S CICERO AVE
UNIVERSITY PARK
S STEGER-MONEE RD
S WESTERN AVE
W EXCHANGE ST
CRETE
MONEE
W CRETE-MONEE RD
W NEW MONEE RD
S WILL CENTER RD
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH10 (Will-Center Rd)
CH48 (Old Monee Rd)
CH53 (Western Ave)
Will County
Illinois
0
2,500
5,000
Feet
HRGreen

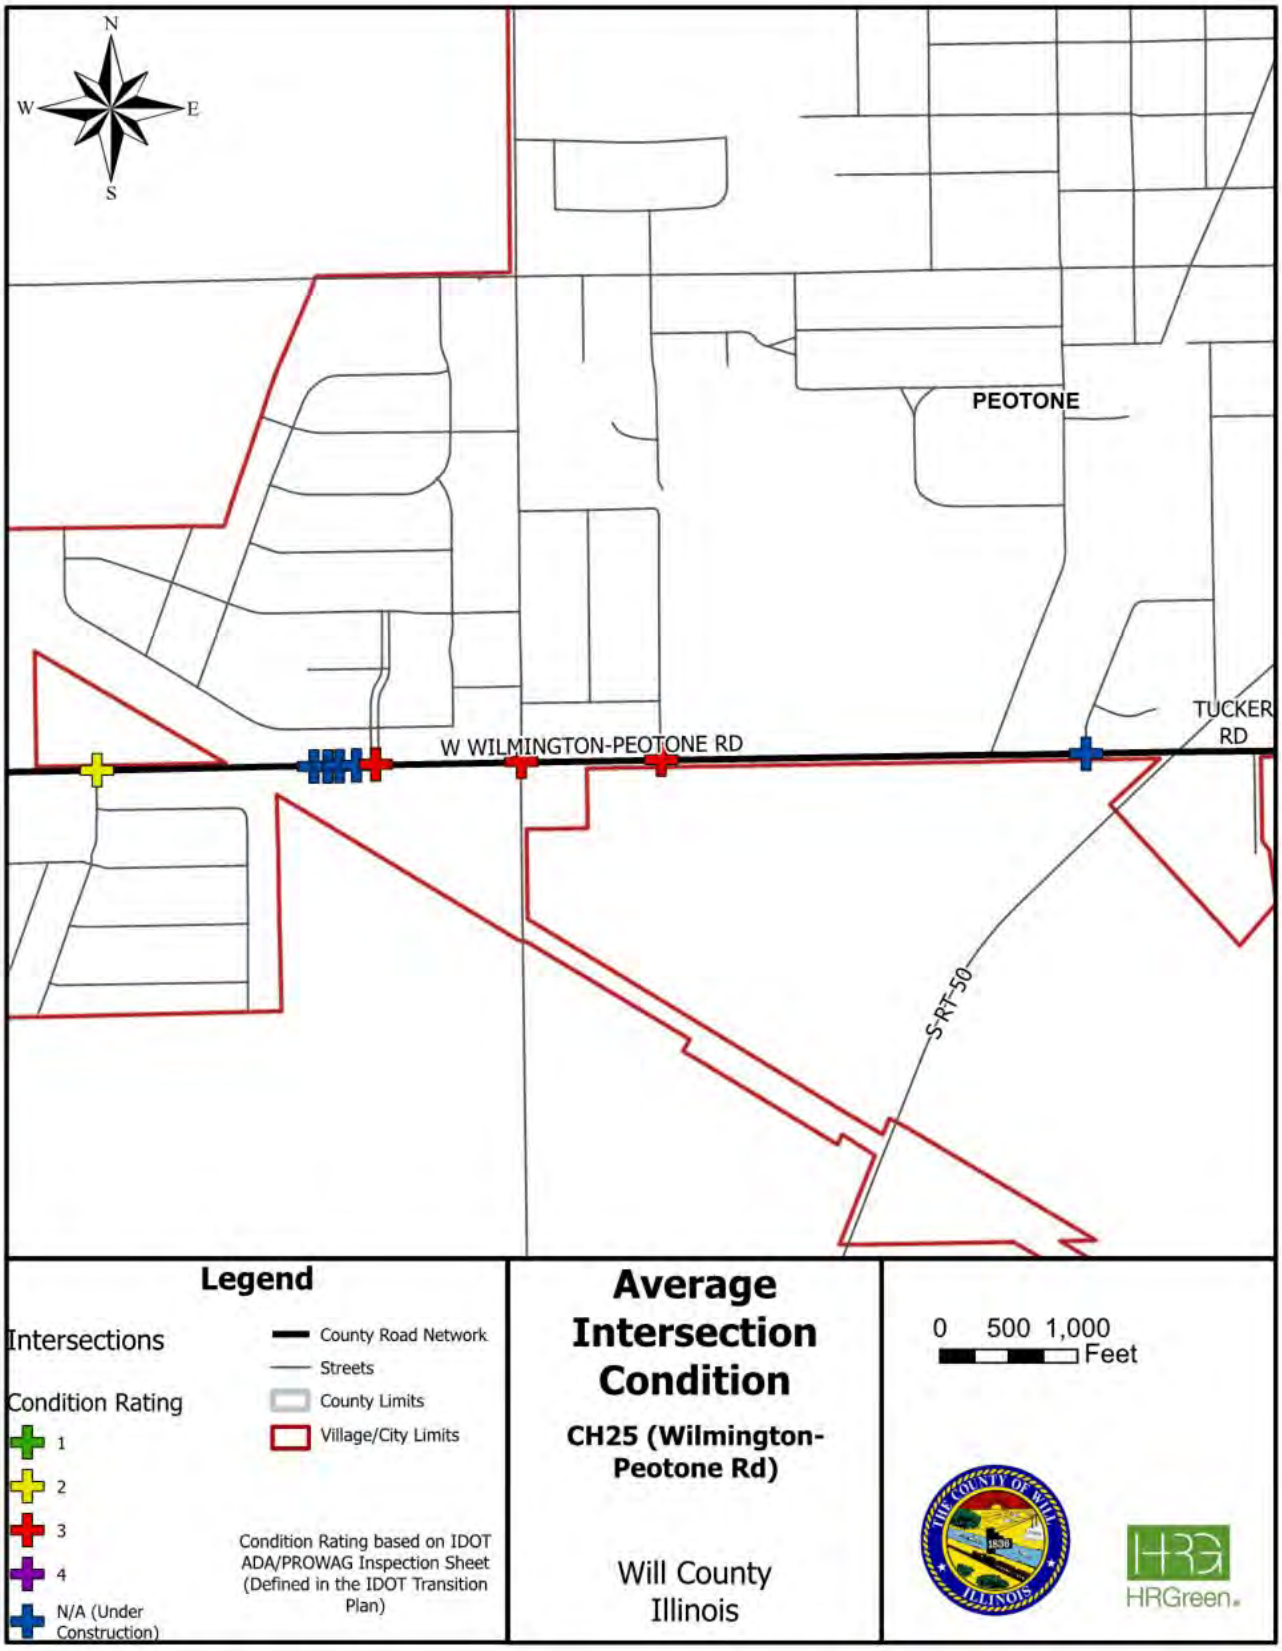
N
W
E
S
PEOTONE
W WILMINGTON-PEOTONE RD
TUCKER RD
S-RT-50
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH25 (Wilmington-Peotone Rd)
Will County Illinois
0 500 1,000 Feet
HRGreen

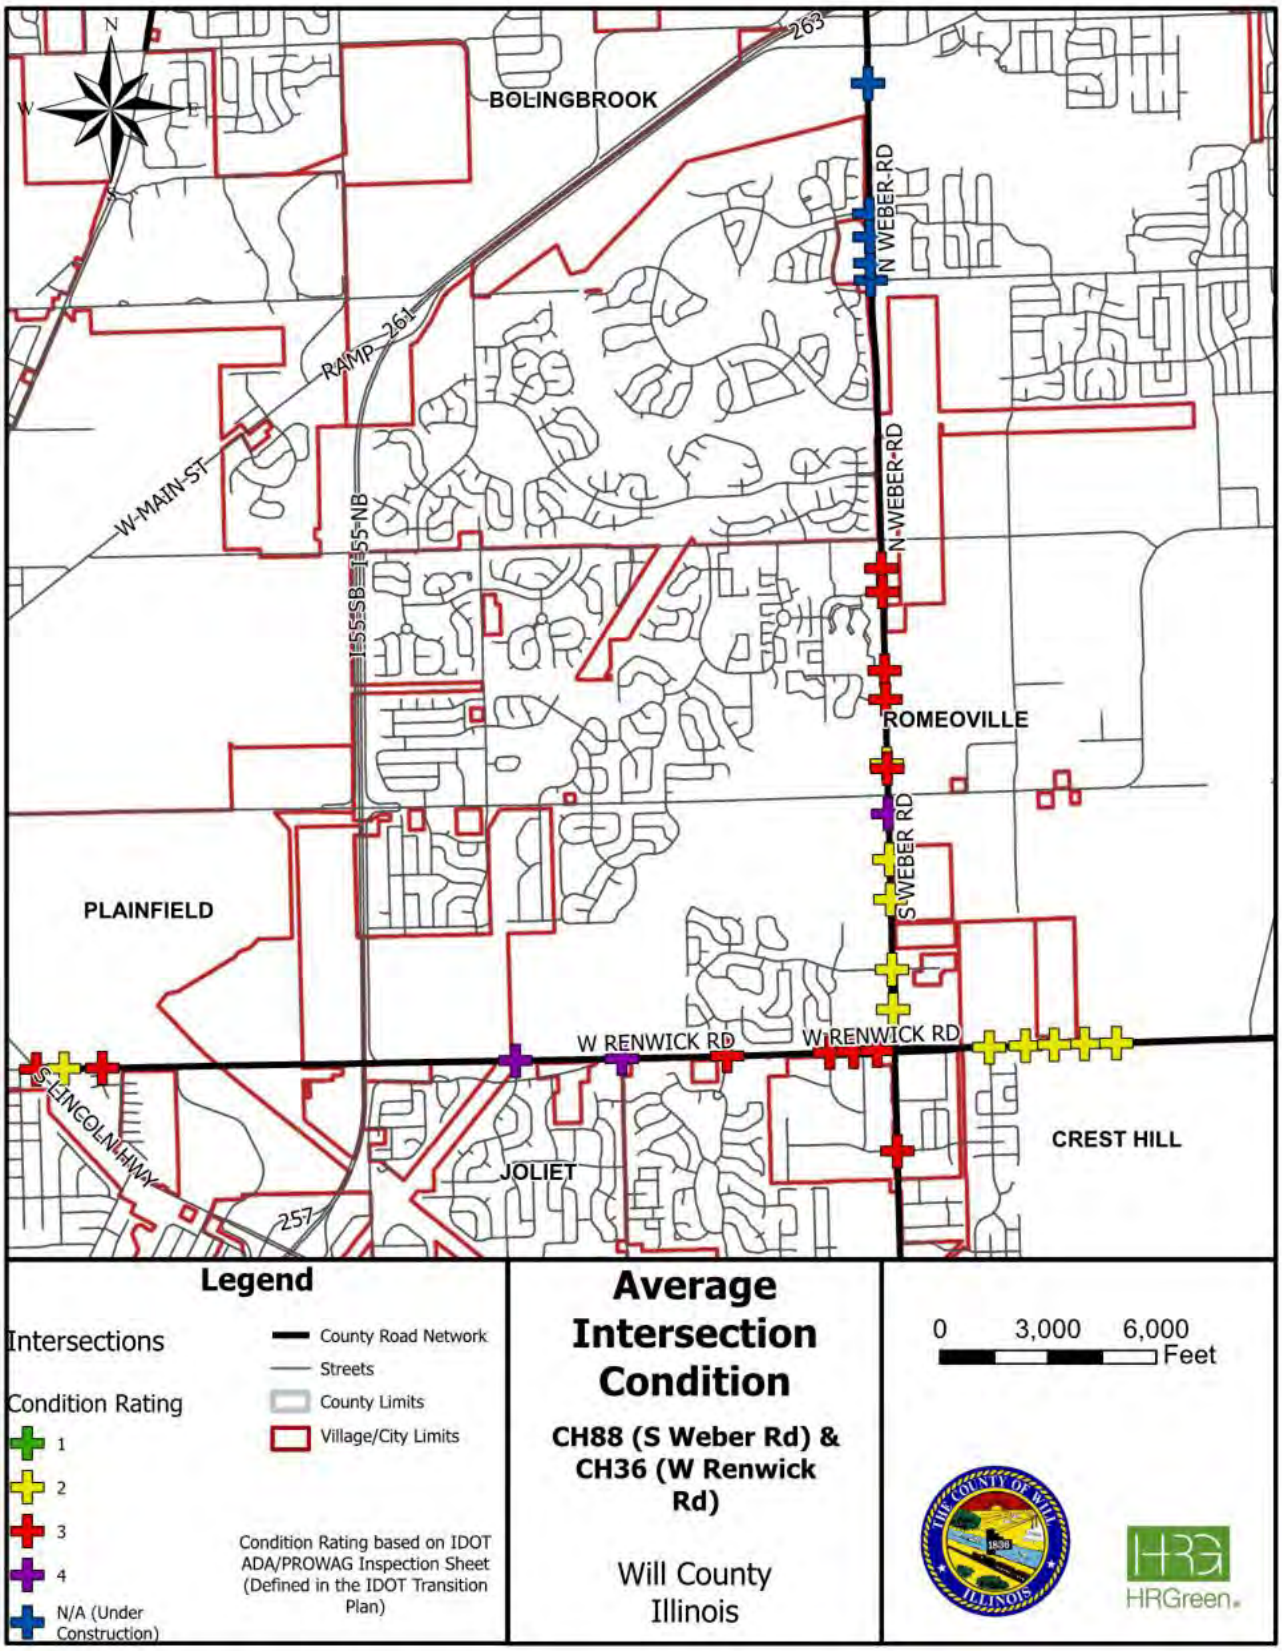
N
W
E
BOLINGBROOK
263
N WEBER RD
RAMP 261
W MAIN ST
I-55 SB
I-55 NB
N WEBER RD
ROMEOVILLE
S WEBER RD
PLAINFIELD
W RENWICK RD
W RENWICK RD
S LINCOLN HWY
257
JOLIET
CREST HILL
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH88 (S Weber Rd) & CH36 (W Renwick Rd)
Will County Illinois
0
3,000
6,000
Feet
HRGreen

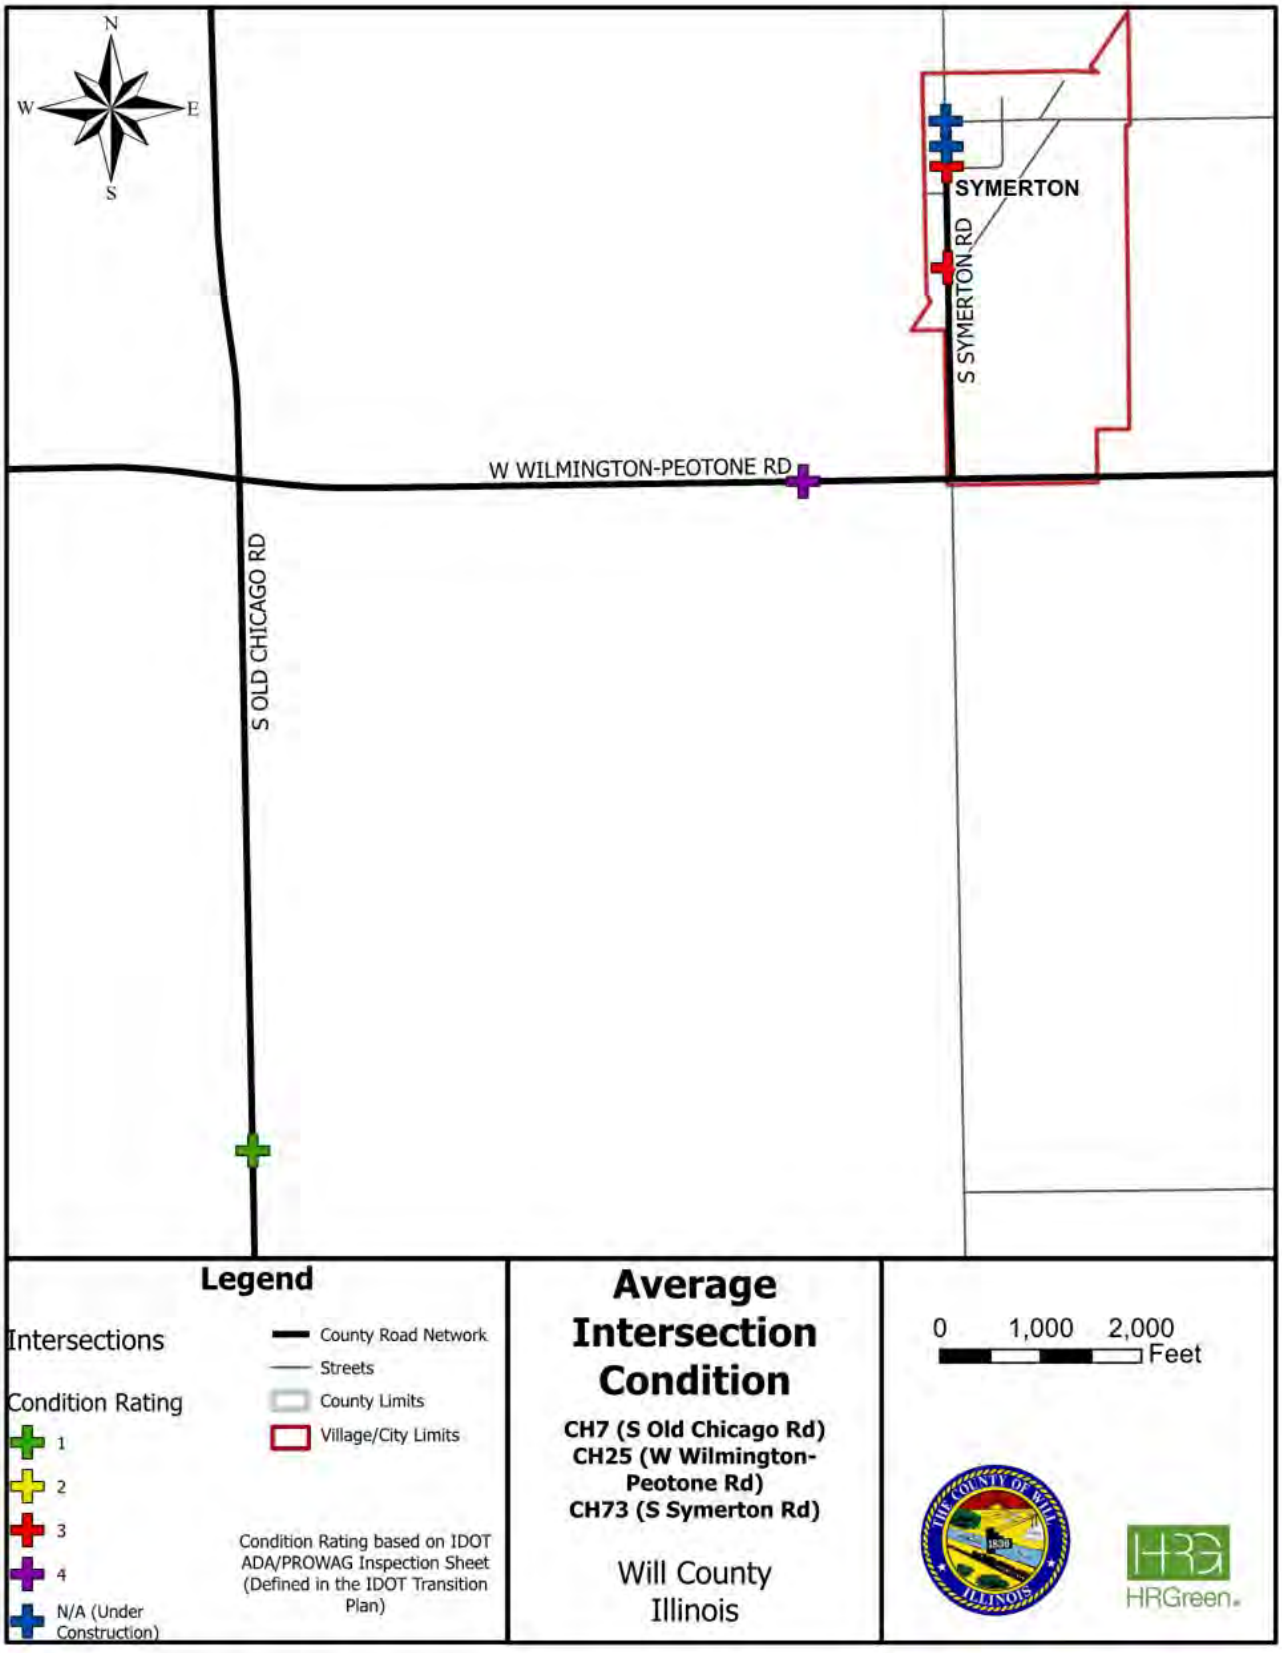
N
W
E
S
SYMERTON
S SYMERTON RD
W WILMINGTON-PEOTONE RD
S OLD CHICAGO RD
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH7 (S Old Chicago Rd)
CH25 (W Wilmington-Peotone Rd)
CH73 (S Symerton Rd)
Will County Illinois
0 1,000 2,000
Feet
HRGreen

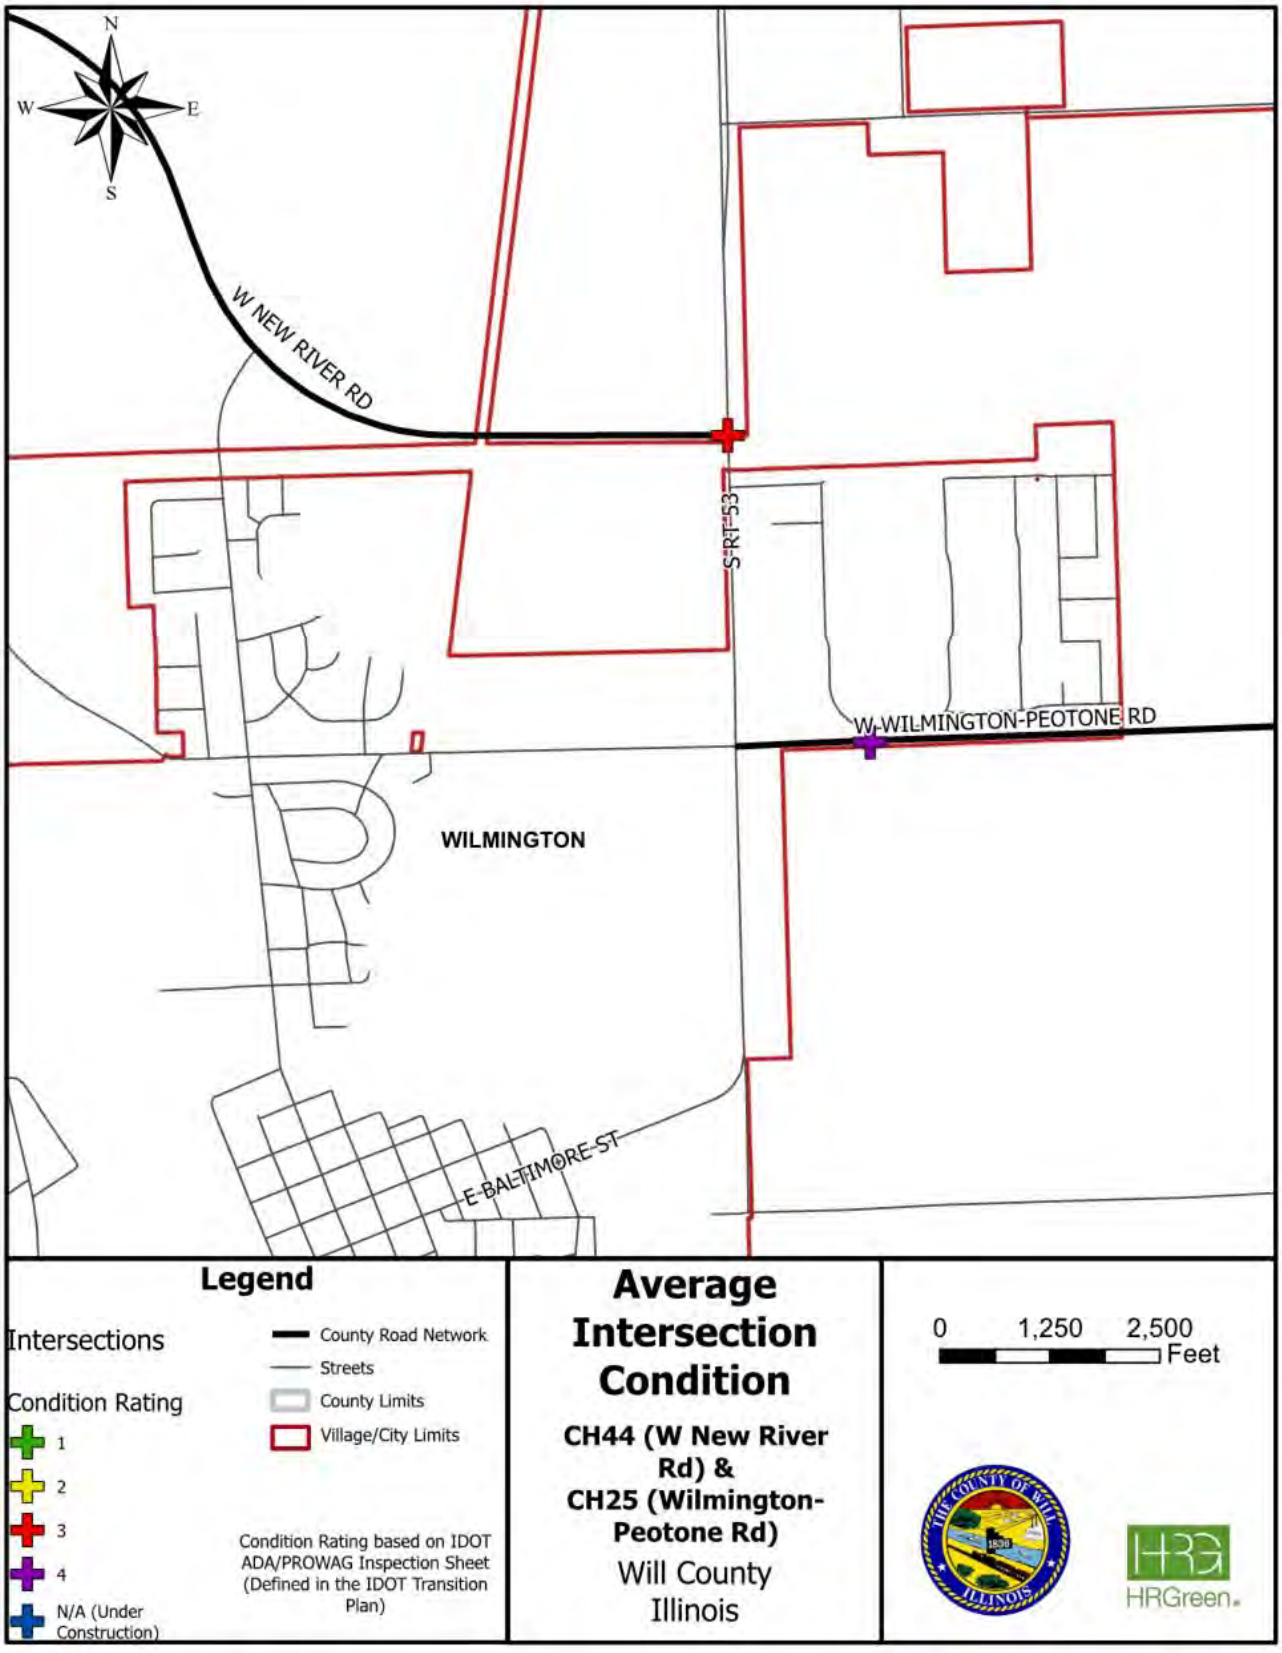
N
W
E
S
W NEW RIVER RD
S RT 53
W WILMINGTON-PEOTONE RD
WILMINGTON
E BALTIMORE ST
Legend
Intersections
Condition Rating
1
2
3
4
N/A (Under Construction)
County Road Network
Streets
County Limits
Village/City Limits
Condition Rating based on IDOT ADA/PROWAG Inspection Sheet (Defined in the IDOT Transition Plan)
Average Intersection Condition
CH44 (W New River Rd) &
CH25 (Wilmington-Peotone Rd)
Will County
Illinois
0
1,250
2,500
Feet
HRGreen

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH62	CH62_Z-110	WCDOT	5/8	5/8	4.3% - 2.7% cross slopes. 55' South of Cleveland.	2029	WCDOT GM
CH62	CH62_Z-111	WCDOT	1/4	2	47" width and 1" horizontal deficiency at curbside. 215' North of Belmont.	2029	WCDOT GM
CH62	CH62_Z-112	WCDOT	5/8	3/4	3.8% Cross slope. 80' South of Belmont.	2029	WCDOT GM
CH62	CH62_Z-113	WCDOT	1/2	3/4	Settling of concrete pads vertical deficiency of.75". 235' South of Belmont.	2029	WCDOT GM
CH62	CH62_Z-114	WCDOT	3/8	1 1/8	Vertical deficiency of 1.125". 185' North of Copperfield.	2029	WCDOT GM
CH62	CH62_Z-115	WCDOT	1/2	1	Concrete pad cut and replaced. 150' North of Copperfield.	2029	WCDOT GM
CH62	CH62_Z-116	WCDOT	1/4	1 1/8	Cracked pad. 105' South of Copperfield.	2029	WCDOT GM
CH62	CH62_Z-117	WCDOT	3 1/2	1 1/4	Missing corner. 115' South of Copperfield.	2029	WCDOT GM
CH62	CH62_Z-118	WCDOT	3/4	5/8	0.625" vertical deficiency. 160' South of Copperfield.	2029	WCDOT GM
CH62	CH62_Z-119	WCDOT	3/8	3/4	Vertical deficiency of .75". 190' South of Copperfield.	2029	WCDOT GM
CH62	CH62_Z-120	WCDOT	3/8	1	0.875" vertical deficiency. 345' South of Copperfield.	2029	WCDOT GM
CH62	CH62_Z-121	WCDOT	1/4	1 1/8	Concrete pad on North has fallen. 390' South of Copperfield.	2029	WCDOT GM
CH62	CH62_Z-122	WCDOT	1/2	3/4	Driveway. 405' South of Copperfield.	2029	WCDOT GM
CH62	CH62_Z-123	WCDOT	1/4	1	0.925" vertical deficiency. 415' South of Copperfield.	2029	WCDOT GM
CH62	CH62_Z-124	WCDOT	1/4	1	Piece of sidewalk missing 3"x2". 425' South of Copperfield.	2029	WCDOT GM
CH62	CH62_Z-125	WCDOT	1/4	3/4	Chipped Curb. Vertical deficiency of .75". 435' South of Copperfield.	2029	WCDOT GM
CH62	CH62_Z-126	WCDOT	1/4	5	Bad fault in sidewalk. 6.2% cross slope. 360' North of Elgin.	2029	WCDOT GM
CH62	CH62_Z-127	WCDOT	3/8	2	Vertical deficiency of 2.375". 355' North of Elgin.	2029	WCDOT GM
CH62	CH62_Z-128	WCDOT	1/8	1 3/4	Vertical deficiency of 1.75". 290' North of Elgin.	2029	WCDOT GM
CH62	CH62_Z-129	WCDOT	1/8	3/4	0.75" vertical deficiency. 275' North of Elgin.	2029	WCDOT GM
CH62	CH62_Z-130	WCDOT	1/4	1 1/4	between driveway beginning and sidewalk area. 160' North of Elgin.	2029	WCDOT GM
CH62	CH62_Z-131	WCDOT	1/4	1	0.75" vertical deficiency. 100' North of Elgin.	2029	WCDOT GM
CH62	CH62_Z-132	WCDOT	1/8	5/8	0.625" vertical deficiency. 45' South of Elgin.	2029	WCDOT GM
CH62	CH62_Z-133	WCDOT	1/4	5/8	0.625" vertical deficiency. 55' South of Elgin.	2029	WCDOT GM
CH62	CH62_Z-134	WCDOT	1/2	1 1/8	Sediment and vertical deficiency of 1.125" and sidewalk missing on south east corner. 305' South of Elgin.	2029	WCDOT GM
CH62	CH62_Z-135	WCDOT	3/8	5/8	0.625" vertical deficiency. 250' North of Sterling.	2029	WCDOT GM
CH62	CH62_Z-136	WCDOT	1/2	2 3/4	Water buffalo box middle of pad. 40' South of Sterling.	2029	WCDOT GM
CH62	CH62_Z-137	WCDOT	1/4	5/8	0.625" vertical deficiency. 170' South of Sterling.	2029	WCDOT GM
CH62	CH62_Z-138	WCDOT	1/2	3/4	0.75" vertical deficiency. 180' South of Sterling.	2029	WCDOT GM
CH62	CH62_Z-139	WCDOT	1	2	Concrete pad has cracks in the middle and his vertically deficiency of 2". 270' South of Sterling.	2029	WCDOT GM
CH62	CH62_Z-140	WCDOT	1/4	3/4	Deterioration also on the side. 285' South of Sterling.	2029	WCDOT GM
CH62	CH62_Z-141	WCDOT	3/8	1/2	0.5" vertical deficiency. 505' South of Sterling.	2029	WCDOT GM
CH62	CH62_Z-142	WCDOT	1/2	1 1/2	Sidewalk to beginning of sidewalk apron 1.5 vertical deficiency. 530' North of Cass.	2029	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH62	CH62_Z-143	WCDOT	1/2	1	1" vertical deficiency. 195' North of Cass.	2029	WCDOT GM
CH62	CH62_Z-144	WCDOT	1/4	1	1" vertical deficiency. 190' North of Cass.	2029	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH24	CH24_Z-101	Beecher	1	1	Numerous cracks and cross slope noncompliant. 195' East of Dunbar.	2023	WCDOT GM
CH24	CH24_Z-102	Beecher	1/4	1/2	Sidewalk has been ground down on north side of sidewalk south side has .5" vertical deficiency. 180' West of Elliott.	2023	WCDOT GM
CH24	CH24_Z-103	Beecher	2	3/4	The sidewalk area has numerous cracks and vertical deficiencies. 165' West of Elliott.	2023	WCDOT GM
CH24	CH24_Z-104	Beecher	1/4	1	0.2% cross slope. 115' West of Elliott.	2023	WCDOT GM
CH24	CH24_Z-105	Beecher	3/4	3/4	Sidewalk is deteriorating cracks and missing concrete. 90' West of Elliott.	2023	WCDOT GM
CH24	CH24_Z-106	Beecher	2	3/4	Concrete disintegrating and cracked, missing concrete. 75' West of Elliott.	2023	WCDOT GM
CH24	CH24_Z-107	Beecher	3/4	1/2	Concrete disintegrating cracked is noncompliant. 70' West of Elliott.	2023	WCDOT GM
CH24	CH24_Z-108	Beecher	2	1	Concrete disintegrating, cracks in concrete. 65' West of Elliott.	2023	WCDOT GM
CH24	CH24_Z-109	Beecher	1/8	5/8	1.3% cross slope. 50' West of Elliott.	2023	WCDOT GM
CH24	CH24_Z-110	Beecher	1 1/2	3/4	Numerous cracks and voids in sidewalk. 45' West of Elliott.	2023	WCDOT GM
CH24	CH24_Z-111	Beecher	1/4	1/2	1.3% cross slope. 100' East of Elliott.	2023	WCDOT GM
CH24	CH24_Z-112	Beecher	1/4	1 5/8	Collection of sediment and numerous cracks in sidewalk and driveway. 145' East of Elliott.	2023	WCDOT GM
CH24	CH24_Z-113	Beecher	1/4	3/4	1.6% cross slope. 165' East of Elliott.	2023	WCDOT GM
CH24	CH24_Z-114	Beecher	3/4	3/4	Concrete pad has deterioration at joint. 190' East of Elliot.	2023	WCDOT GM
CH24	CH24_Z-115	Beecher	2	1	Deterioration of concrete a joint. 200' East of Elliott.	2023	WCDOT GM
CH24	CH24_Z-116	Beecher	1 3/4	1	Three concrete pads in this area have numerous cracks and concrete missing. 135' West of Gould.	2023	WCDOT GM
CH24	CH24_Z-117	Beecher	1/8	3/8	North side of sidewalk has cracks. 120' West of Gould.	2023	WCDOT GM
CH24	CH24_Z-118	Beecher	1/4	3/4	1.9% cross slope. 65' west of Gould.	2023	WCDOT GM
CH24	CH24_Z-119	Beecher	3/4	3/4	Sidewalk has cracks and a vertical deficiency. 45' West of Gould.	2023	WCDOT GM
CH24	CH24_Z-120	Beecher	1/8	3/4	Concrete pads vertically deficient. 90' East of Gould.	2023	WCDOT GM
CH24	CH24_Z-121	Beecher	1/2	1	Cracks and vertical deficiencies have developed due to tree on south side of walk. 110' East of Gould.	2023	WCDOT GM
CH24	CH24_Z-122	Beecher			.3% cross slope. 355' West of Woodward.	2023	WCDOT GM
CH24	CH24_Z-123	Beecher	3/8	5/8	Cross slope is 3.9%. 315' West of Woodward.	2023	WCDOT GM
CH24	CH24_Z-124	Beecher	1/4	3/4	0.5% cross slope. 130' West of Woodward.	2023	WCDOT GM
CH24	CH24_Z-125	Beecher	1/8	3/4	1% cross slope. 120' West of Woodward.	2023	WCDOT GM
CH24	CH24_Z-126	Beecher	1/8	1 1/4	Concrete pads on west side of this joint have sloped towards clean out of drain, vertical deficiency 1". 100' West of Woodward.	2023	WCDOT GM
CH24	CH24_Z-127	Beecher	1/2	1/2	Concrete has cracked unevenly in middle of sidewalk. Numerous cracks. 90' West of Woodward.	2023	WCDOT GM
CH24	CH24_Z-128	Beecher	4	1 1/8	This area has a vertical deficiency on the east side. East has disintegrating concrete and a 3.5" horizontal deficiency. 75' West of Woodward.	2023	WCDOT GM
CH24	CH24_Z-129	Beecher	1/4	1 1/4	Patch was put on this joint but has missing concrete on south side of walk. 55' West of Woodward.	2023	WCDOT GM
CH24	CH24_Z-130	Beecher	9	1 1/2	This area of the sidewalk for approximately 30' broken and cracked BAD. 40' West of Woodward.	2023	WCDOT GM
CH24	CH24_Z-131	Beecher	1/2	3/4	Turning area top of ramp to north-south sidewalk high on west side low on east side. 40' East of Woodward.	2023	WCDOT GM
CH24	CH24_Z-132	Beecher	8	1 1/4	Concrete triangle section is falling down and cracked off. 100' East of Woodward.	2023	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH24	CH24_Z-133	Beecher	1/4	3/4	0.8% cross slope. 125' East of Woodward.	2023	WCDOT GM
CH24	CH24_Z-134	Beecher	1/4	1 1/8	0.1% cross slope. 150' East of Woodward.	2023	WCDOT GM
CH24	CH24_Z-135	Beecher	1/4	1 1/4	4.8% cross slope. 190' West of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-136	Beecher	5/8	1/2	3.6% cross slope. 130' West of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-137	Beecher	5/8	1 1/2	Newer concrete pad is compliant older pad is noncompliant on cross slope. 105' West of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-138	Beecher	1/2	1 1/2	Newer pad of concrete vertically deficient. 85' West of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-139	Beecher	5/8	1	1.1% cross slope. 65' East of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-140	Beecher	1/2	1	0.7% cross slope. 70' East of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-141	Beecher	1/3	3/4	0.9% cross slope. 75' East of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-142	Beecher	1/8	1	1.1% cross slope. 105' East of Woodward.	2023	WCDOT GM
CH24	CH24_Z-143	Beecher	3/4	3/4	Cracked pads. 110' East of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-144	Beecher	1/8	1 1/2	0.3% cross slope. 145' East of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-145	Beecher			1.2% cross slope. 150' East of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-146	Beecher			225' East of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-147	Beecher	1/8	1 1/4	2.3% cross slope. 255' East of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-148	Beecher	2	5/8	0.3% cross slope. 305' East of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-149	Beecher			350' East of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-150	Beecher	1/8	3/4	Sloped toward drain. 355' East of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-151	Beecher	1/8	5/8	3.9% cross slope. 380' East of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-152	Beecher	1/8	2	5.6% cross slope. 395' East of Maxwell.	2023	WCDOT GM
CH24	CH24_Z-153	Beecher			395' West of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-154	Beecher	1/8	3/4	Vertical deficiency. 245' West of Catalpa	2023	WCDOT GM
CH24	CH24_Z-155	Beecher	1/4	1	0.4% cross slope. 230' West of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-156	Beecher	3/8	1 1/4	2.9% cross slope. 195' West of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-157	Beecher	1/2	1 1/4	Sediment collected at base. 180' West of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-158	Beecher			145' west of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-159	Beecher			135' West of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-160	Beecher			110' West of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-161	Beecher	1/2	1 1/2	2.4% cross slope. 90' West of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-162	Beecher	1/8	1 1/2	3.5% cross slope. 85' West of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-163	Beecher			85' West of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-164	Beecher			70' West of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-165	Beecher			Chipped pad with vertical deficiency. 10' East of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-166	Beecher			65' East of Catalpa.	2023	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH24	CH24_Z-167	Beecher	1/2	1/2	Cracked concrete. 105' East of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-168	Beecher			110' East of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-169	Beecher			125' East of Catalpa.	2023	WCDOT GM
CH24	CH24_Z-170	Beecher	1/2	1 1/2	3.1% cross slope. 110' East of Prairie.	2023	WCDOT GM
CH24	CH24_Z-171	Beecher	1/2	1 1/4	0.3% cross slope. 150' East of Prairie.	2023	WCDOT GM
CH24	CH24_Z-172	Beecher			5.9% cross slope. 210' East of Prairie.	2023	WCDOT GM
CH24	CH24_Z-173	Beecher		3/4	2.7% cross slope. 425' East of Prairie.	2023	WCDOT GM
CH24	CH24_Z-174	Beecher	1/4	3/4	Vertical deficiency. 425' West of Dixie.	2023	WCDOT GM
CH24	CH24_Z-175	Beecher	1/4	1 5/8	0.3% cross slope. 400' West of Dixie.	2023	WCDOT GM
CH24	CH24_Z-176	Beecher	1	1	Curb and sediment built up with 2" concrete curb still protruding upward. 210' West of Dixie.	2023	WCDOT GM
CH24	CH24_Z-177	Beecher	4	1/4	Hole in sidewalk cracks 4"x 6' deteriorating area. 185' West of Dixie.	2023	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH88	CH88_Z-101	Bolingbrook	3/8	1	Vertical deficiency of .75". 70' South of Lily Cache.	2027	WCDOT GM
CH88	CH88_Z-102	Bolingbrook	1/4	1 5/8	Vertical deficiency of 1.5". 70 ' South of Lily Cache.	2027	WCDOT GM
CH88	CH88_Z-103	Bolingbrook	1/4	1	Vertical deficiency of .8125". 125' South of Lily Cache.	2027	WCDOT GM
CH88	CH88_Z-104	Bolingbrook	3/8	2	Drain with vertical deficiency of 2". 155' South of Lily Cache.	2027	WCDOT GM
CH88	CH88_Z-105	Bolingbrook	1/4	5/8	Vertical deficiency of .625". 170' South of Lily Cache.	2027	WCDOT GM
CH88	CH88_Z-106	Bolingbrook	1 1/2	3/8	Tree with vertical deficiency of 1.5". 190' South of Lily Cache.	2027	WCDOT GM
CH88	CH88_Z-107	Bolingbrook	1/2	1/4	Sediment in PAR. 235' South of Lily Cache.	2027	WCDOT GM
CH88	CH88_Z-108	Bolingbrook	1/4	1 1/4	Beginning of ramp. 220' North of Chanticleer.	2027	WCDOT GM
CH88	CH88_Z-109	Bolingbrook	1/4	3/4	Sediments on path. 220' North of Chanticleer.	2027	WCDOT GM
CH88	CH88_Z-110	Bolingbrook	3/8	3/4	Carriage walk to business. 185' North of Chanticleer.	2027	WCDOT GM
CH88	CH88_Z-111	Bolingbrook	5/8	3/4	Vertical deficiency of .75". 155' North of Chanticleer.	2027	WCDOT GM
CH88	CH88_Z-112	Bolingbrook	1/2	1 1/4	Vertical deficiency of 1.5". 120' North of Chanticleer.	2027	WCDOT GM
CH88	CH88_Z-113	Bolingbrook	3/8	3/4	Vertical deficiency of .75". 245' South of Chanticleer.	2027	WCDOT GM
CH88	CH88_Z-114	Bolingbrook	1/4	1	Settlement collecting in this area. 500' South of Chanticleer.	2027	WCDOT GM
CH88	CH88_Z-115	Bolingbrook	1/4	1	Vertical deficiency of 1". 445' North of Wingfield.	2027	WCDOT GM
CH88	CH88_Z-116	Bolingbrook	3/8	3/4	Vertical deficiency of .75". 420' North of Wingfield.	2027	WCDOT GM
CH88	CH88_Z-117	Bolingbrook	5/8	3/4	Adjacent sidewalk leading to business. 300' North of 111th.	2027	WCDOT GM
CH88	CH88_Z-118	Bolingbrook	1	1	Horizontal and vertical deficiency at adjacent sidewalk. 70' North of 111th.	2027	WCDOT GM
CH88	CH88_Z-119	Bolingbrook	1/2	3/4	Vertical deficiency of .625". 365' North of Parkside.	2027	WCDOT GM
CH88	CH88_Z-120	Bolingbrook	1/2	3/4	Vertical deficiency of .75". 235' North of Parkside.	2027	WCDOT GM
CH88	CH88_Z-121	Bolingbrook	1/4	1	Vertical deficiency of 1.25". 160' North of Parkside.	2027	WCDOT GM
CH88	CH88_Z-122	Bolingbrook		1	Vertical deficiency of ,925". 535' South of Parkside.	2027	WCDOT GM
CH88	CH88_Z-123	Bolingbrook	1	3/8	Cross slope of 3.8% with a horizontal gap of .75". 445' North of 115th.	2027	WCDOT GM
CH88	CH88_Z-124	Bolingbrook	1/4	1/4	Find line crack and sidewalk. 285' North of 115th.	2027	WCDOT GM
CH88	CH88_Z-125	Bolingbrook	1 1/2	1	Concrete on west side of manhole cracked and broken off falling toward street and vertical height difference manhole to sidewalk .75". 650' South of 115th.	2027	WCDOT GM
CH88	CH88_Z-126	Bolingbrook	5/8	3/4	Vertical deficiency of .75" and a horizontal gap of 5/8". 905' South of 115th.	2027	WCDOT GM
CH88	CH88_Z-127	Bolingbrook	1/4	1 1/2	Vertical deficiency of 1.5". 920' South of 115th.	2027	WCDOT GM
CH88	CH88_Z-128	Bolingbrook	3 1/2	4	Pot hole in walk. 940' South of 115th.	2027	WCDOT GM
CH88	CH88_Z-129	Bolingbrook	1/2	5/8	Manhole cover in PAR. 985' South of 115th.	2027	WCDOT GM
CH88	CH88_Z-130	Bolingbrook	5/8	5/8	Concrete corner missing new concrete as of 8-12-22. 1050' North of Remington.	2027	WCDOT GM
CH88	CH88_Z-131	Bolingbrook			Fractured concrete. 120' North of Remington.	2027	WCDOT GM
CH14	CH14_Z-169	Bolingbrook		1	Branches from tree in PAR 70" from ground. 690' South of 111th.	2023	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH14	CH14_Z-172	Bolingbrook	1	1/4	Running slope on walk is 7.8% for 15' downslope to storm drain area. 2220' North of W 127th.	2023	WCDOT GM
CH14	CH14_Z-173	Bolingbrook	1		Cross slope is draining to culvert area at 4.2% most of the sidewalk is failing. 2085' North of W 127th.	2023	WCDOT GM
CH89	CH89_Z-112	Bolingbrook			Asphalt has been applied to try to alleviate trip hazard but is settled approximately 1" vertically away from bridge. 880' North of Alan Deathrage.	2028	WCDOT GM
CH89	CH89_Z-113	Bolingbrook	3/4		Horizontal gap of .5". 865' North of Alan Deathrage.	2028	WCDOT GM
CH89	CH89_Z-114	Bolingbrook			Cracked and chipped pads with a horizontal gap of 2.5" and a vertical deficiency of 2". 845' North of Alan Deathrage.	2028	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH32	CH32_Z-104	Channahon	1 1/4	1/8	Horizontal gap of 2". 660' South of W McGowan Woods.	2025	Local
CH32	CH32_Z-105	Channahon	1 3/4		1.4% cross slope. 700' North of Mohawk.	2025	Local
CH32	CH32_Z-106	Channahon	1		0.8% cross slope. 650' North of Mohawk.	2025	Local
CH32	CH32_Z-107	Channahon	1 3/4	1 1/2	Asphalt crack is deteriorating on east side of bike path more than the west, pictures taken. 550' North of Mohawk.	2025	Local
CH32	CH32_Z-108	Channahon	1 1/4	1 1/2	Asphalt is collapsing towards culvert on east side and collapsing on west side has been sealed and weed accumulation in joint. 520' North of Mohawk.	2025	Local
CH32	CH32_Z-109	Channahon	1 1/4	1	Asphalt joint which is deteriorating in collapsing towards the middle of joint. 465' North of Mohawk.	2025	Local
CH32	CH32_Z-110	Channahon		2	This is a concrete island which is 1' in the middle of driveway and crosswalk asphalt has sunk down due to drain. 240' North of Mohawk.	2025	Local
CH32	CH32_Z-111	Channahon	1 1/4	1/4	Pathway sloping from east to west and 4.7% angle on a severe pitch towards phone box. 200' North of Mohawk.	2025	Local
CH32	CH32_Z-112	Channahon	2	1/2	Expansion of asphalt bike path collapsing. 50' North of Mohawk.	2025	Local
CH32	CH32_Z-113	Channahon	1	1	Trees roots are causing a vertical deficiency, bike path area and slope of walk is 5.2%. 250' South of Mohawk.	2025	Local
CH32	CH32_Z-114	Channahon			2.9% cross slope. 345' South of Mohawk.	2025	Local
CH32	CH32_Z-115	Channahon	1		1" horizontal gap. 80' South of Crowfoot.	2025	Local
CH32	CH32_Z-116	Channahon		1	Pothole by area 12"x14". Cross slope is 3.6%. 250' East of S Potawatomie.	2025	Local
CH32	CH32_Z-117	Channahon		1 3/4	Pothole in the area approximately 3'x4' and 16" wide. 300' East of S Potawatomie.	2025	Local
CH32	CH32_Z-118	Channahon	1	1	Concrete pad to the north of this inspection joint has vertical and horizontal deficiencies. 105' North of W McCowan.	2025	Local
CH32	CH32_Z-119	Channahon		1 1/4	Concrete pads north of this area settled approximately 1.75" and sloping from that point to 5.8% proximately 8' away. 60' North of W McCowan.	2025	Local
CH32	CH32_Z-120	Channahon			This area is in question because of sidewalk sloping off into culvert area which is filled with stone. 280' South of W McCowan.	2025	Local

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH49	CH49_Z-101	Crete	1/4	1 3/8	Vertical deficiency of concrete pad, south side of walkway. 1730' West of Independence.	2028	Local
CH49	CH49_Z-102	Crete	3/8	5/8	0.5% cross slope. 1650' West of Independence.	2028	Local
CH49	CH49_Z-103	Crete	3/8	5/8	2.3% cross slope. 1625' West of Independence.	2028	Local
CH49	CH49_Z-104	Crete	1/2	5/8	2.7% cross slope. 1610' West of Independence.	2028	Local
CH49	CH49_Z-105	Crete	1/4	1	1.8% cross slope. 1600' West of Independence.	2028	Local
CH49	CH49_Z-106	Crete	1/4	3/4	Deterioration on both sides of joint and vertical deficiency. 1405' West of Independence.	2028	Local
CH49	CH49_Z-107	Crete	3/8	3/4	Manhole on north side of pathway has a vertical deficiency sidewalk PAR is approximately 44". 1395' West of independence.	2028	Local
CH49	CH49_Z-108	Crete	3/8	1/2	Running slope 3.3%. 1355' West of Independence.	2028	Local
CH49	CH49_Z-109	Crete	1/4	1 1/4	4% cross slope. 1280' West of Independence.	2028	Local
CH49	CH49_Z-110	Crete	3/4	1/2	Crack on East 1/3 of concrete pad deterioration. 1165' West of Independence.	2028	Local
CH49	CH49_Z-111	Crete	1/8	1	Beginning 30" of sidewalk sloping towards culvert heading east. 960' West of Independence.	2028	Local
CH49	CH49_Z-112	Crete	1/4	3/4	Concrete pads headed west sloping towards Culvert. 930' West of Independence.	2028	Local
CH49	CH49_Z-113	Crete	1/4	3/4	3.3% cross slope. 815' West of Independence.	2028	Local
CH49	CH49_Z-114	Crete	1/4	1/2	3.2% cross slope. 805' West of Independence.	2028	Local
CH49	CH49_Z-115	Crete	1 1/8	1/8	vertical and horizontal deficiencies at top of ramp. 55' West of Independence.	2028	Local
CH49	CH49_Z-116	Crete	1/4	3/4	Chipped pad. 60' East of Independence.	2028	Local
CH49	CH49_Z-117	Crete	1	1/4	Cracks along water valve and sloping of concrete to valve. 350 East of Independence.	2028	Local
CH49	CH49_Z-118	Crete	3/4	3/4	Sidewalk has a vertical deficiency at manhole, cracks at valve and manhole. 35' East of Sangamon.	2028	Local
CH49	CH49_Z-119	Crete	1/2	1	0.5% cross slope. 150' West of Peoria.	2028	Local
CH49	CH49_Z-120	Crete	1/4	1/2	2% cross slope. 100' West of Peoria.	2028	Local
CH49	CH49_Z-121	Crete	1/4	1	5.1% cross slope. 10' East of Peoria.	2028	Local
CH49	CH49_Z-122	Crete	2	1 1/8	Chipped concrete approximately 4" x 6"□. 40' East of Peoria.	2028	Local
CH49	CH49_Z-123	Crete	5/8	3/4	2.7% cross slope. 75' East of Peoria.	2028	Local
CH49	CH49_Z-124	Crete	1/4	1 1/8	Concrete pad has severe deterioration and vertical deficiencies. 210' East of Peoria.	2028	Local
CH49	CH49_Z-125	Crete	1/2	3/4	2.2% cross slope. 210' West of Washington.	2028	Local
CH49	CH49_Z-126	Crete	1/4	5/8	0.3% cross slope. 150' West of Washington.	2028	Local
CH49	CH49_Z-127	Crete	1/4	1	2.9% cross slope. 120' West of Washington.	2028	Local
CH49	CH49_Z-128	Crete	1/2	5/8	0.9% cross slope. 120' West of Washington.	2028	Local
CH49	CH49_Z-129	Crete	1/8	1	1.2% cross slope. 45' West of Washington.	2028	Local
CH49	CH49_Z-130	Crete	1/4	3/4	3.8 % cross slope at manhole. 200' East of Washington.	2028	Local
CH49	CH49_Z-131	Crete	1/4	3/4	Cross slope on sidewalk noncompliant. Transition between bridge and sidewalk area 1.75" vertical deficiency. 210' West of Lincoln.	2028	Local
CH49	CH49_Z-132	Crete	1/8	3/4	4.1% cross slope. 200' West of Lincoln.	2028	Local

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH49	CH49_Z-133	Crete	1/8	3/4	5.9% cross slope and only 59" wide. 140' West of Lincoln.	2028	Local
CH49	CH49_Z-134	Crete	1/2	2	Concrete has settled in this corner from here to corner. 30' East of Lincoln.	2028	Local
CH49	CH49_Z-135	Crete	1/4	5/8	Sidewalk is only 58.5" to curb from wall also concrete missing patch 6" x 8" wide. 50' East of Lincoln.	2028	Local
CH49	CH49_Z-136	Crete	1/4	1/2	Concrete disintegrating many pockmarks throughout sidewalk area. 30' East of Columbia.	2028	Local
CH49	CH49_Z-137	Crete	1 1/2	3/4	Cross slope 3.1%. 120' East of Vincennes.	2028	Local
CH49	CH49_Z-138	Crete	3	1 1/4	Vertical deficiency in concrete pads and a section concrete approximate 6" x 2". 145' West of Lumber.	2028	Local
CH49	CH49_Z-139	Crete	1/2	1/2	Crack running perpendicular to PAR. 125' West of Lumber.	2028	Local
CH49	CH49_Z-140	Crete	1/8	1	1.3% cross slope. 105' West of Lumber.	2028	Local
CH49	CH49_Z-141	Crete	1 3/4	1/2	Deterioration of concrete pad cracked. 185' East of Lumber.	2028	Local
CH49	CH49_Z-142	Crete	1 1/4	1/2	Water control shut off in middle of sidewalk deterioration around cover. 200' West of Benton.	2028	Local
CH49	CH49_Z-143	Crete	3	1 1/2	Corner of concrete sidewalk missing. 175' West of Benton.	2028	Local
CH49	CH49_Z-144	Crete	1	1/8	Horizontal crack of 1" running with PAR, utility pole patch. 160' West of Benton.	2028	Local
CH49	CH49_Z-145	Crete	1/4	1/2	Water manhole cover lower than sidewalk. 120' West of Benton.	2028	Local
CH49	CH49_Z-146	Crete	2 1/2	2	Deterioration of concrete pad at water manhole. 100' West of Benton.	2028	Local
CH49	CH49_Z-147	Crete	1 1/2	3/4	Concrete deterioration at joint. 100' West of Benton.	2028	Local
CH49	CH49_Z-148	Crete	1/4	1/2	3.9% cross slope. 95' West of Benton.	2028	Local
CH49	CH49_Z-149	Crete	3/4	5/8	6.1% cross slope. 80' West of Benton.	2028	Local
CH49	CH49_Z-150	Crete	2 1/2	5/8	Deterioration of corner of pad is filled with sediment. 75' West of Benton.	2028	Local
CH49	CH49_Z-151	Crete	1/8	5/8	3.4% cross slope. 45' West of Benton.	2028	Local
CH49	CH49_Z-152	Crete	1/8	1/2	8.3% cross slope. 90' East of Benton.	2028	Local
CH49	CH49_Z-153	Crete	1/4	5/8	Asphalt patch in par cross slope 11.6%. 110' East of Benton.	2028	Local
CH49	CH49_Z-154	Crete	1/4	1/2	Asphalt patch in PAR and sediment at roadside curb and sidewalk. 130' East of Benton.	2028	Local
CH49	CH49_Z-155	Crete	1/4	5/8	3.7% cross slope. 145' East of Benton.	2028	Local
CH49	CH49_Z-156	Crete	3	1	Asphalt patch in PAR with sediment. 150' East of Benton.	2028	Local
CH49	CH49_Z-157	Crete	2	1 1/4	Deterioration at beginning of driveway ramp. 160' East of Benton.	2028	Local
CH49	CH49_Z-158	Crete	1/4	3/4	Cross slope 9.6% and cracked driveway. 115' West of Main.	2028	Local
CH49	CH49_Z-159	Crete	1/4	3/4	Middle of driveway. 110' West of Main.	2028	Local
CH49	CH49_Z-160	Crete	1/4	3/4	Sediment built up on east side of pad. 90' West of Main.	2028	Local
CH49	CH49_Z-161	Crete	1/4	2	Numerous deficiencies on the sidewalk in this area. 70' West of Main.	2028	Local
CH49	CH49_Z-162	Crete	1/4	1	Numerous deficiencies in this area. 50' West of Main.	2028	Local
CH49	CH49_Z-163	Crete	1/4	3/4	Numerous deficiencies in this area. 40' West of Main.	2028	Local
CH49	CH49_Z-164	Crete	1/4	1 1/4	Beginning pad at edge of the driveway. 65' East of Main.	2028	Local
CH49	CH49_Z-165	Crete	1/4	1	5.3% cross slope. 150' East of Main.	2028	Local
CH49	CH49_Z-166	Crete	3/4	5/8	1.6% cross slope. 160' East of Main.	2028	Local

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH49	CH49_Z-167	Crete	3/4	3/4	Cracked sidewalk pad. 170' East of Main.	2028	Local
CH49	CH49_Z-168	Crete	3/4	3/4	Driveway opening. 150' West of Wood.	2028	Local
CH49	CH49_Z-169	Crete	1/4	1	6.6% cross slope. 145' West of Wood.	2028	Local
CH49	CH49_Z-170	Crete	3/4	1 1/4	Concrete pads vertical and horizontal deficiencies. 135' West of Wood.	2028	Local
CH49	CH49_Z-171	Crete	1/2	1 3/8	9.5% cross slope. 110' West of Wood.	2028	Local
CH49	CH49_Z-172	Crete	1/4	1	7.1% cross slope. 45' West of Wood.	2028	Local
CH49	CH49_Z-173	Crete	1/4	3/4	5% cross slope. 90' East of Wood.	2028	Local
CH49	CH49_Z-174	Crete	1/2	3/4	Beginning of driveway has cracked sidewalk section. 175' West of Elizabeth.	2028	Local
CH49	CH49_Z-175	Crete	1	3/4	Concrete patch on sidewalk horizontal deficient. 110' West of Elizabeth.	2028	Local
CH49	CH49_Z-176	Crete	1/4	3/4	1.5% cross slope. 80' East of Elizabeth.	2028	Local
CH49	CH49_Z-177	Crete	1/4	3/4	3.2% cross slope. 65' East of Park.	2028	Local
CH49	CH49_Z-178	Crete	1/4	1 1/4	1.4% cross slope. 70' East of Park.	2028	Local
CH49	CH49_Z-179	Crete	1/4	1 1/8	Cracked Sidewalk pad. 75' East of Park.	2028	Local
CH49	CH49_Z-180	Crete	3/8	1	1.3% cross slope. 80' East of Park.	2028	Local
CH49	CH49_Z-181	Crete	3/8	5/8	0.4% cross slope. 145' East of Park.	2028	Local
CH49	CH49_Z-182	Crete	1/4	1 1/4	4.3% cross slope. 145' East of Park.	2028	Local
CH49	CH49_Z-183	Crete	1/4	5/8	5.9% cross slope. 35' West of Selleck.	2028	Local
CH49	CH49_Z-184	Crete	1/4	5/8	4% cross slope. 25' East of Selleck.	2028	Local
CH49	CH49_Z-185	Crete	1	1/2	0.4% cross slope. 10' West of Perry.	2028	Local
CH49	CH49_Z-186	Crete	3/4	1 1/4	1.6% cross slope. 105' East of Perry.	2028	Local
CH49	CH49_Z-187	Crete	1/4	1 1/4	0.9% cross slope. 120' West of East St.	2028	Local
CH49	CH49_Z-188	Crete	1/4	1	0.9% cross slope. 105' West of East St.	2028	Local
CH49	CH49_Z-189	Crete	1/4	1 3/4	3% cross slope. 55' West of East St.	2028	Local
CH49	CH49_Z-190	Crete	1 1/4	1	1" vertical deficiencies and cracked in middle. 45' West of East St.	2028	Local
CH49	CH49_Z-191	Crete	1/4	1/2	0.6% cross slope. 35' East of East St.	2028	Local
CH49	CH49_Z-192	Crete	1/4	3/4	0.75" vertical deficiency. 160' East of East St.	2028	Local
CH49	CH49_Z-193	Crete	3/4	1 1/4	Edge of driveway. 190' West of Wood St.	2028	Local

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH74	CH74_Z-100	Frankfort	1/2		2.6% cross slope. 1105' East of S 80th.	2028	5 Year Plan
CH74	CH74_Z-101	Frankfort	1/2	1 3/8	Sidewalk is sloping on west concrete pad, 1.5" vertical deficiency. 1125' East of S 80th.	2028	5 Year Plan
CH74	CH74_Z-102	Frankfort		1/2	Cross slope 6.25% towards culvert. 1345' East of S 80th.	2028	5 Year Plan
CH74	CH74_Z-103	Frankfort	5/8	1 1/8	Vertical deficiency on top side of sidewalk 1.125" horizontal deficiency .625". 1560' East of S 80th.	2028	5 Year Plan
CH74	CH74_Z-104	Frankfort	5/8	1/4	Joint next to manhole cover has .625" horizontal deficiency and a perpendicular crack. 1535' West of Majestic.	2028	5 Year Plan
CH74	CH74_Z-105	Frankfort	1/2	1 1/4	Concrete pad on east side is 1.25" higher than west. 1440' West of Majestic.	2028	5 Year Plan
CH74	CH74_Z-106	Frankfort	3/4	3/4	3% cross slope. 1215' West of Majestic.	2028	5 Year Plan
CH74	CH74_Z-107	Frankfort	1/2	1/2	The concrete pads have numerous cracks and are deteriorating. 970' West of Majestic.	2028	5 Year Plan
CH74	CH74_Z-108	Frankfort	1 1/2	1 1/2	Two concrete pads severely broken with hole on north side of pad. 925' west of Majestic.	2028	5 Year Plan
CH74	CH74_Z-109	Frankfort	1 1/4	3/4	Transition between new and old concrete cross slope is 5.5%. 900' West of Majestic.	2028	5 Year Plan
CH74	CH74_Z-110	Frankfort	1/4	1/4	Concrete pad has a small crack. 545' West of 96th.	2028	5 Year Plan
CH74	CH74_Z-111	Frankfort	1	1 3/4	Very bad cracking and vertical deficiency of sidewalk. 70' West of S La Grange.	2028	5 Year Plan
CH74	CH74_Z-112	Frankfort	1/2	3/4	0.2% cross slope. 130' West of S La Grange.	2028	5 Year Plan
CH74	CH74_Z-113	Frankfort	1/2	1	vertical joint has tried to be modified (ground down) picture taken 170' West of S La Grange..	2028	5 Year Plan
CH74	CH74_Z-114	Frankfort	1	1	Pothole patch that has vertical deficiency in this area. 125' East of Regency..	2028	5 Year Plan
CH74	CH74_Z-115	Frankfort	1/4	1	This area also has a tree which is growing to approximate 70" vertical clearance. 30' East of Regency.	2028	5 Year Plan
CH74	CH74_Z-116	Frankfort	1/2	1/2	Joint has been ground down to try to make compliant. 540' West of Heritage.	2028	5 Year Plan
CH74	CH74_Z-117	Frankfort	1/4	3/4	Vertical difference of 1" on north side of sidewalk. 560' West of Heritage.	2028	5 Year Plan
CH74	CH74_Z-118	Frankfort	5/8	3/4	Concrete pad has been ground down to be compliant. 620' West of heritage.	2028	5 Year Plan
CH74	CH74_Z-119	Frankfort	1/2	1/2	3.4% cross slope. 640' West of Heritage.	2028	5 Year Plan
CH74	CH74_Z-120	Frankfort	1/3	3/4	Concrete pad is low on south side and high on north side .75". 270' East of Wolf.	2028	5 Year Plan
CH74	CH74_Z-121	Frankfort	1/2	3/4	1.7% cross slope. 260' East of Wolf.	2028	5 Year Plan
CH74	CH74_Z-122	Frankfort	1/4	1 1/4	3.2% cross slope. 140' East of Wolf.	2028	5 Year Plan
CH74	CH74_Z-123	Frankfort	1/4	1 1/2	This side where concrete pad has been ground down but on north side has .75" vertical deficiency. 115' East of Wolf.	2028	5 Year Plan
CH74	CH74_Z-124	Frankfort	1/4	1 1/4	Concrete pad has settled next to AT&T underground cable box south side of 1.75" vertical deficiency on south side. 100' East of Wolf.	2028	5 Year Plan
CH74	CH74_Z-125	Frankfort		1 1/8	Sidewalk reaching to top of ramp has vertical deficiency of 1.25" and has been ground down to make compliant. 60' West of Wolf.	2028	5 Year Plan
CH74	CH74_Z-126	Frankfort	1/2	1/2	3.1% cross slope. 90' West of Wolf.	2028	5 Year Plan
CH74	CH74_Z-127	Frankfort	1/4	1	2.8% cross slope. 95' West of Wolf.	2028	5 Year Plan
CH74	CH74_Z-128	Frankfort	1/3	1/2	Crack along concrete pad in line with manhole cover. 120' West of Wolf.	2028	5 Year Plan
CH74	CH74_Z-129	Frankfort	1/4	3/4	60" wide. 160' West of Wolf.	2028	5 Year Plan
CH74	CH74_Z-130	Frankfort	1/4	1/4	Concrete pad has 16' x 24" section that has cracked. 185' West of Wolf.	2028	5 Year Plan
CH74	CH74_Z-131	Frankfort	1	1	Concrete to west has vertical deficiency of 1". 635' West of Wolf.	2028	5 Year Plan

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH74	CH74_Z-132	Frankfort	1/4	2	This has a buffalo box cover with 2" vertical deficiency. Concrete sidewalk has cracked and sloping towards fire hydrant. 645' West of Wolf.	2028	5 Year Plan
CH74	CH74_Z-133	Frankfort	1	1 3/4	Manhole in middle of PAR has horizontal and vertical deficiencies >1". 660' West of Wolf.	2028	5 Year Plan
CH74	CH74_Z-134	Frankfort	1/4	1/2	Vertical deficiency of .5". 750' West of Wolf.	2028	5 Year Plan
CH74	CH74_Z-135	Frankfort	1/8	5/8	2.3% cross slope. 815' West of Wolf.	2028	5 Year Plan
CH74	CH74_Z-136	Frankfort	1/4	5/8	0.1% cross slope. 1075' West of Wolf.	2028	5 Year Plan
CH74	CH74_Z-137	Frankfort	1/8	3/4	Horizontal deficiency in the sidewalk perpendicular to PAR .75" wide. 1305' West of Wolf.	2028	5 Year Plan
CH74	CH74_Z-138	Frankfort	1/8	1/8	Hairline fractures forming in this area. 1235' East of 116th.	2028	5 Year Plan
CH74	CH74_Z-139	Frankfort	5/6	1/2	Manhole halfway in sidewalk .5" vertical and .75" horizontal deficiency. 45' West of 116th.	2028	5 Year Plan
CH74	CH74_Z-140	Frankfort	1/2	3/4	Sidewalk has cracked deterioration approximately 45"x 2'□along concrete joint. 45' West of Ledgestone.	2028	5 Year Plan
CH74	CH74_Z-141	Frankfort	4	1/2	Southwest corner of sidewalk pad at turning area has deteriorated. 35' West of Ledgestone.	2028	5 Year Plan

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH4	CH4_Z-101	Homer Glen	3/4	5/8	Concrete in south side has a vertical deficiency .625". 630' North of W 163rd.	2028	Local
CH4	CH4_Z-102	Homer Glen	1/4	5/8	Concrete pad has a vertical deficiency of .625" on each side south side pad lower the north side. 510' North of W 163rd.	2028	Local
CH4	CH4_Z-103	Homer Glen	1/8	5/8	Concrete pad on South has a vertical deficiency .5". 450' North of W 163rd.	2028	Local
CH4	CH4_Z-104	Homer Glen	1/2	1 1/4	Asphalt has a vertical deficiency of 1.25 ". 90' West of S Syd Creek.	2028	Local
CH16	CH16_Z-101	Homer Glen	1/4	3/4	This area sidewalk has vertical deficiencies towards street area approximately 7" long x 3" wide causing PAR to be noncompliant and north approximately 2' is a section of concrete12"x6" also missing. 65' North of W Glengary.	2028	Local
CH16	CH16_Z-102	Homer Glen		5/8	4.6% Cross slope with vertical deficiency of .5". 220' South of W Glengary.	2028	Local
CH16	CH16_Z-103	Homer Glen	1/4	1 5/8	Sidewalk has a vertical deficiency of 1.625" on the east side. 290' South of W Glengary.	2028	Local
CH16	CH16_Z-104	Homer Glen		1	Cross slope of 3% with vertical deficiency of .9375". 370' South of W Glengary.	2028	Local
CH16	CH16_Z-105	Homer Glen		1/2	0.5" vertical deficiency at manhole and cracking of walk. 380' South of W Glengary.	2028	Local
CH37	CH37_Z-102	Homer Glen		1 3/4	This area between curb ramp areas concrete pad has a vertical deficiency of 1.75". 25' West of Mallard.	2028	Local
CH37	CH37_Z-103	Homer Glen		1 1/2	Concrete pad between curb ramp area has a vertical deficiency of 1.5". 25' West of Mallard.	2028	Local
CH37	CH37_Z-104	Homer Glen		1 1/2	This triangular area between crosswalks has a vertical deficiency of 1.75" around perimeter compared to curbs. 20' East of Mallard.	2028	Local
CH37	CH37_Z-105	Homer Glen		1 3/4	Concrete pad between curb ramps have a vertical deficiency of 1.75" perimeter. 20' East of Mallard.	2028	Local
CH37	CH37_Z-106	Homer Glen	1/2	3/4	Vertical deficiency of .75" on north side of path. 80' Cook.	2028	Local
CH37	CH37_Z-101	Homer Glen	5/8	3/4	Concrete pad has vertical and horizontal deficiencies and a section of walk is missing 3"x6". 1225' West of S Gougar.	2028	Local

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH5_	CH5_Z-101	Joliet		3/4	Vertical deficiency of .75". 855' West of Golfview.	2032-2037	Local
CH5_	CH5_Z-102	Joliet		5/8	Vertical deficiency of .625". 875' East of Essington.	2032-2037	Local
CH5_	CH5_Z-103	Joliet		5/8	Vertical deficiency of .625". 750' East of Essington.	2032-2037	Local
CH5_	CH5_Z-104	Joliet	1		Horizontal gap .625" - 1". 650' East of Essington.	2032-2037	Local
CH5_	CH5_Z-105	Joliet	1/2		Horizontal gap .5". 640' East of Essington.	2032-2037	Local
CH5_	CH5_Z-106	Joliet		1 1/2	Vertical deficiency of 1.25". 620' East of Essington.	2032-2037	Local
CH5_	CH5_Z-107	Joliet		3/4	Vertical deficiency of .75". 600' East of Essington.	2032-2037	Local
CH5_	CH5_Z-108	Joliet		1 1/4	Vertical deficiency of .875". 460' East of Essington.	2032-2037	Local
CH5	CH5_Z-109	Joliet		7/8	Vertical deficiency of .875". 250' East of Essington.	2032-2037	Local
CH5	CH5_Z-110	Joliet		3/4	Vertical deficiency of .75". 150' East of Essington.	2032-2037	Local
CH5	CH5_Z-111	Joliet		1	Vertical deficiency of .9375". 140' East of Essington.	2032-2037	Local
CH5	CH5_Z-112	Joliet			Chipped pad 3.25" wide. 90' East of Essington.	2032-2037	Local
CH51	CH51_Z-101	Joliet	1/4	1 3/4	Concrete pad approximately 7' x 6" has vertical deficiency of 2' to the south near fire hydrant newly installed Pole in this area. 5' East of Pawnee	2032-2037	Local
CH51	CH51_Z-102	Joliet	1	2	This area is the sidewalk driveway area which is deteriorated and sediment and gravel has built up. 150' East of Pequot.	2032-2037	Local
CH51	CH51_Z-103	Joliet	1/4	1/2	0.5" vertical deficiency. 30' East of Pequot.	2032-2037	Local
CH52	CH52_Z-101	Joliet	3/4	2/5	2.3% cross slope. 625' South of W Maple.	2032-2037	Local
CH52	CH52_Z-102	Joliet	5/8	1/2	3.3% cross slope. 735' South of W Maple.	2032-2037	Local
CH52	CH52_Z-103	Joliet	5/8	1/2	3.3% cross slope. 760' South of W Maple.	2032-2037	Local
CH52	CH52_Z-104	Joliet	1/4	5/8	3.2% cross slope. 800' South of W Maple.	2032-2037	Local
CH52	CH52_Z-105	Joliet	5/8	1/2	Vertical deficiency .5" on north south. 805' North of Golf.	2032-2037	Local

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH4	CH4_Z-105	Lockport	1/8	1/2	Concrete pad to south of joint has a vertical deficiency of .5". 30' South of W Victoria.	2027	WCDOT GM
CH4	CH4_Z-106	Lockport	1/4	1/2	Area has vertical deficiency of.5". 70' South of W Victoria.	2027	WCDOT GM
CH4	CH4_Z-107	Lockport	1/4	1/2	Concrete pad north has vertical deficiency of .5" and is sloping towards houses in a noncompliant percentage. 275' South of W Victoria.	2027	WCDOT GM
CH4	CH4_Z-108	Lockport	3/4	1/2	Sidewalk is sloping toward pond area cross slope 3.1%. 210' North of W Ashton.	2027	WCDOT GM
CH4	CH4_Z-109	Lockport	3/4	1/8	0.75" horizontal deficiency. 45' South of W Ashton.	2027	WCDOT GM
CH62	CH62_Z-101	Lockport	5/8	1	Vertical deficiency of .925". 190' North of Neuberry Ridge.	2029	WCDOT GM
CH62	CH62_Z-102	Lockport	1/2	3/4	Cross slope 1%. 150' North of Neuberry Ridge.	2029	WCDOT GM
CH62	CH62_Z-103	Lockport	1/2	1	Cracked pavement. 350' South of Neuberry Ridge.	2029	WCDOT GM
CH62	CH62_Z-104	Lockport	1 1/2	1 1/2	Cracked pavement with a 1.5" gap. 485' South of Neuberry Ridge.	2029	WCDOT GM
CH62	CH62_Z-105	Lockport	1 3/8	1/4	Cracked pavement. 615' South of Neuberry Ridge.	2029	WCDOT GM
CH62	CH62_Z-106	Lockport	1	1/4	Cracked pavement. 710' South of Neuberry Ridge.	2029	WCDOT GM
CH62	CH62_Z-107	Lockport	1 1/2	1/4	Cracked pavement. 805' South of Neuberry Ridge.	2029	WCDOT GM
CH62	CH62_Z-108	Lockport	1 3/4	1 1/2	Cracked pavement. 825' South of Neuberry Ridge.	2029	WCDOT GM
CH62	CH62_Z-109	Lockport	5/8		Cracked pavement with plants growing on it. 990' South of Neuberry Ridge.	2029	WCDOT GM
CH75	CH75_Z-101	Lockport	1 3/4		Tree roots in asphalt pathway. 90' East of S Long Meadow.	2028	WCDOT GM
CH75	CH75_Z-102	Lockport		3/4	Sidewalk is collapsing, asphalt has been cut and falling toward manhole. 35' East of S Long Meadow	2028	WCDOT GM
CH75	CH75_Z-103	Lockport		3/4	Vertical deficiency of.75 in crosswalk between asphalt and curb (crosswalk). On S Cedar Ridge.	2028	WCDOT GM
CH75	CH75_Z-104	Lockport		1	1" Horizontal gap. 275' West of Cedar Ridge.	2028	WCDOT GM
CH75	CH75_Z-105	Lockport			Accumulation of debris of pine needles on bike path. 325' West of Long Meadow.	2028	WCDOT GM
CH75	CH75_Z-106	Lockport		1 1/4	Sidewalk is sloping towards pond area, cross slope is 3.2%. 530' West of Cedar Ridge.	2028	WCDOT GM
CH75	CH75_Z-107	Lockport	3/4		Sidewalk is fine towards pond area, on south side cross Slope is 5.3%. 575' West of Cedar Ridge.	2028	WCDOT GM
CH75	CH75_Z-108	Lockport		3/4	0.75" vertical and horizontal deficiencies. 695' West of Cedar Ridge.	2028	WCDOT GM
CH75	CH75_Z-100	Lockport	3/4		Concrete has been broken and cracked on south side. 715' West of Cedar Ridge.	2028	WCDOT GM
CH75	CH75_Z-109	Lockport		1	Concrete pad and west is vertically deficient 1". 225' West of Blackfoot.	2028	WCDOT GM
CH75	CH75_Z-110	Lockport	1/2	5/8	This area starts 100' path that has a bicycle tire mark in the path. 455' West of Blackfoot.	2028	WCDOT GM
CH75	CH75_Z-111	Lockport	3/4		Concrete is vertically deficient and still problem with overhanging trees in par. 475' East of Finley.	2028	WCDOT GM
CH75	CH75_Z-112	Lockport			Concrete has deteriorated and has caused pitting also trees are overhanging into PAR. 400' East of Finley.	2028	WCDOT GM
CH75	CH75_Z-113	Lockport	1 1/3		Concrete is 1.375" vertically deficient. 320' East of Finley.	2028	WCDOT GM
CH75	CH75_Z-114	Lockport	3/4	3/4	Concrete pads have a vertical and horizontal deficiency. 310' East of Finley.	2028	WCDOT GM
CH75	CH75_Z-115	Lockport	1/2	1/2	0.625" vertical deficiency on south side of concrete pad. 215' East of Finley.	2028	WCDOT GM
CH75	CH75_Z-116	Lockport	5/8		North side concrete pad .625" vertical deficiency and trees are overhanging into PAR. 85' East of Finley.	2028	WCDOT GM
CH75	CH75_Z-117	Lockport	1	3/4	Concrete pad to East is .75" vertically deficient. 815' West of Finley.	2028	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH75	CH75_Z-118	Lockport	1	1/4	960' East of Farrell.	2028	WCDOT GM
CH75	CH75_Z-119	Lockport			Vertical deficiency of 7/8". 395' East of Farrell.	2028	WCDOT GM
CH75	CH75_Z-120	Lockport			Manhole on pad. 75' East of Farrell.	2028	WCDOT GM
CH75	CH75_Z-121	Lockport		1/2	Vertical deficiency of .5". 40' East of Bello.	2028	WCDOT GM
CH75	CH75_Z-122	Lockport	3/4	3 1/2	These two pads are vertically deficient 3.5".adjacent sidewalk is compliant. 35' West of Bello.	2028	WCDOT GM
CH75	CH75_Z-123	Lockport		3	Concrete pad has settled near manhole deteriorated, concrete pieces, pictures taken. 45' West of Bello.	2028	WCDOT GM
CH75	CH75_Z-124	Lockport		1 1/4	Corner of concrete approximate 16" x 24' missing on the south east corner has fallen off. 55' West of Bello.	2028	WCDOT GM
CH75	CH75_Z-125	Lockport	1 1/4		0.625" horizontal gap. 65' West of Bello.	2028	WCDOT GM
CH75	CH75_Z-126	Lockport		5/8	Vertical deficiency of .625". 70' West of Bello.	2028	WCDOT GM
CH75	CH75_Z-127	Lockport		3/4	Vertical deficiency of .5". 170' West of Bello.	2028	WCDOT GM
CH75	CH75_Z-128	Lockport		1 1/8	Vertical deficiency of 1.125". 185' West of Bello.	2028	WCDOT GM
CH75	CH75_Z-129	Lockport		1/2	Vertical deficiency of.5" on this pad, control boxes to the south of lower pad on property. 265' West of Bello.	2028	WCDOT GM
CH75	CH75_Z-130	Lockport		1 1/4	These two pads have a vertical deficiency of 1.5"on each side, joints on both end. 345' West of Bello.	2028	WCDOT GM
CH75	CH75_Z-131	Lockport		1 1/4	Vertical deficiency of 1.25". 50' East of Read.	2028	WCDOT GM
CH75	CH75_Z-132	Lockport		1	Cross slope of .3% with 1" Vertical deficiency. 65' East of Read.	2028	WCDOT GM
CH75	CH75_Z-133	Lockport			Cracked pad. 75' East of Read.	2028	WCDOT GM
CH75	CH75_Z-134	Lockport		5/6	Corner missing on pad with .825" Vertical deficiency. 190' East of Read.	2028	WCDOT GM
CH75	CH75_Z-135	Lockport			Cracked pad. 200' East of Read.	2028	WCDOT GM
CH75	CH75_Z-136	Lockport		1 5/8	Cracked pad. 205' East of Read.	2028	WCDOT GM
CH75	CH75_Z-137	Lockport		3/4	Concrete is missing, a 5" x 7" area at joint. 40' East of Strawberry Hill.	2028	WCDOT GM
CH75	CH75_Z-138	Lockport			Cross slope of 7.2%. Cracked pad. 55' West of Strawberry Hill.	2028	WCDOT GM
CH75	CH75_Z-139	Lockport		3/4	1" vertical deficiency. 95' West of Strawberry Hill.	2028	WCDOT GM
CH75	CH75_Z-140	Lockport		1 1/4	3.7% cross slope. 120' West of Strawberry Hill.	2028	WCDOT GM
CH75	CH75_Z-141	Lockport		2	Vertical deficiency of 1.75". 110' East of Peachtree.	2028	WCDOT GM
CH75	CH75_Z-142	Lockport	1		0.75" horizontal gap. 120' East of Peachtree.	2028	WCDOT GM
CH75	CH75_Z-143	Lockport			Cracked pad with 2' of chipped pad. 130' East of Peachtree.	2028	WCDOT GM
CH75	CH75_Z-144	Lockport			Cracked pad. 140' East of Peachtree.	2028	WCDOT GM
CH75	CH75_Z-145	Lockport			Cracked pad. 95' West of Peachtree.	2028	WCDOT GM
CH75	CH75_Z-146	Lockport		1 1/4	Vertical deficiency of 1.25". 150' West of Peachtree.	2028	WCDOT GM
CH75	CH75_Z-147	Lockport			Chipped pads. 145' East of Summit.	2028	WCDOT GM
CH75	CH75_Z-148	Lockport			Vertical deficiency of 1.125" and cracked pad. 30' East of Summit.	2028	WCDOT GM
CH75	CH75_Z-149	Lockport			Cracking. 135' West of Summit.	2028	WCDOT GM
CH75	CH75_Z-150	Lockport			Vertical deficiency of .75". 150' West of Summit.	2028	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH17	CH17_Z-101	Manhattan	3/8	1/2	0.7% cross slope. 165' East of Marion.	2029	WCDOT GM
CH17	CH17_Z-102	Manhattan	1/3	5/8	Vertical deficiency on south side of sidewalk .625". 50' West of Fairview.	2029	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH32	CH32_Z-101	Minooka	2		Uneven ramp. 5' West of Santos.	2035	WCDOT GM
CH32	CH32_Z-102	Minooka	1		Vertical deficiency of 1.75". 20' East of Santos.	2035	WCDOT GM
CH32	CH32_Z-103	Minooka		1 1/4	This area has severe vertical deficiency in the bike path 1.75" very severe. 65' East of Santos.	2035	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH38	CH38_Z-101	Mokena		1	Buffalo box that is vertically deficiency of .75". 30' East of Creekview.	2029	Local
CH38	CH38_Z-102	Mokena	1 1/4	1/4	1' horizontal deficiency. 220' West of Swan.	2029	Local
CH38	CH38_Z-103	Mokena	1 1/2	2 1/2	Bike path is deteriorating and sloping towards landscaped area causing horizontal deficiency parallel to PAR 1"and areas pictures taken. 55' East of Swan.	2029	Local
CH38	CH38_Z-104	Mokena			Deterioration on the south side of bike path in sunken area of vegetation coming through. 340' East of 114th.	2029	Local
CH38	CH38_Z-105	Mokena	1 1/2	3/4	Horizontal deficiency with approximately 1.5" wide filled with grass deteriorating the south side of pathway heading east, 20' sloping off and cracks filled with sediment. 275' West of S Mill Creek.	2029	Local
CH38	CH38_Z-106	Mokena			Cracked pads with vertical deficiency of 1". 50' West of Wolf.	2029	Local
CH64	CH64_Z-101	Mokena	1/2	3/4	Cross slope of .7%. 35' East of Breckenridge.	2028	Local
CH64	CH64_Z-102	Mokena	1/4	1 3/4	Vertical difference of 1.75" just north of right away. 20' East of Brackenridge.	2028	Local
CH64	CH64_Z-103	Mokena	3/8	1 1/4	Sediments have collected on street side of path. 70' East of S Townline.	2028	Local
CH64	CH64_Z-104	Mokena	1 1/4	3/4	Concrete pad has cracks parallel and perpendicular. 170' East of S Townline.	2028	Local
CH64	CH64_Z-105	Mokena	1/4	1 1/4	Concrete pad has vertical deficiency. 400' East of S Townline.	2028	Local
CH64	CH64_Z-106	Mokena	3/4	1	5.2% cross slope. 515' East of S Townline.	2028	Local
CH64	CH64_Z-107	Mokena	1/2	1	Cross slope of 3.6%. 600' East of S Townline.	2028	Local
CH64	CH64_Z-108	Mokena	1/2	5/8	Cross slope of 2.9%. 630' East of S Townline.	2028	Local
CH64	CH64_Z-109	Mokena	1/2	3/4	Cross slope of 3%. 650' East of S Townline.	2028	Local
CH64	CH64_Z-110	Mokena	1/4	1 1/8	0.8% cross slope. 685' East of S Townline.	2028	Local
CH64	CH64_Z-111	Mokena	1/2	1	0.6% cross slope. 750' West of Glennell.	2028	Local
CH64	CH64_Z-112	Mokena	1/2	1	Cross slope of 4.6%. 650' West of Glennell.	2028	Local
CH64	CH64_Z-113	Mokena	1/4	1	0.7% cross slope. 635' West of Glennell.	2028	Local
CH64	CH64_Z-114	Mokena	1/2	2	Water manhole near area. 465' West of Glennell.	2028	Local
CH64	CH64_Z-115	Mokena	1/2	2	Manhole for Mokena water in area. 445' West of Glennell.	2028	Local
CH64	CH64_Z-116	Mokena	3/8	1	3.7% cross slope. 395' West of Glennell.	2028	Local
CH64	CH64_Z-117	Mokena	3/8		1.7% cross slope. 350' West of Glennell.	2028	Local
CH64	CH64_Z-118	Mokena	1/4	5/8	1.3% cross slope. 35' East of Glennell.	2028	Local
CH64	CH64_Z-119	Mokena	1	1/4	4.7% cross slope. 105' West of Woodhaven.	2028	Local
CH64	CH64_Z-120	Mokena	1/4	1/4	Concrete pad has cracked near Culvert area. 45' West of Woodhaven.	2028	Local
CH84	CH84_Z-111	Mokena	1 1/2	3/4	Chipped corner and concrete pad. 340' East of 85th.	2030	Local
CH84	CH84_Z-112	Mokena	1/2	3/4	2.3% cross slope. 280' East of 85th.	2030	Local
CH84	CH84_Z-113	Mokena	1	1 1/8	2.6% cross slope. 220' East of 85th.	2030	Local
CH84	CH84_Z-114	Mokena	3/4	1 1/2	0.8% cross slope. 185' East of 85th.	2030	Local
CH84	CH84_Z-115	Mokena	1/4	3/8	Crack in sidewalk affecting two pads. 150' East of 85th.	2030	Local

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH84	CH84_Z-116	Mokena	1	1/4	3.2% cross slope. 75' West of 88th.	2030	Local
CH84	CH84_Z-117	Mokena	1/4	5/8	3.1% cross slope. 325' West of 88th.	2030	Local
CH84	CH84_Z-118	Mokena	1	1/8	1.4% cross slope. 340' West of 88th.	2030	Local
CH84	CH84_Z-119	Mokena	1/4	1	1.7% cross slope. 390' West of 88th.	2030	Local
CH84	CH84_Z-120	Mokena	1/4	1	59"□ wide. 665' East of Darvin.	2030	Local
CH84	CH84_Z-121	Mokena	3/4	3/4	4.9% cross slope. 430' East of Darvin.	2030	Local
CH84	CH84_Z-122	Mokena	1/4	1	1.7% cross slope. 390' East of Darvin.	2030	Local
CH84	CH84_Z-123	Mokena	1/2	1 1/4	Cross slope 8.3%. 360' East of Darvin.	2030	Local
CH84	CH84_Z-124	Mokena	1/4	3/4	Cross slope 5.3 %. 350' East of Darvin.	2030	Local
CH84	CH84_Z-125	Mokena	3/8	3/4	0.5% cross slope. 230' East of Darvin.	2030	Local
CH84	CH84_Z-126	Mokena	1/2	1	4.7% cross slope. 175' East of Darvin.	2030	Local
CH84	CH84_Z-127	Mokena	1/4	3/4	2.5% cross slope. 165' East of Darvin.	2030	Local
CH84	CH84_Z-128	Mokena	18	3/4	Asphalt patch has been applied in sidewalk. 55' East of Darvin.	2030	Local
CH84	CH84_Z-129	Mokena	3	3/4	Missing spot of sidewalk. 835' West of Darvin.	2030	Local
CH84	CH84_Z-130	Mokena	3/8	1 1/4	Broken off piece of sidewalk with missing corner. 965' West of Darvin.	2030	Local
CH84	CH84_Z-131	Mokena	1/2	5/8	Vertical deficiency .625". 665' East of Henry.	2030	Local
CH84	CH84_Z-132	Mokena	1/2	3/8	Track missing concrete at manhole. 450' East of Henry.	2030	Local
CH84	CH84_Z-133	Mokena	1/2	5/8	2.8% cross slope. 235' East of Henry.	2030	Local
CH84	CH84_Z-134	Mokena	1/2	1/2	6.5% cross slope. 60' East of Henry.	2030	Local
CH84	CH84_Z-135	Mokena			5.1% cross slope. 35' East of Henry.	2030	Local
CH84	CH84_Z-136	Mokena	1/2	1	2.2% cross slope. 345' West of Henry.	2030	Local
CH84	CH84_Z-137	Mokena	1/4	5/8	1.7% cross slope. 355' West of Henry.	2030	Local
CH84	CH84_Z-138	Mokena	1/4	5/8	Hydrant near. 305' East of Old Lagrange.	2030	Local
CH84	CH84_Z-139	Mokena	1/4	5/8	Value near. 280' East Old Lagrange.	2030	Local
CH84	CH84_Z-140	Mokena	1/8	5/8	Near Buffalo box. 270' East of Old Lagrange.	2030	Local
CH84	CH84_Z-141	Mokena	1/2	1/2	0.2% cross slope. 260' East of Old Lagrange.	2030	Local
CH84	CH84_Z-142	Mokena	1/4	1 1/4	Storm drain near. 140' East of Old Lagrange.	2030	Local
CH84	CH84_Z-143	Mokena	1/4	3/4	Storm drain near. 125' East of Old Lagrange.	2030	Local
CH84	CH84_Z-144	Mokena	2	2 1/2	Storm drain manhole cover has produced a crack and sidewalk. 50' West of Old Lagrange.	2030	Local
CH84	CH84_Z-145	Mokena	1/4	2 1/4	5.5% cross slope. 75' West of Old Lagrange.	2030	Local
CH84	CH84_Z-146	Mokena	1/4	1 3/8	5.9% cross slope. 90' West of Old Lagrange.	2030	Local
CH84	CH84_Z-147	Mokena	1/4	1 1/8	Cross slope 3.6% at transition of sidewalk width. 70' West of Old Lagrange.	2030	Local
CH84	CH84_Z-148	Mokena	3/8	1/2	Cross slope 2.7%. 160' West of Old Lagrange.	2030	Local
CH84	CH84_Z-149	Mokena	3	3/4	Missing concrete near manhole. 190' West of Old Lagrange.	2030	Local

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH84	CH84_Z-150	Mokena	1/4	3/4	Severe cross slope toward curb. 245' West of Old Lagrange.	2030	Local
CH84	CH84_Z-151	Mokena	3/8	2 1/4	Storm drain near. 130' East of Lagrange.	2030	Local
CH84	CH84_Z-152	Mokena	1/4	1 5/8	3.9% cross slope. 125' East of Lagrange.	2030	Local
CH84	CH84_Z-153	Mokena	1/4	1/2	6.0% cross slope. 115' East of Lagrange.	2030	Local
CH84	CH84_Z-154	Mokena	1 1/4	1 1/2	Traffic signal manhole vertically 1.5" higher than sidewalk area. 90' East of Lagrange.	2030	Local
CH84	CH84_Z-155	Mokena	1	1/2	Crack running perpendicular to par. 80' East of Lagrange.	2030	Local
CH84	CH84_Z-156	Mokena	1/4	1/2	Cross slope of walk is 3.0%. 75' East of Lagrange.	2030	Local

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH89	CH89_Z-101	Naperville			Horizontal gap 5/8". 145' South of Knoch Knolls.	2025	Local
CH89	CH89_Z-102	Naperville		1 3/4	Asphalt is vertically deficient towards lamp post. 410' South of Knoch Knolls.	2025	Local
CH89	CH89_Z-103	Naperville	3/4		Horizontal gap of .75". 115' North of Eagle Brook.	2025	Local
CH89	CH89_Z-104	Naperville	5/8		Horizontal gap of .628". 490' South of Eagle Brook.	2025	Local
CH89	CH89_Z-105	Naperville			Horizontal gap of .5". 535' South of Eagle Brook.	2025	Local
CH89	CH89_Z-106	Naperville			Horizontal gap of .5". 685' South of Eagle Brook.	2025	Local
CH89	CH89_Z-107	Naperville	5/8		Horizontal gap of .625". 1685' North of Alan Deathrage.	2025	Local
CH89	CH89_Z-108	Naperville		3/4	Concrete pad on Eastside has vertical deficiency .75". 1445' North of Alan Deathrage.	2025	Local
CH89	CH89_Z-109	Naperville		3/4	Concrete has a .75" vertical deficiency at asphalt. 1360' North of Alan Deathrage.	2025	Local
CH89	CH89_Z-110	Naperville	2	1 1/4	Asphalt area approximately 7' x 12' connecting to bridge concrete has settled 2" vertically and a 1.5"horizontall deficiency from bridge pictures taken. 1195' North of Alan Deathrage.	2025	Local
CH89	CH89_Z-111	Naperville	1 3/8	3/8	The spot was taken under bridge the tunnel is starting to deteriorate. 1185' North of Alan Deathrage.	2025	Local
CH14	CH14_Z-101	Naperville		3/4	100' S of 87th	2023	WCDOT GM
CH14	CH14_Z-102	Naperville			125' S of 87th	2023	WCDOT GM
CH14	CH14_Z-103	Naperville	1 1/2	1/8	Expansion joint horizontal deficiency,1"wide and sidewalk is sloping towards residential area. 130' S of 87th	2023	WCDOT GM
CH14	CH14_Z-104	Naperville	1		Sediment in PAR noncompliant. 50' N of Hillview.	2023	WCDOT GM
CH14	CH14_Z-105	Naperville	1/3	1	Concrete pads are vertically deficient. 40' South of Hillview.	2023	WCDOT GM
CH14	CH14_Z-106	Naperville	1/2	1/2	Concrete pads are vertically deficient. 90' South of Hillview.	2023	WCDOT GM
CH14	CH14_Z-107	Naperville	1/8	1	Concrete pads are vertically deficient Cross slope. 105' South of Hillview. noncompliant	2023	WCDOT GM
CH14	CH14_Z-108	Naperville	1/4	1	Concrete pads are vertically deficient 1", cross slope noncompliant. 125' South of Hillview.	2023	WCDOT GM
CH14	CH14_Z-109	Naperville	1/8	1	Concrete pads are settling, less than 60" in width due to grass overgrowth. 175' South of Hillview.	2023	WCDOT GM
CH14	CH14_Z-110	Naperville	1/4	1 1/8	Concrete pad has vertical deficiency of 1.25" on north east corner of pad. 205' North of Plainview.	2023	WCDOT GM
CH14	CH14_Z-111	Naperville	1/2	1 1/2	Pads have a vertical deficiency of 1.25". 140' North of Plainview.	2023	WCDOT GM
CH14	CH14_Z-112	Naperville			Pads have a vertical deficiency of 1.25". 130' North of Plainview.	2023	WCDOT GM
CH14	CH14_Z-113	Naperville	1/4	1 1/3	Concrete pads have settled on the northside sediment built up in southeast corner on these two newer looking pads. 115' North of Plainview.	2023	WCDOT GM
CH14	CH14_Z-114	Naperville	1/8	1/8	This area has vertically deficient concrete pads that meet in the middle with or a growth on perimeter and 1" of sediment buildup on the side of the sidewalk. 65' North of Plainview.	2023	WCDOT GM
CH14	CH14_Z-115	Naperville	1/8	3/4	Manhole in this area is vertically deficient .75 "on north east corner pads to the south and the north 1" vertically deficient at location. Pad on north side of sidewalk has grass and sediment built up an overgrowth on sides. 55' North of Plainview	2023	WCDOT GM
CH14	CH14_Z-116	Naperville	1/8	1/2	Concrete pads are vertically deficient .5" there is a white drain cover on personal property. 100' South of Plainview.	2023	WCDOT GM
CH14	CH14_Z-117	Naperville	1/4	1 1/4	Concrete pad is vertically deficient to the north. 195' South of Plainview.	2023	WCDOT GM
CH14	CH14_Z-118	Naperville	1/8	1	Concrete pads vertical deficiency of 1". 115' North of Countryview	2023	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH14	CH14_Z-119	Naperville			Manhole in this area is vertically deficient .75" North. 55' North of Countryview.	2023	WCDOT GM
CH14	CH14_Z-120	Naperville	1/3	2	Concrete pads have settled cross a is 4.1% with a 2" vertical deficiency on west side of sidewalk. 100' South of Countryview.	2023	WCDOT GM
CH14	CH14_Z-121	Naperville	1/4	1	Trees in peoples property are causing sidewalks to cause vertical deficiencies hear. 115' South of Countryview.	2023	WCDOT GM
CH14	CH14_Z-122	Naperville	1/8	1	Concrete pad to the north has cross level 3.2 causing heave in concrete pads in this area on duty trees. 130' South of Countryview.	2023	WCDOT GM
CH14	CH14_Z-123	Naperville	1/8	1/2	Settling of concrete pad to the south of driveway cracks, 5". 165' South of Countryview.	2023	WCDOT GM
CH14	CH14_Z-124	Naperville	1/8	1/2	Drain tile leading toward sidewalk causing sediment and concrete pad to settle. 180' South of Countryview	2023	WCDOT GM
CH14	CH14_Z-125	Naperville	1/4	1 1/4	Concrete pad has settled due to a vehicles driving over sidewalk area in this area pictures taken. 260' South of Countryview.	2023	WCDOT GM
CH14	CH14_Z-126	Naperville	1/8	1 3/4	Sidewalk has a cross slope 5.6 settling has occurred your concrete pads were resurfaced to the north but has very bad pitting. 300' South of Countryview.	2023	WCDOT GM
CH14	CH14_Z-127	Naperville	1/4	3/4	Sidewalk pants have settled in this area undulating. 325' South of Countryview. on the cross slope	2023	WCDOT GM
CH14	CH14_Z-128	Naperville		5/8	Concrete pad to the north has settled .75" due to tree adjacent to pad. 330' South of Countryview.	2023	WCDOT GM
CH14	CH14_Z-129	Naperville	3/4	1	This area has an electrical manhole in the middle of the concrete pad and has 1â€ horizontal deficiency on each side of pad Manhole is lower than concrete pad on South questionable. 400' South of Countryview.	2023	WCDOT GM
CH14	CH14_Z-130	Naperville	1/4	1/2	Pads have .5" vertical deficiency. 345' North of Leverenz	2023	WCDOT GM
CH14	CH14_Z-131	Naperville	1/2	1/2	Sidewalk pad and 3.5% cross slope and .5" vertically deficient. 80' South of Leverenz.	2023	WCDOT GM
CH14	CH14_Z-132	Naperville			Cross slope is at 3.5%. 95' South of Levevrenz	2023	WCDOT GM
CH14	CH14_Z-133	Naperville		3/4	Asphalt was applied to provide slope. 120' South of Leverenz.	2023	WCDOT GM
CH14	CH14_Z-134	Naperville			Concrete is cracked and deteriorated and falling apart. 140' South of Leverenz.	2023	WCDOT GM
CH14	CH14_Z-135	Naperville	1/4	1/2	Concrete pads are vertically deficient .5". 230' South of Leverenz.	2023	WCDOT GM
CH14	CH14_Z-136	Naperville			Cross slope 5. 9%. 350' South of Leverenz.	2023	WCDOT GM
CH14	CH14_Z-137	Naperville			Cross slope 3.5%. 400' South of Leverenz.	2023	WCDOT GM
CH14	CH14_Z-138	Naperville			Cross slope is 6. 5% and marked to be fixed. 475' South of Leverenz.	2023	WCDOT GM
CH14	CH14_Z-139	Naperville	1/4	1	Concrete pads are vertically deficient 1.0". 495' North of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-140	Naperville	1/2	5/6	Concrete pads are vertically deficient .75". 465' North of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-141	Naperville	3/4	1 3/4	This area has been marked to be adjusted and fixed, marked with pink paint. manhole has 1.75"vertical deficiency on west side of manhole. 455' North of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-142	Naperville		1 3/4	Concrete pads are vertically deficient .75". 430' North of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-143	Naperville	1/8	2 1/2	Concrete pads are vertically deficient 2.5"on east and west side compared to other side grass is overgrown only given 47"for PAR. 420' North of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-144	Naperville	1/4	1 1/4	This is the most severe cross slope next to telephone pole 13.5% 52". 385' North of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-145	Naperville	1/8	1 3/4	Concrete pads are vertically deficiency of 1.75" difference on each side and slope is 13.9%. 380' North of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-146	Naperville	1/2	2 1/2	Concrete pads have a vertically deficiency. 360' North of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-147	Naperville	1/2	1 3/4	1.5" vertical deficiency. 320' North of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-148	Naperville	1/2	3/4	Concrete pad on the south has sloped down .75" on east side. 315' North of Gateshead.	2023	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH14	CH14_Z-149	Naperville	3/4	3	This an extremely bad area of where concrete has cracked and sloped down to 13Â° cross slope. 280' North of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-150	Naperville	1/4	1	Concrete on Northern pad has a vertical deficiency of .925". 250' North of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-151	Naperville	1/4	3/4	Pad to the south has a vertical deficiency of.75"on west side. 210' North of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-152	Naperville	1/2	1/2	Sediment has collected in northeast corner in manhole next has a .5" vertical deficiency compared to pathway. 65' North of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-153	Naperville		2	Concrete pad at intersection of crosswalks has been cracked and has a vertical deficiency fallen. 45' North of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-154	Naperville			Cracked pads to be replaced. 35' South of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-155	Naperville			Cracked pads to be replaced. 55' South of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-156	Naperville			Cracked pad to be replaced. 70' South of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-157	Naperville			Cracked and chipped pads along with vertical deficiency .75" north and 1.5 South. 215' South of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-158	Naperville			Asphalt has been applied to reduce trip hazard. 260' South of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-159	Naperville		2	Concrete pad has vertical deficiency due to bridge. 750' South of Gateshead. area	2023	WCDOT GM
CH14	CH14_Z-160	Naperville	3 1/2		Vertical deficiency Asphalt poured is fix. 775' South of Gateshead.	2023	WCDOT GM
CH14	CH14_Z-161	Naperville	1	1/2	1" horizontal deficiency where the pads connect. 300' North of 95th	2023	WCDOT GM
CH14	CH14_Z-162	Naperville	1	1/4	Cross slope 3.2%. 910' North of Conan Doyle.	2023	WCDOT GM
CH14	CH14_Z-163	Naperville		2	Asphalt is settled, causing a dip in the asphalt of1.5". 515" South of Conan Doyle.	2023	WCDOT GM
CH14	CH14_Z-165	Naperville	2		Cracked pavement. 408' South of Saratoga.	2023	WCDOT GM
CH14	CH14_Z-164	Naperville			Cracked pavement. 25' South of Saratoga.	2023	WCDOT GM
CH14	CH14_Z-166	Naperville			Cracked pavement. 265' North of 104th.	2023	WCDOT GM
CH14	CH14_Z-167	Naperville	1 1/4	1/3	15" width with horizontal deficiency of .925". 535' South of 104th.	2023	WCDOT GM
CH14	CH14_Z-168	Naperville			Expansion between existing pads asphalt is more than .75" and vertical deficiency on Eastside is 1.5"vertical and horizontal deficiency. 740' South of 104th .	2023	WCDOT GM
CH66	CH66_Z-101	Naperville	1/3	3/4	Walk to West has vertical deficiency of .75". 65' West of Book.	2032	WCDOT GM
CH66	CH66_Z-102	Naperville	1 3/4	3 1/2	Concrete pads are vertically deficient looks newer than older sidewalk in area. 80' West of Book.	2032	WCDOT GM
CH66	CH66_Z-103	Naperville		1	Sediments are collecting at walk. 380' West of Book.	2032	WCDOT GM
CH66	CH66_Z-104	Naperville	3/4	5/8	Sidewalk at electrical manhole approximately .75" vertical deficiency. 440' West of Book.	2032	WCDOT GM
CH66	CH66_Z-105	Naperville		2 1/2	Gutter curb has fallen 2.5" sidewalk bad also. 470' West of Book.	2032	WCDOT GM
CH66	CH66_Z-106	Naperville		3/4	Cross slope 1.6% with Vertical deficiency of .5" to 1". 555' West of Book.	2032	WCDOT GM
CH66	CH66_Z-107	Naperville		1 1/2	1.5" horizontal deficiency between sidewalk and curb. 590' West of Book.	2032	WCDOT GM
CH66	CH66_Z-108	Naperville		1 1/4	Cross slope of 5.6% with a vertical deficiency of 1.25". 605' West of Book.	2032	WCDOT GM
CH66	CH66_Z-109	Naperville		5/8	Cross slope of 2.4% and vertical deficiency of 9/16". 620' West of Book.	2032	WCDOT GM
CH66	CH66_Z-110	Naperville	1	1	Vertical deficiency at sidewalk. 640' East of Thatcher.	2032	WCDOT GM
CH66	CH66_Z-111	Naperville	1/3	1	Concrete pads are vertically deficient .5"on west side of path. 520' East of Thatcher.	2032	WCDOT GM
CH66	CH66_Z-112	Naperville	1/4	5/8	Vertical deficiency on south side of concrete pads and also horizontal deficiency along curb and sidewalk. 485' East of Thatcher.	2032	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH66	CH66_Z-113	Naperville	1/4	3/4	Vertical deficiency on walkway. 475' East of Thatcher.	2032	WCDOT GM
CH66	CH66_Z-114	Naperville	1/3	3/4	0.5" vertical deficiency. 325' East of Thatcher.	2032	WCDOT GM
CH66	CH66_Z-115	Naperville	1	1	Sidewalk is low on south side and high on northside, puddling of water to the west. 265' East of Thatcher.	2032	WCDOT GM
CH66	CH66_Z-116	Naperville	1/8	1 1/4	Cross slope 2.5% towards Rd. 165' East of Thatcher.	2032	WCDOT GM
CH66	CH66_Z-117	Naperville	1	1/4	Cross slope of .5% with .75" horizontal gap. 95' West of Thatcher.	2032	WCDOT GM
CH66	CH66_Z-118	Naperville	1/8	5/8	3.5% cross slope. 395' West of Thatcher.	2032	WCDOT GM
CH66	CH66_Z-119	Naperville	1/3	3/4	South side concrete pad has .75" vertical deficiency. 455' West of Thatcher.	2032	WCDOT GM
CH66	CH66_Z-120	Naperville	1/2	1	Sediment built up and west side of the connecting concrete pads. 740' West of Thatcher.	2032	WCDOT GM
CH66	CH66_Z-121	Naperville	1/3	1	Cross slope is approximate 4%. 750' West of Thatcher.	2032	WCDOT GM
CH66	CH66_Z-122	Naperville	1/4	1/2	Cross slope of 1.4% with a vertical deficiency of .5". 770' West of Thatcher.	2032	WCDOT GM
CH66	CH66_Z-123	Naperville	1/2	1	This area has eight pads of noncompliant sidewalk manhole approximate 12'east. 430' East of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-124	Naperville	1	5/8	Cross slope is 7.1%. 420' East of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-125	Naperville	1/2	5/8	This area has eight noncompliant pads of sidewalk manhole approximate 12'east. 400' East of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-126	Naperville	1/4	1	Cross slope is 4.6%. 390' East of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-127	Naperville	1/4	1	Sidewalk on west side has a vertical deficiency of 1" next to curb. 345' East of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-128	Naperville	1/4	1	Cross slope of 2.9% with vertical deficiency of 5/8". 360' East of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-129	Naperville	1/2	1 1/4	Sidewalk to adjacent sidewalk has 1.25" vertical deficiency on north side and 1" on south side. 320' East of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-130	Naperville	1/4	1	Cross slope is 5.6% towards SPC manhole. 260' East of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-131	Naperville	1/2	3/4	Cross slope of 2.1% with Vertical deficiency of 5/8". 225' East of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-132	Naperville	1/4	5/8	Sidewalk is vertically deficient on south side of sidewalk 2" vertical deficiency between curb and sidewalk area new road along this area. 210' East of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-133	Naperville	1/4	1/2	North side has vertical deficiency, south side is flush. 80' East of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-134	Naperville	1/4	1/2	Cross slope of .8% with a vertical deficiency of .5". 290' West of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-135	Naperville	1/2	5/6	Cross slope of 3.7% with a vertical deficiency of .75". 375' West of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-136	Naperville		1 1/4	vertical deficiency of 1.125". 875' West of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-137	Naperville		5/8	Concrete is settling towards roadway	2032	WCDOT GM
CH66	CH66_Z-138	Naperville	1/4	1	Pads have sloped towards sidewalk. 890' West of Chokeberry	2032	WCDOT GM
CH66	CH66_Z-139	Naperville	5/8	3/4	0.75" vertical deficiency and a manhole for the electrical 6'east of this joint. 945' West of Chokeberry.	2032	WCDOT GM
CH66	CH66_Z-140	Naperville	3/4	1 1/2	Sidewalk has a 1.5" vertical deficiency on west side. 715' East of route 59.	2032	WCDOT GM
CH66	CH66_Z-141	Naperville		2 1/2	Manhole to north of this concrete pad has vertical deficiency of 2.25". 710' East of route 59.	2032	WCDOT GM
CH66	CH66_Z-142	Naperville			Northside of sidewalk has approximately 2â€ x 2â€ piece of concrete missing. 285' East of route 59.	2032	WCDOT GM
CH66	CH66_Z-143	Naperville		3/4	0.75" vertical deficiency. 275' East of route 59.	2032	WCDOT GM
CH66	CH66_Z-144	Naperville		1/2	Concrete pads on north side of road have been broken and 1.5" vertical deficiency. 200' East of route 59	2032	WCDOT GM
CH66	CH66_Z-145	Naperville			Concrete pads in this area have been cracked, deteriorating and an adjacent pole on the south side of pad. 185' East of route 59.	2032	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH66	CH66_Z-146	Naperville	1/8	5/8	Concrete pads have cracked and sloping down towards tree. 160' East of route 59.	2032	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH4	CH4_Z-110	New Lenox	3/4	5/8	Cross slope of 4.7%. 235' South of W Illinois.	2027	WCDOT GM
CH4	CH4_Z-111	New Lenox	1/4	5/8	Cross slope of 2.4%. 375' North of W Otto.	2027	WCDOT GM
CH4	CH4_Z-112	New Lenox	1/4	5/8	1.7% cross slope. 135' North of W Otto.	2027	WCDOT GM
CH4	CH4_Z-113	New Lenox	1/4	3/4	1.5% cross slope. 130' South of W Otto.	2027	WCDOT GM
CH4	CH4_Z-114	New Lenox	3/4	1 1/2	This area has various deficiencies. 445' South of W Otto.	2027	WCDOT GM
CH74	CH74_Z-142	New Lenox	1/4	5/8	Hole filled with brick approximately 8"x8". No known reason why its€™s there. Man made. 305' East of Heather Glen.	2024-2026	5 Year Plan
CH74	CH74_Z-143	New Lenox	1/4	1	1.4% cross slope. 220' West of Heather Glen.	2024-2026	5 Year Plan
CH74	CH74_Z-144	New Lenox	1/2	2	3.6% cross slope. 230' West of Heather Glen.	2024-2026	5 Year Plan
CH74	CH74_Z-145	New Lenox	1/4	1 1/4	2.5% cross slope. 260' West of Heather Glen.	2024-2026	5 Year Plan
CH74	CH74_Z-146	New Lenox	1/4	1 1/4	Concrete section on northside of walk 6" x 3â€ missing. 320' West of Tower.	2024-2026	5 Year Plan
CH74	CH74_Z-147	New Lenox	1/2	1 1/2	6.0% cross slope and 7.0% running. 300' East of Schoolhouse.	2024-2026	5 Year Plan
CH74	CH74_Z-148	New Lenox	1/2	1/2	0.375" vertical deficiency with .8% cross slope. 115' East of Rachel Ridge.	2024-2026	5 Year Plan
CH74	CH74_Z-149	New Lenox	1/4	3/4	Cross slope of 2.5%. 450' West of Rachel Ridge.	2024-2026	5 Year Plan
CH74	CH74_Z-150	New Lenox	2	1/4	Horizontal deficiency joint which has been caulked but has separated again. 315' East of Calistoga.	2024-2026	5 Year Plan
CH74	CH74_Z-151	New Lenox	3/4	5/8	2.3% cross slope. 25' West of Foxwood.	2024-2026	5 Year Plan
CH74	CH74_Z-152	New Lenox	3	1 1/2	Corner of concrete sidewalk missing. 390' East of Nelson.	2024-2026	5 Year Plan
CH74	CH74_Z-153	New Lenox	3/4	1/2	Vertical deficiency of .5". 45' East of Nelson.	2024-2026	5 Year Plan
CH74	CH74_Z-154	New Lenox	1/4	1	Vertical deficiency of 1". 470' East of Heather Way.	2024-2026	5 Year Plan
CH74	CH74_Z-155	New Lenox	1/4	5/8	Concrete pad on each side has vertical deficiency of.625". 225' East of Heather Way.	2024-2026	5 Year Plan
CH63	CH63_Z-101	New Lenox	1	3/4	Pad has a crack approximately 12' in line with par 3' wide. 825' North of Chiszar.	2028	WCDOT GM
CH63	CH63_Z-102	New Lenox	1/4	3	Concrete for three Pads approximately 3' wide has cracked and sloping towards Street. 100' North of Chiszar.	2028	WCDOT GM
CH63	CH63_Z-103	New Lenox	1/4	5/8	0.3% cross slope. 100' North of Chiszar.	2028	WCDOT GM
CH63	CH63_Z-104	New Lenox	3/4	1	Vertical deficiency of .925". 30' South of Chiszar.	2028	WCDOT GM
CH63	CH63_Z-105	New Lenox	1/4	3/4	2.5% cross slope. 40' South of Chiszar.	2028	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH48	CH48_Z-101	Park Forest	1/8	1/2	Vegetation overgrowth on pathway PAR only 36". 260' East of Blackhawk.	2028	WCDOT GM
CH48	CH48_Z-102	Park Forest	1/2	1/2	5.5% cross slope. 210' East of Blackhawk.	2028	WCDOT GM
CH48	CH48_Z-103	Park Forest	1/2	3/8	1.5% cross slope. 95' East of Blackhawk.	2028	WCDOT GM
CH48	CH48_Z-104	Park Forest	1/4	1	Numerous deficiencies. 80' East of Blackhawk.	2028	WCDOT GM
CH48	CH48_Z-105	Park Forest	1/4	3/4	0.3% cross slope. 50' East of Blackhawk.	2028	WCDOT GM
CH48	CH48_Z-106	Park Forest	3/4	1 1/2	This newer concrete pad is 58" wide. 45' East of Blackhawk.	2028	WCDOT GM
CH48	CH48_Z-107	Park Forest	3/4	1 1/2	5.9% cross slope. 40' East of Blackhawk.	2028	WCDOT GM
CH48	CH48_Z-108	Park Forest	1/4	2	Severe vertical deficiencies and severe cross slope. 50' West of Blackhawk.	2028	WCDOT GM
CH48	CH48_Z-109	Park Forest	1/8	3/4	7.6% Cross slope. 65' west of Blackhawk.	2028	WCDOT GM
CH48	CH48_Z-110	Park Forest	1/4	3/4	8% cross slope. 120' West of Blackhawk.	2028	WCDOT GM
CH48	CH48_Z-111	Park Forest	1/4	3/4	4.2% cross slope. 50' East of Monee ct.	2028	WCDOT GM
CH48	CH48_Z-112	Park Forest	1/4	1 1/4	2.7% cross slope. 95' West of Monee ct.	2028	WCDOT GM
CH48	CH48_Z-113	Park Forest	1/4	3/4	0.9% cross slope. 45' West of S Orchard.	2028	WCDOT GM
CH48	CH48_Z-114	Park Forest	1/4	1/2	Numerous cracks and sediment in area. 180' East of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-115	Park Forest	1/4	1/2	Cross slope 6.3%. 110' East of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-116	Park Forest	1/4	3/4	5.5% cross slope. 75' East of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-117	Park Forest	1/2	1/2	Numerous cracks in the sidewalk. 10' West of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-118	Park Forest	1/2	1/2	Numerous cracks in pavement. 45' West of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-119	Park Forest	1/4	3	7.4% cross slope. 115' West of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-120	Park Forest	1/4	1 1/4	Cracking of concrete pad and vertical deficiencies. 130' Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-121	Park Forest	1	3/4	Concrete pad has broken pieces on corners with vertical deficiencies of .75". 155' West of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-122	Park Forest	3/4	1/2	1.4% cross slope. 170' West of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-123	Park Forest	1/4	1/2	4.6% cross slope. 220' West of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-124	Park Forest	1/4	3/4	4.2% cross slope. 290' West of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-125	Park Forest	1/4	1/3	Cracked corner on concrete pad. 220' West of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-126	Park Forest	1/2	5/8	Cross slope 5.9%. 260' West of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-127	Park Forest	1/4	1/2	Grass is overgrown into sidewalk area numerous cracks. 345' West of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-128	Park Forest	3/8	5/8	4% cross slope. 390' West of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-129	Park Forest	1/4	5/8	3.4% cross slope. 395' West of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-130	Park Forest	3	1 1/4	Numerous cracks and deterioration of walk. 435' West of Thorn Creek.	2028	WCDOT GM
CH48	CH48_Z-131	Park Forest	1 1/4	5/8	4.1% cross slope. 420' East of Niagara.	2028	WCDOT GM
CH48	CH48_Z-132	Park Forest	2	3/4	Deterioration in the middle and both ends of concrete pad and vertical difference of .625". 415' East of Niagara.	2028	WCDOT GM
CH48	CH48_Z-133	Park Forest	1/4	1	6.8% cross slope. 170' East of Niagara.	2028	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH48	CH48_Z-134	Park Forest	1/4	3/4	6.9% cross slope. 45' East of Niagara.	2028	WCDOT GM
CH48	CH48_Z-135	Park Forest	1/2	3/4	Cross slope of 7.5%. 35' East of Niagara.	2028	WCDOT GM
CH48	CH48_Z-136	Park Forest	1/4	1/2	6.1% cross slope. 155' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-137	Park Forest	1/2	5/8	Parallel cracks in par. 230' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-138	Park Forest	3/4	5/8	2.9% cross slope. 250' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-139	Park Forest	3/4	1/4	Cross slope 4.6%. 290' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-140	Park Forest	6	3/4	Deteriorating concrete for approximately 12" x1.25". 310' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-141	Park Forest	2	3/4	3.6% cross slope. 330' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-142	Park Forest	1/4	1	Asphalt patch. 370' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-143	Park Forest	2	3/4	Broken concrete in corner of pad. 380' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-144	Park Forest	1/2	1/2	Asphalt patch. 395' West of Niagara	2028	WCDOT GM
CH48	CH48_Z-145	Park Forest	2	1 1/4	Cracked pads. 440' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-146	Park Forest	2	1	Cracked pad. 450' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-147	Park Forest	1/4	1	6.4% cross slope. 540' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-148	Park Forest	1/4	5/8	6.3% cross slope. 595' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-149	Park Forest	1/4	3/4	5.9% cross slope. 615' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-150	Park Forest	1/4	1	4.2% cross slope. 730' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-151	Park Forest	1/4	1	10.5% cross slope. 800' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-152	Park Forest	1/4	3/4	10.1% cross slope. 815' West of Niagara.	2028	WCDOT GM
CH48	CH48_Z-153	Park Forest	3/8	1	5.0% cross slope. 800' East of indianwood.	2028	WCDOT GM
CH48	CH48_Z-154	Park Forest	3/8	1 1/4	5.0 %cross slope. 785' East of indianwood.	2028	WCDOT GM
CH48	CH48_Z-155	Park Forest	1	3/4	5.1% cross slope. 575' East of indianwood.	2028	WCDOT GM
CH48	CH48_Z-156	Park Forest	1	3/8	Cracked concrete pads. 525' East of indianwood.	2028	WCDOT GM
CH48	CH48_Z-157	Park Forest	1/8	1	4.9% cross slope. 330' East of indianwood.	2028	WCDOT GM
CH48	CH48_Z-158	Park Forest	1/2	1 1/4	Concrete has cracked in a section and its€™s falling towards Street. 105' East of indianwood.	2028	WCDOT GM
CH48	CH48_Z-159	Park Forest	3/4	5/8	8.5% cross slope. 65' East of indianwood.	2028	WCDOT GM
CH48	CH48_Z-160	Park Forest	5/8	5/8	4.2% cross slope. 50' East of indianwood.	2028	WCDOT GM
CH48	CH48_Z-161	Park Forest	1/2	1	7.9% cross slope. 100' West of indianwood.	2028	WCDOT GM
CH48	CH48_Z-162	Park Forest	1 3/4	3/4	5.5% cross slope. 150' West of indianwood.	2028	WCDOT GM
CH48	CH48_Z-163	Park Forest	1/4	5/8	4.6% cross slope. 180' West of indianwood.	2028	WCDOT GM
CH48	CH48_Z-164	Park Forest	1/4	3/4	7.6% cross slope. 205' West of indianwood.	2028	WCDOT GM
CH48	CH48_Z-165	Park Forest	1/8	3/4	5.3% cross slope. 155' East of Tampa.	2028	WCDOT GM
CH48	CH48_Z-166	Park Forest	1/4	3/4	6.4% cross slope. 125' East of Tampa.	2028	WCDOT GM
CH48	CH48_Z-167	Park Forest	1/4	5/8	6.4% cross slope. 100' East of Tampa.	2028	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH48	CH48_Z-168	Park Forest	1/8	3/4	8% cross slope. 65' West of Tampa.	2028	WCDOT GM
CH48	CH48_Z-169	Park Forest	1/2	1 1/4	3.6% cross slope. 145' West of Tampa.	2028	WCDOT GM
CH48	CH48_Z-170	Park Forest	3 1/2	3/4	Deterioration of sidewalk area. 215' West of Tampa.	2028	WCDOT GM
CH48	CH48_Z-171	Park Forest	3 3/4	1	Deterioration of concrete at joints 1" vertically and 3.5" horizontal deficient. 200' East of Tamarack.	2028	WCDOT GM
CH48	CH48_Z-172	Park Forest	1/8	1/2	Cracked sidewalk pad on east side of path that has sediment collected due to crack. 185' East of Tamarack.	2028	WCDOT GM
CH48	CH48_Z-173	Park Forest	4	1	Deterioration of joint between€™s driveway and sidewalk. 80' East of Tamarack.	2028	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH25	CH25_Z-101	Peotone	3/4	1/4	The two sidewalk pads in this area on the south side have been cracked and are deteriorating. 30' East of S Rathje.	2028	5 Year Plan
CH25	CH25_Z-102	Peotone	1/8	1	1% cross slope. 130' East of S Rathje.	2028	5 Year Plan
CH25	CH25_Z-103	Peotone	1/2	5/8	1.6% cross slope. 275' West of Division.	2028	5 Year Plan
CH25	CH25_Z-104	Peotone	1/2	3/4	Concrete has settled on this west side of this pad due to falling off of concrete pads. 165' East of Division.	2028	5 Year Plan

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH14	CH14_Z-170	Plainfield		3/4	Concrete has settled on west side .75". 1750' South of Rodeo.	2023	WCDOT GM
CH14	CH14_Z-171	Plainfield			Crack long sidewalk and sidewalks 58" wide. 1785' South of Rodeo.	2023	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH36	CH36_Z-101	Romeoville			Cracked pad 33" long. 325' West of Zachary.	2028	WCDOT GM
CH36	CH36_Z-102	Romeoville		1 1/4	Chipped corner 2" wide with 1.25" vertical deficiency. 365' East of Zachary.	2028	WCDOT GM
CH36	CH36_Z-103	Romeoville	5/8	1 1/2	Vertical deficiency of .5" - 1.25". 605' West of Weber.	2028	WCDOT GM
CH36	CH36_Z-104	Romeoville	1/2	1 1/4	Next to fire hydrant. 395' West of Weber.	2028	WCDOT GM
CH36	CH36_Z-105	Romeoville			Diagonal crack along concrete sidewalk, 8' long. 315' West of Weber.	2028	WCDOT GM
CH36	CH36_Z-106	Romeoville	3/4	3/4	Horizontal gap of 1" with vertical deficiency of .75". 180' West of Weber.	2028	WCDOT GM
CH36	CH36_Z-107	Romeoville		3/4	Crack on south side of pavement. 115' West of Weber.	2028	WCDOT GM
CH88	CH88_Z-132	Romeoville	1/4	3/4	Vertical deficiency of .75". 95' South of Taylor.	2024	5 Year Plan
CH88	CH88_Z-133	Romeoville	1/4	3/4	Vertical deficiency of .75". 105' South of Taylor.	2024	5 Year Plan
CH88	CH88_Z-134	Romeoville	1/4	1	vertical deficiency. 445' South of Taylor.	2024	5 Year Plan
CH88	CH88_Z-135	Romeoville			Vertical deficiency of .5". 275' North of Creekside.	2024	5 Year Plan
CH88	CH88_Z-136	Romeoville	1 1/2	2	Vertical deficiency of 2". 65' South of Creekside.	2024	5 Year Plan
CH88	CH88_Z-137	Romeoville	1/4	1 3/8	Edison manholes to east. 100' South of Creekside.	2024	5 Year Plan
CH88	CH88_Z-138	Romeoville	1/4	1 3/8	Vertical deficiency of 1.375". 105' South of Creekside.	2024	5 Year Plan
CH88	CH88_Z-139	Romeoville	1/4	5/8	Vertical deficiency of .625". 615' North of Airport rd.	2024	5 Year Plan
CH88	CH88_Z-140	Romeoville	1/4	2 1/2	Severe vertical deficiency AT&T manhole located on east side. 290' North of Airport rd.	2024	5 Year Plan
CH88	CH88_Z-141	Romeoville	1/4	5/8	Vertical deficiency. 290' North of Airport rd.	2024	5 Year Plan
CH88	CH88_Z-142	Romeoville	1/4	5/8	Vertical deficiency of .75". 140' North of Airport rd.	2024	5 Year Plan
CH88	CH88_Z-143	Romeoville	3/4	3/4	Concrete pad has cracked in middle. 135' North of Airport rd.	2024	5 Year Plan
CH88	CH88_Z-144	Romeoville	3	3/4	Depression and concrete trip hazard. 120' North of Airport rd.	2024	5 Year Plan
CH88	CH88_Z-145	Romeoville	1	1 3/8	Vertical deficiency on the concrete pad. 100' North of Airport rd.	2024	5 Year Plan
CH88	CH88_Z-146	Romeoville	3 1/2	1	Concrete cracking at joint cross slope extreme. 90' North of Airport rd.	2024	5 Year Plan
CH88	CH88_Z-147	Romeoville	1 1/8	3/4	Concrete pad has separated from adjacent. 80' North of Airport rd.	2024	5 Year Plan
CH88	CH88_Z-148	Romeoville	1/4	3/4	Vertical deficiency of .75". 1525' North of Grand Haven.	2029	WCDOT GM
CH88	CH88_Z-149	Romeoville	3/4	3/4	Two concrete patches have vertical deficiency between both pads. 150' South of Grand Haven.	2029	WCDOT GM
CH88	CH88_Z-150	Romeoville	1/3	1 1/2	Vertical deficiency between two sunken pads. 160' South of Grand Haven.	2029	WCDOT GM
CH88	CH88_Z-151	Romeoville	1/2	3/4	Cross slope of 2.1% with vertical deficiency of .75". 165' South of Grand Haven.	2029	WCDOT GM
CH88	CH88_Z-152	Romeoville	3	3/4	Section of concrete sidewalk missing approximately 6" x 3". 290' South of Grand Haven.	2029	WCDOT GM
CH88	CH88_Z-153	Romeoville	1		Cross slope of 1% with Horizontal gap of 1".	2029	WCDOT GM
CH88	CH88_Z-154	Romeoville		1	Cross slope of 1.4% with a horizontal gap of 1". 680' South of Grand Haven.	2029	WCDOT GM
CH88	CH88_Z-155	Romeoville	1/8	1	Cross slope 3.7%. 395' North of Renwick.	2029	WCDOT GM
CH88	CH88_Z-156	Romeoville		1	Sidewalk is sloping towards sign 3.5% cross slope. 110' North of Renwick.	2029	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH73	CH73_Z-101	Symerton	1/2	1/8	This is a sidewalk that is approximately 10' wide next to a church has various undulations long pathway. 110' North of W South.	2028	WCDOT GM
CH73	CH73_Z-102	Symerton	3/8	3/4	This area is marked with yellow parking lanes. 15' North of W South.	2028	WCDOT GM
CH73	CH73_Z-103	Symerton	1/2	1 1/2	Vertical deficiency of concrete pads. 10' North of W South.	2028	WCDOT GM

County Highway Number	Location ID	Jurisdiction	Crack Width (inches)	Vertical Difference (inches)	Defect Field Notes	Estimated Year of Improvement	Program
CH83	CH83_Z-101	Tinley Park	3 1/4	1 3/4	Broken corner of pad. 60' South of 183rd.	2023	5 Year Plan
CH83	CH83_Z-102	Tinley Park	1/4	3/4	Cross slope of 2.3%. 75' South of 183rd.	2023	5 Year Plan
CH83	CH83_Z-103	Tinley Park	1/4	1 1/2	Cross slope of 1% with a vertical deficiency of 1.5". 140' South of 183rd.	2023	5 Year Plan
CH83	CH83_Z-104	Tinley Park	1/4	5/8	Cross slope of 1.4% with a vertical deficiency of .625". 285' South of 183rd.	2023	5 Year Plan
CH83	CH83_Z-105	Tinley Park	1/4	2 1/4	Cross slope 5%. 560' South of 183rd.	2023	5 Year Plan
CH83	CH83_Z-106	Tinley Park	1/4	5/8	Cross slope 4%. 585' South of 183rd.	2023	5 Year Plan
CH83	CH83_Z-107	Tinley Park	1/4	5/8	Cross slope 1.9%. 600' South of 183rd.	2023	5 Year Plan
CH83	CH83_Z-108	Tinley Park	2	1/2	Cross slope .6%. 465' North of W 185th.	2023	5 Year Plan
CH84	CH84_Z-101	Tinley Park	1/4	3/4	4.7% cross slope. 1270' East of 76th.	2028	Local
CH84	CH84_Z-102	Tinley Park	144	8	concrete pad not poured. 1005' East of 76th	2028	Local
CH84	CH84_Z-103	Tinley Park	3/4	1 3/4	0.8% cross slope. 765' East of 76th.	2028	Local
CH84	CH84_Z-104	Tinley Park	5/8	1	Cross slope of .8%. 745' East of 76th.	2028	Local
CH84	CH84_Z-105	Tinley Park	3/8	1	Cross slope 4.3%. 735' East of 76th.	2028	Local
CH84	CH84_Z-106	Tinley Park	1/2	1	Manhole with numerous cracks perpendicular and parallel to par. 50' West of Brookside Glen.	2028	Local
CH84	CH84_Z-107	Tinley Park	1 1/4	1 1/4	Broken piece of sidewalk at joint. 1385' West of 80th.	2028	Local
CH84	CH84_Z-108	Tinley Park	1	1 1/4	3.1% cross slope. 1460' West of 80th.	2028	Local
CH84	CH84_Z-109	Tinley Park	1/2	3/4	2.4% cross slope. 1470' West of 80th.	2028	Local
CH84	CH84_Z-110	Tinley Park	3/8	1/2	Broken piece of sidewalk and deterioration. 1475' West of 80th.	2028	Local
